


New Construction

PROGRESS UPDATE
September 2024

Fairport Harbor New Pre K-12 School



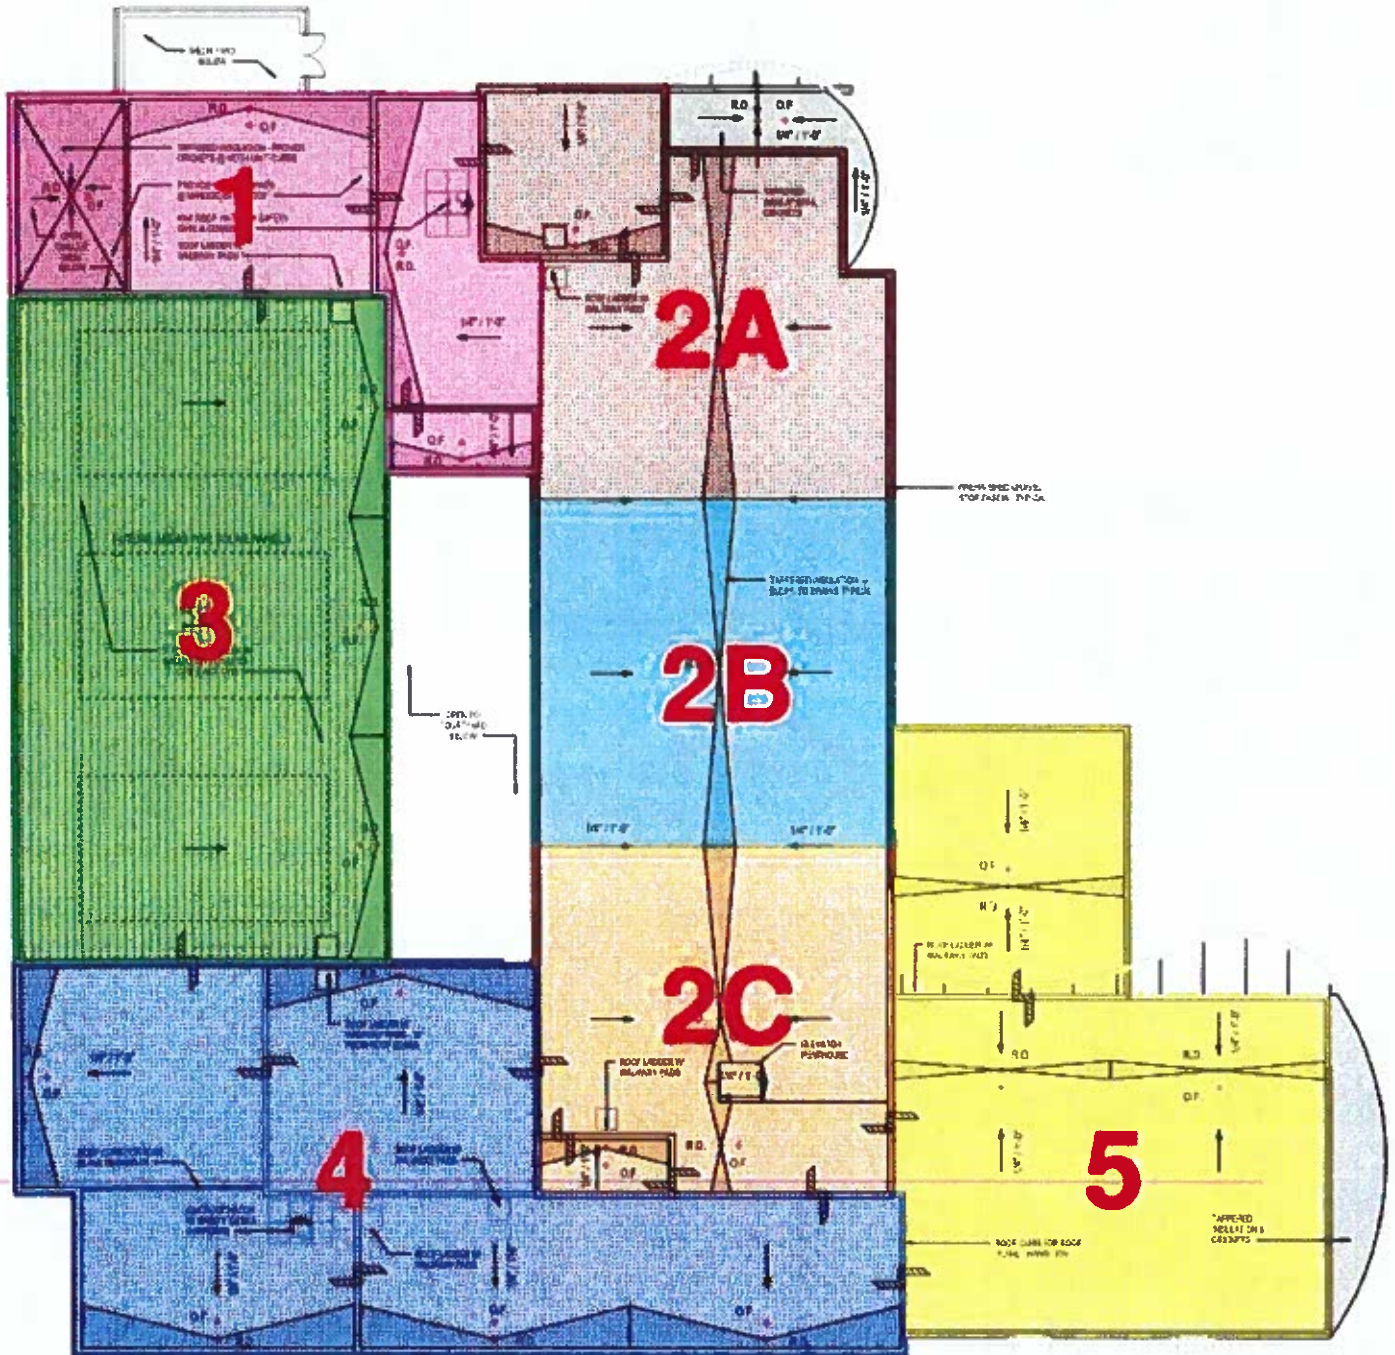

PROJECT SUMMARY

North 1/3 of Area 3 (Phase 1)


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

September 2024 Progress

- Setting Bar Joist and Deck—Complete
- Overhead Ductwork—Complete
- Mechanical Piping—In Progress
- Stair Tower #4—Complete
- Fire Alarm Wiring—In Progress

Upcoming Progress

- Roof Blocking
- Roof Membrane

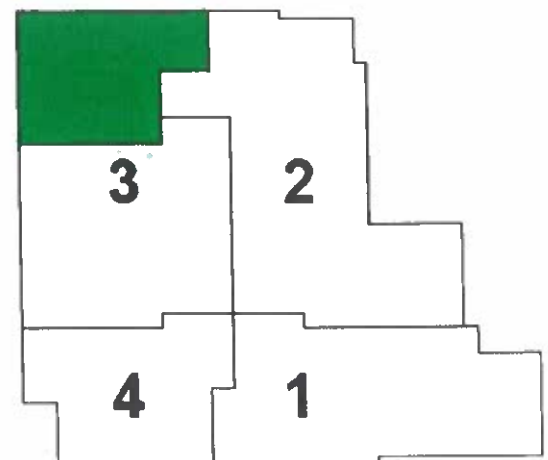

PROJECT SUMMARY

North 1/3 of Area 2 (Phase 2A)


- **Educational Classrooms**

September 2024 Progress



- **Setting Bar Joist and Deck—Complete**
- **Window Blocking and Sheeting—Complete**
- **Brick Veneer—In Progress**
- **Fire Alarm Wiring—In Progress**
- **Ductwork on 3rd Floor—In Progress**

Upcoming Progress

- **Roof Blocking**
- **Roof Membrane**

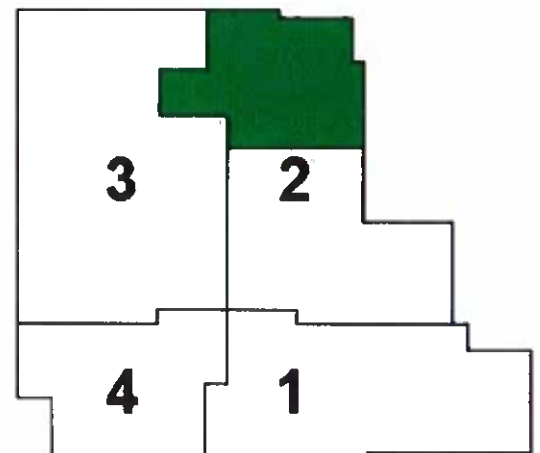

PROJECT SUMMARY

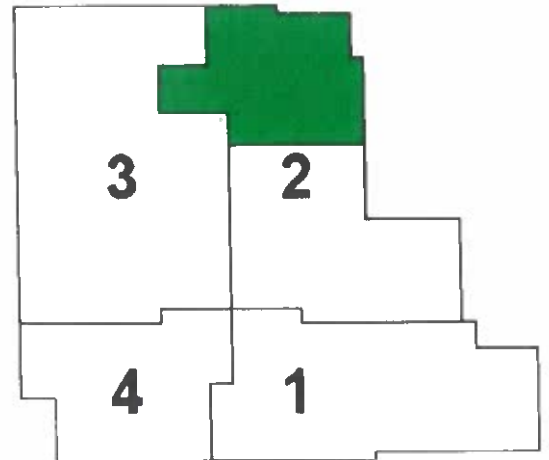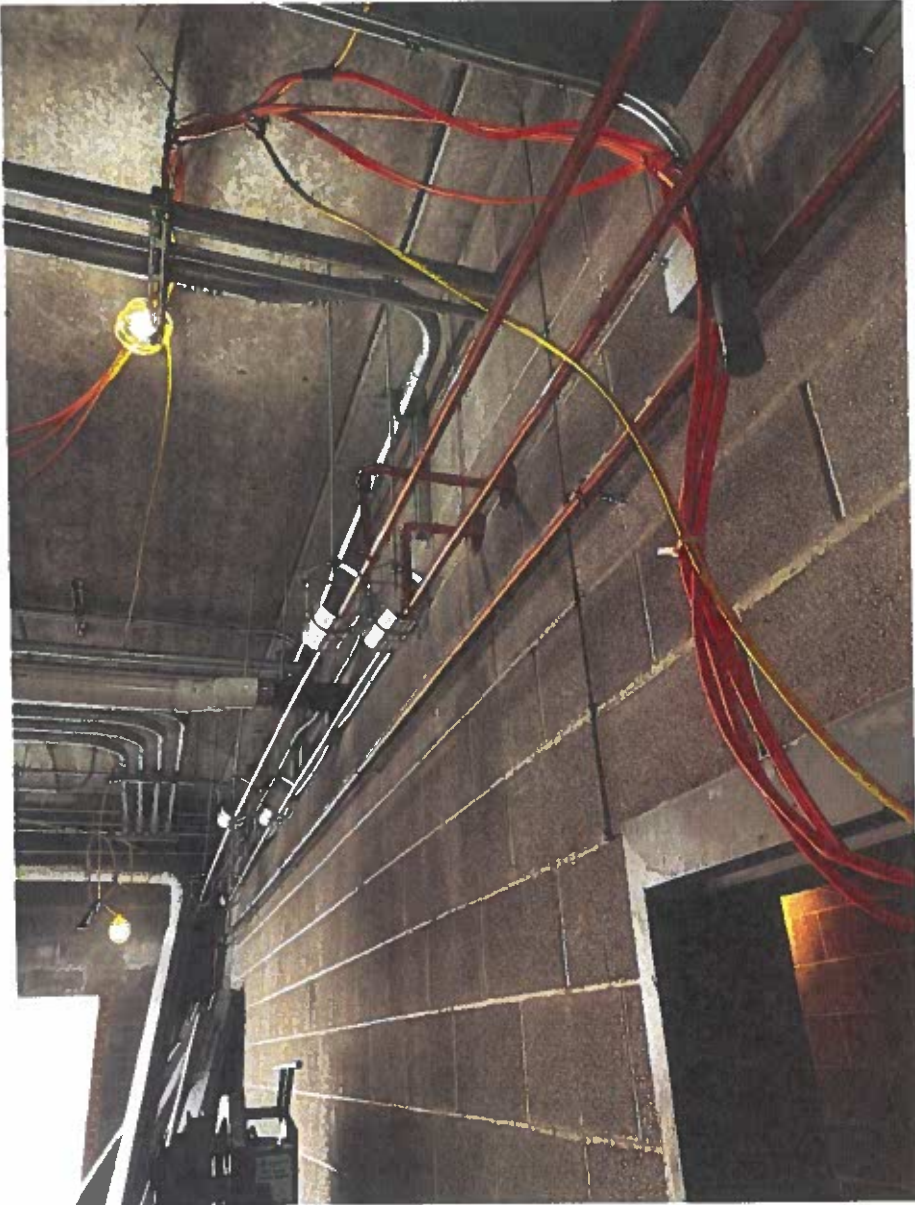

PROJECT SUMMARY

South 2/3 of Area 2 (Phase 2B and 2C)


- **Educational Classrooms**

September 2024 Progress



- Slab On Grade—Complete
- 1st Floor Masonry to Bearing—Complete
- 1st Floor Structural Steel—Complete
- 2nd Floor Structural Steel—Complete
- Second Floor Precast Plank—In Progress
- In Wall Rough In's—In Progress

Upcoming Progress

- Masonry Bearing on Second Floor
- 2nd Floor Topping
- Overhead Plumbing Rough In
- Overhead Electrical Rough In
- In wall Rough In's 2nd Floor

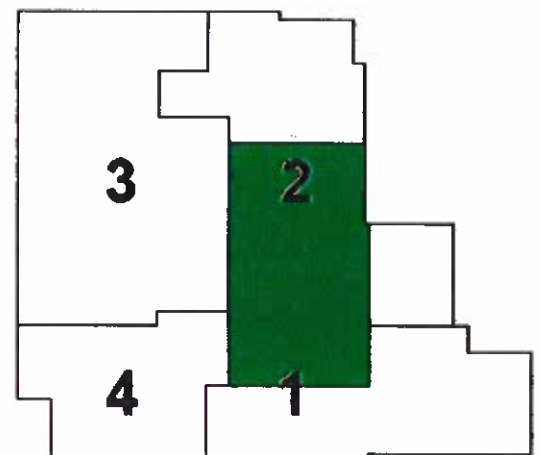

PROJECT SUMMARY

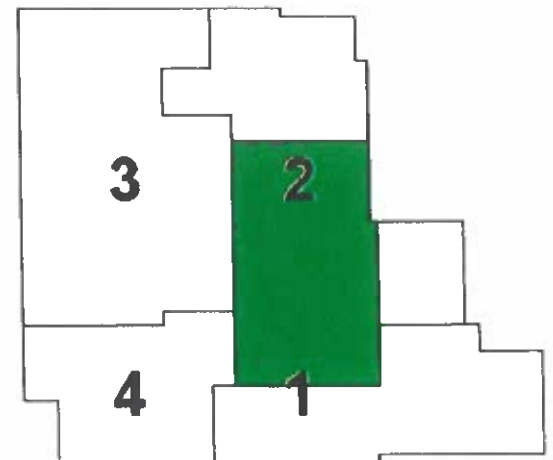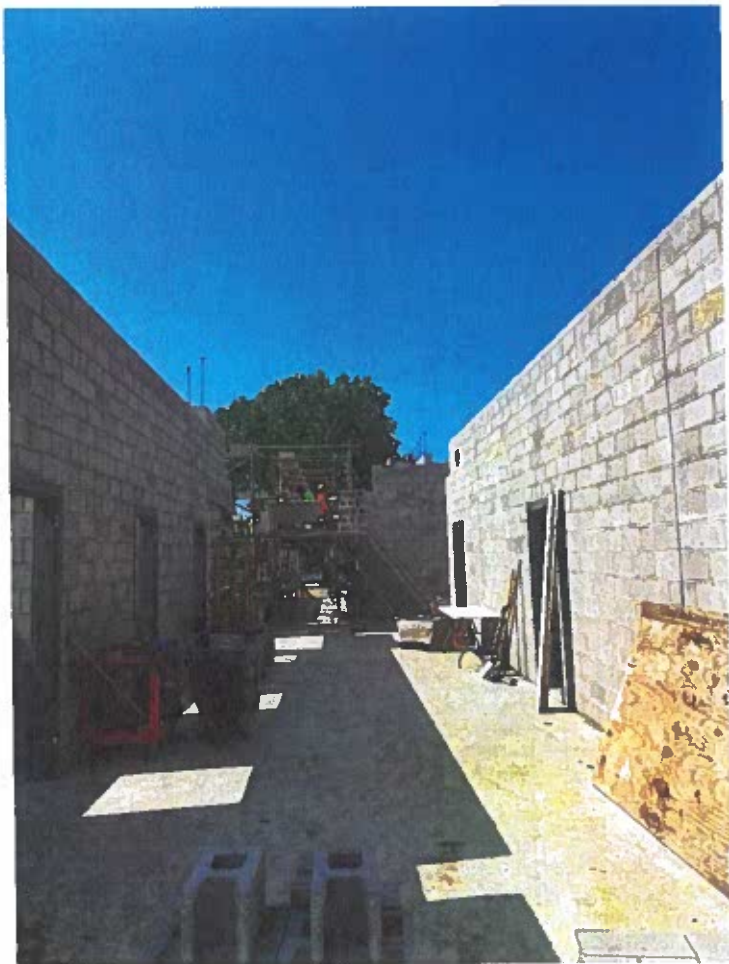

PROJECT SUMMARY

South 2/3 of Area 3 (Phase 3)


- Auxiliary GYM
- Gymnasium

September 2024 Progress

- Footers—Complete
- Precast Wall Panels 85%—Complete

Upcoming Progress

- Joist and Decking
- Demising Wall
- Slab on Grade

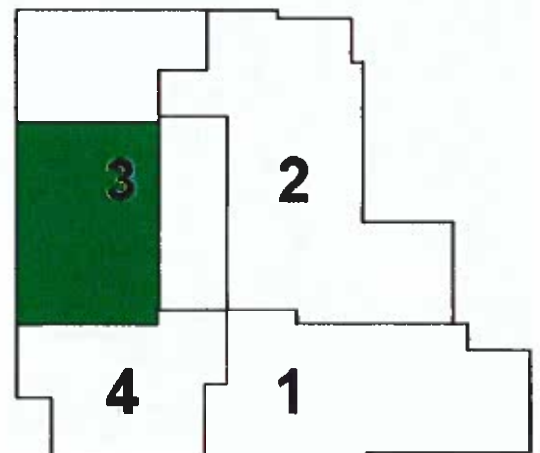

PROJECT SUMMARY

