

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
September 26, 2024

Business Services



PROJECT COMPLETE LIST

2024/2025



Site	Item Description	Funding Source	Completed Date
Grandview College Preparatory Academy	Iron Fence Painting	Facilities	09/2024
Nelson Elementary School	New HVAC Unit Replacement	Facilities	09/2024
Palm Elementary School	New HVAC Unit Replacement	Facilities	09/2024
Sparks Middle School	Front Office Security Barrier	Facilities	09/2024
Wing Lane Elementary School	HVAC Repair	Facilities	09/2024
Workman High School	Pool Fencing	Facilities	09/2024
Baldwin Academy Dibble Adult School Grazide Elementary School Kwis Elementary School La Puente High School Los Molinos Elementary School Wilson High School	Phase II of re-roofing	Facilities	09/2024
California	Bottle Filling Station	Facilities	08/2024
Cedarlane	Playground Asphalt	Facilities	08/2024
Cedarlane	Portable Installation	Facilities	08/2024
Grandview	Parking Lot Restriping	Facilities	08/2024

PROJECT COMPLETE LIST

2024/2025




Site	Item Description	Funding Source	Completed Date
Los Molinos	Bottle Filling Station	Facilities	08/2024
Mesa Robles	Classroom Flooring	Facilities	08/2024
Wing Lane	Playground Restriping	Facilities	08/2024
Wing Lane	Portable Installation	Facilities	08/2024
District Office	Portables/Restroom	Facilities	07/2024
Districtwide	Banners	Facilities	07/2024
Wilson High School	Little Theatre Improvement	CTE Grant	07/2024

Projects Completed as of September 26, 2024

NEW!

Grandview College Prep Academy – Iron Fence Painting

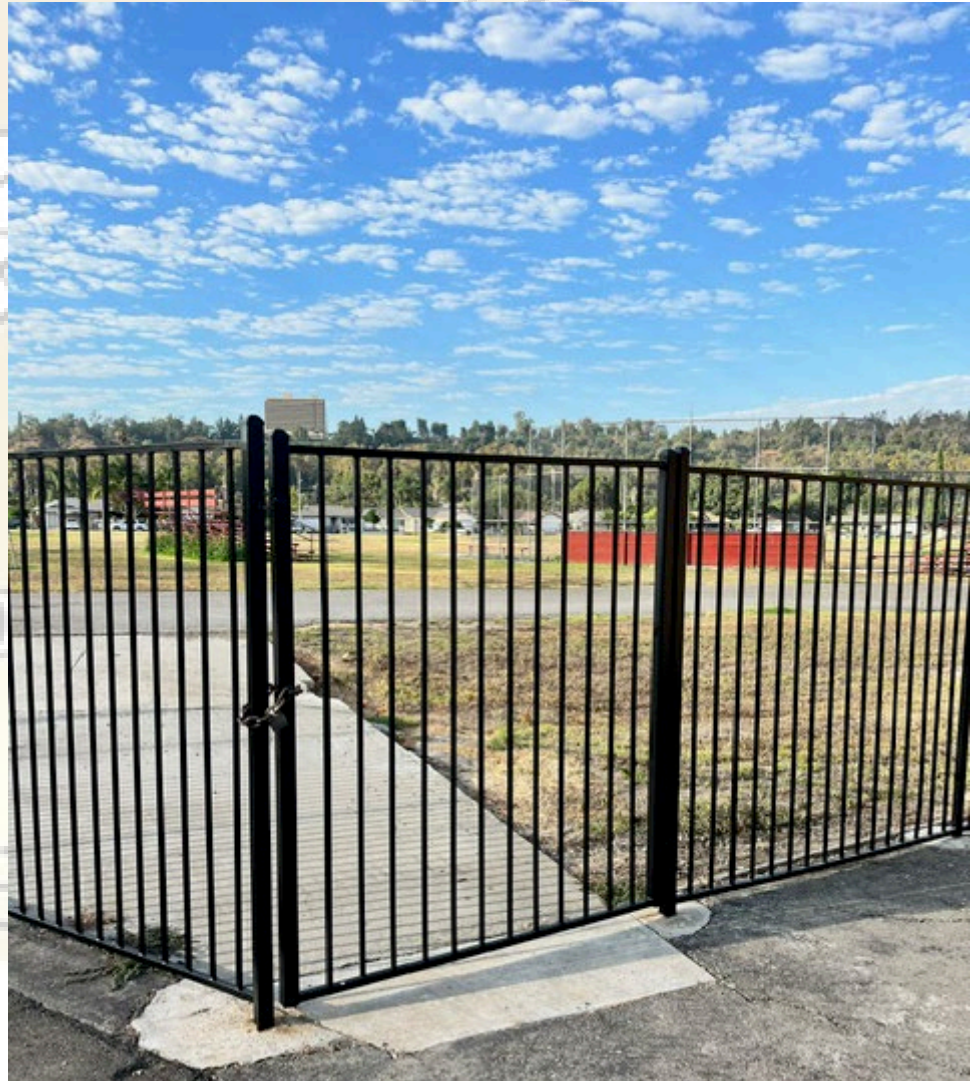

Projects Completed as of September 26, 2024

Nelson Elementary School, E-1 – AC Unit Replacement

NEW!



Projects Completed as of September 26, 2024

Palm Elementary School, P3- AC Unit Replacement

NEW!



NEW!

Projects Completed as of September 26, 2024

Sparks Middle School – Front Office Counter



Projects Completed as of September 26, 2024


Workman High School – Pool Fence Compliance

NEW!

BEFORE



AFTER

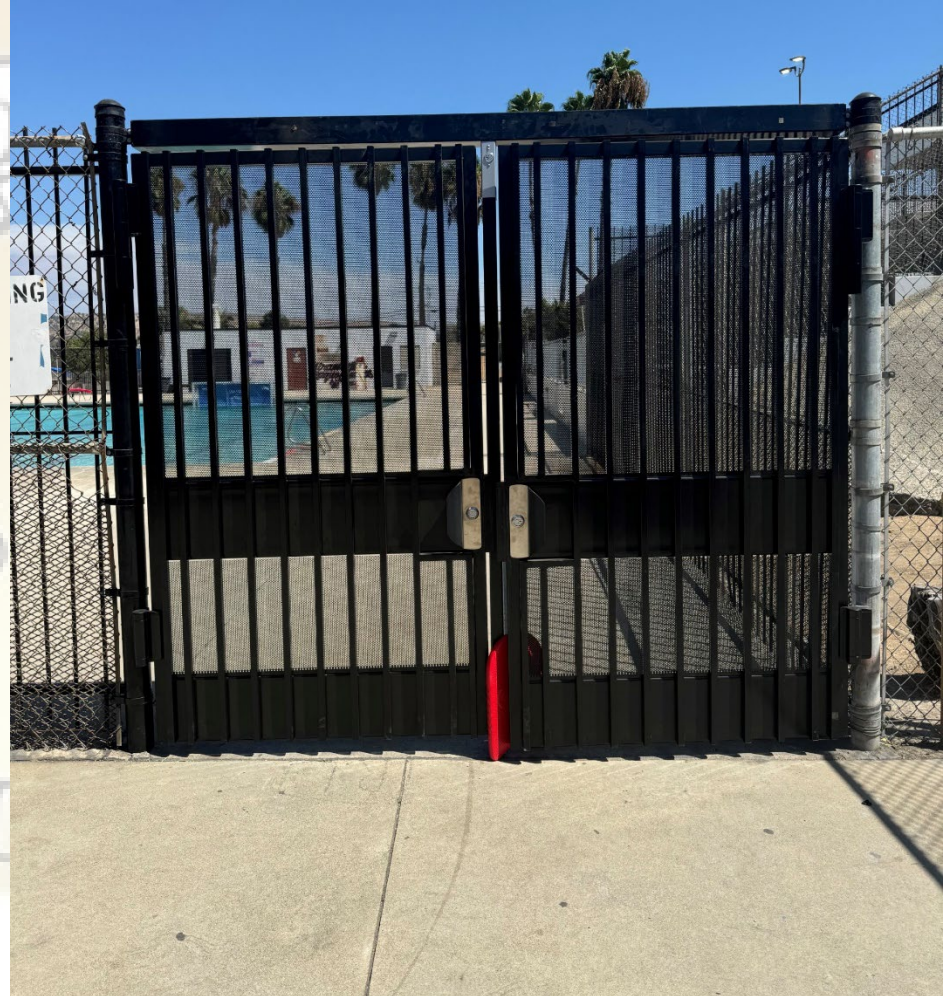

Projects In Progress

2024-2025



Projects in Progress as of September 26, 2024

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	Pending	ESSR/ General	TBD
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	Facilities	TBD
Kwis Elementary School	Baseball Fields	Complete	Approved	Pending	TBD	Facilities	TBD
La Puente High School	Custom Shade Structure	Complete	Approved	Pending	Pending	Facilities	TBD
Los Altos High School	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Complete	Approved	Complete	In Progress	Facilities	11/2024
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD
Sierra Vista Middle School	HVAC Repair MPR Room	N/A	N/A	Complete	In Progress	Facilities	09/2024
Stimson Learning Center	Phase II of re-roofing	Complete	Complete	Complete	In Progress	Facilities	10/2024
Wedgeworth Elementary School	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Wilson High School	Media Center	Pending	Pending	Pending	Pending	Grant	06/2025
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD

Projects in Progress as of September 26, 2024

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Workman High School	Phase II Stadium and Baseball Field (Phase I Track & Field and Softball Field Complete) OPTION B	Complete	Approved	Approved	In Progress	Facilities	TBD
Workman High School	Shade Structure, Wall, & Lighting	Complete	Pending	Pending	Pending	Facilities	TBD

Projects in Progress as of September 26, 2024

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD
Amar Center	Phase II of Re-Roofing	Complete	N/ A	Pending	Pending	Child Development	TBD
Fairgrove Academy Head Start	Playground & Shade Structure	Complete	Approved	Complete	In Progress	Child Development	09/2024
Nelson Elementary School Head Start	Playground, Shade Structure, & Accessibility Path of Travel	Complete	Approved	Complete	In Progress	Child Development	09/2024
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Pending	Pending	Pending	Pending	Child Development	TBD

Projects in Progress as of September 26, 2024

Special Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
La ssa lette Elementary School	Inclusive Playground	NA	NA	Complete	In Progress	Facilities	09/ 2024

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Construction of NEW Performing Arts Center @ Temple Academy	Complete	Complete	Pending	TBD	Adult Ed	12/ 2026
Dibble Adult Ed	Admin Upgrade	In Progress	NA	Pending	Pending	Adult Ed	TBD
Dibble Adult Ed	Phase II of Re-Roofing	N/ A	N/ A	Complete	In Progress	Adult Ed	10/ 2024
Willow Adult Ed	Marquee	Complete	NA	Pending	Pending	Adult Ed	TBD

Projects in Progress as of September 26, 2024

Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Pending	TBD	Food Services	TBD
District Office	Warehouse Freezer	Complete	NA	Pending	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Pending	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	Pending	TBD	Food Services	TBD

The background features a large, faint watermark of the Unifield School District logo. The logo is circular and contains the text "UNIFIELD SCHOOL DISTRICT" around the perimeter and "1970" at the bottom. In the center is a stylized illustration of a building with three arches. A horizontal bar with a green-to-teal gradient is positioned across the top of the page, partially overlapping the logo.

Next Report – October 24, 2024
