


Completed/Work in Progress:

- Complete base coat of blacktop
- Continue MCM on E and Batten Seam Panels on Area C and A (Trim/finish on entire areas and West elevations).
- Exterior Furring and Dense Glass complete except outside Area D elevation
- Completed pouring of terrazzo in Area C upstairs
- Completed Tile Area B bathroom walls. Floors prepped and started
- Work Continued Duct work in Area E
- Work continued Installation of lighting
- Continued work Electrical in Kitchen, Mezzanine Storm Shelter, Media Center, and Area E
- Exterior weather/air barrier complete
- Stair seats and Area B and D formed and ready to pour


Upcoming Look Ahead:

- Finish handrail and other related items to stairs
- Another load of MCM panels delivery the week of 10-28-24
- Rough Grading at Entrance Slopes
- Complete Permeable Pavers Scheduled for week of 10-21-24
- Complete Hydroseed and Sod in areas that are ready. Starting 10-14-24
- Finish Unistrut install in Vo Ag Lab
- Install glass in frames installed
- Sprinkler Rough-In Locker Room area and Storm Shelter
- > Installation of Strom Shelter Projectile Shields
- Pour seating under stair





Area A – Ceiling Grid has Begun in Classrooms

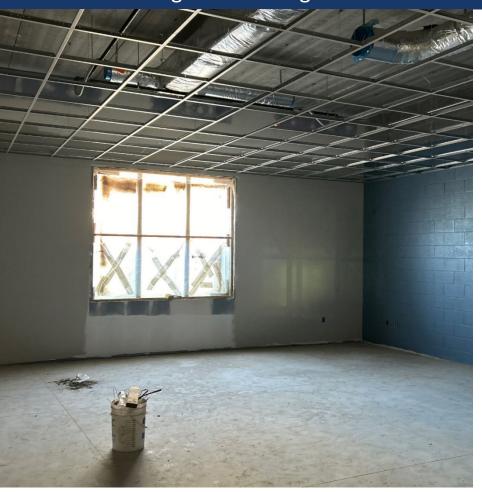




Area A – Ceiling Grid has Begun in Corridors






Area B – Platform under Stair Formed

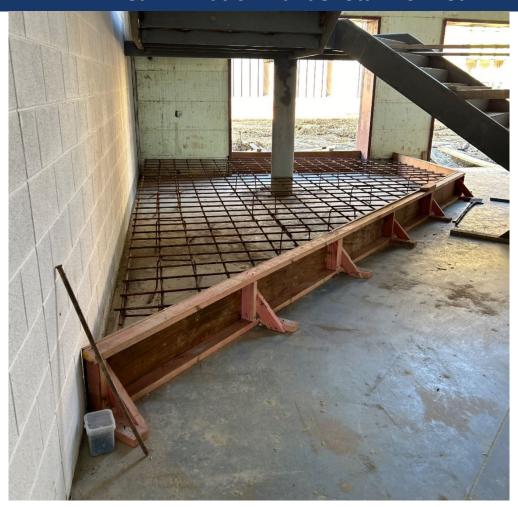




Area D – Interior Soffit Framing has Begun in Media Center

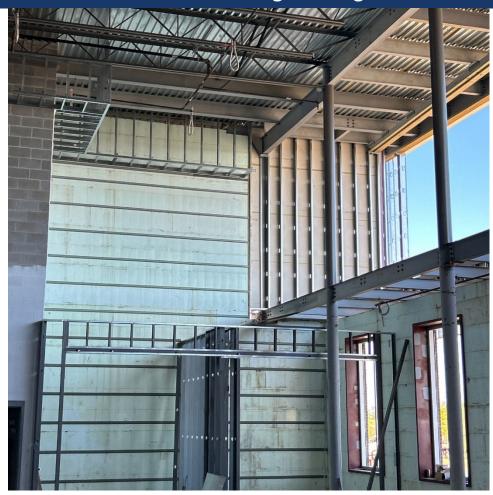



Area D – Media Center Window Framing has Begun

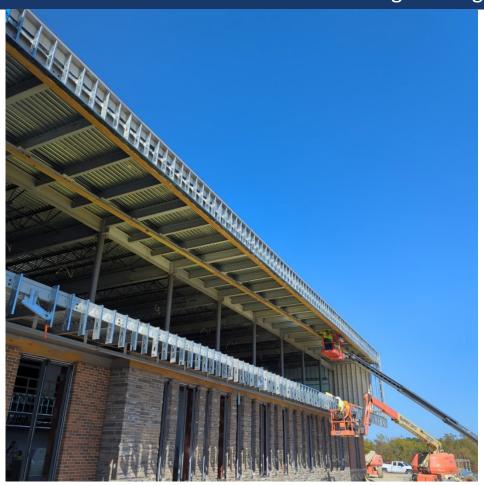



Area F – Gym Structure Painted





Site – Paving has Begun





Site – Prepping Bus Area for Paving

