


Mary E. Britton Middle School

➤ **Completed/Work in Progress:**

- Finished Steel tube for decorative handrail
- Continue MCM on E and Batten Seam Panels on Area C and A (Trim/Finish on entire areas and West elevations). Batten Seam on Low Roof Area B
- Finished Sheetrock in Area B/Administration
- Finished A, B and D second floor terrazzo pour except landings
- Tile completed in Cooler/Freezer
- Exterior weather/air barrier complete. (Touch ups in various areas)
- Finish Strut install for canopies
- Finished above ceiling work for Unistrut installation in Vo Ag Classroom

➤ **Upcoming Look Ahead:**

- Finish handrail and other related items to stairs
- Another load of MCM panels delivery the week of 10-28-24 (200 panels)
- Rough Grading at Entrance Slopes
- Complete Permeable Pavers Scheduled for week of 10/28/24
- Install glass in frames available. Starting 10/21/24
- Complete Kitchen tile
- Move into Area E with Terrazzo
- Sprinkler Rough-in Locker Room area and Storm Shelter
- Start metal studs and soffit in cafeteria
- Unit Start-ups

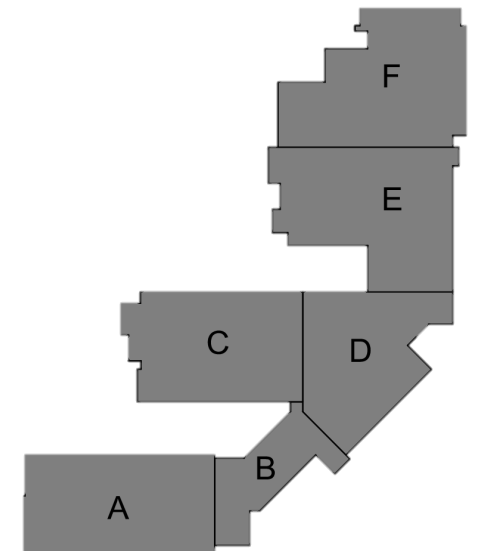

Mary E. Britton Middle School

Area A – Canopies Support Install Continues



Week Ending October 25, 2024

Mary E. Britton Middle School



Area A – Glass Install in Windows Continues



Week Ending October 25, 2024

Mary E. Britton Middle School




Area D – Under Stair Seating Poured



Week Ending October 25, 2024

Mary E. Britton Middle School



Area E – Cafeteria Windows Installed



Week Ending October 25, 2024

Mary E. Britton Middle School



Area E – Cafeteria Ductwork Install has Begun



Week Ending October 25, 2024

Mary E. Britton Middle School

Area F – Hollow Metal Frames being set



Week Ending October 25, 2024

Mary E. Britton Middle School



Area F – Kitchen Floor Prep



Week Ending October 25, 2024

Mary E. Britton Middle School



Site – Sod has begun



Week Ending October 25, 2024
