



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 28th, 2024



Last 5 Days:

- Segment D B&G Club Admin Area Flooring Install
- Segment D Admin Area Finishes – Casework & Wood Door Installation
- Segment D Admin Area – Wall and Floor Tile at Restrooms
- Segment D Admin Area – Ceiling Grid Installation.
- Taping in the Segment D Radius Entryway
- Interior Painting in Administrative Area
- Ceiling Cloud and MEPS Finishes in the Common's Area Continued.
- GYM 194 Overhead work Continued.
- LMC Flooring In-Progress
- Segment E&G Punchlist Items In-Progress
- Demolition in Phase 3A Started on the Exterior
- ID Room Buildout – Drywall Taping

Next 5 Days:

- Segment D Admin Area: Casework, Doors and Hardware to Continue
- Segment D Radius Entry Exterior Concrete.
- Interior Finishes in the Radius Entryway
- Interior Painting – Segment F ID Room
- Painting to Continue in the Administrative Office Area.
- Exterior Canopy Roofing and Soffit Installation Continued.
- GYM 194 Overhead Work to be completed.
- Floor Prep to begin for GYM 194 Wood Floor Install.
- ID Room Buildout In-Progress.
- LMC Flooring to be Completed.
- M&J Pre-Punchlist in Segment B and Exterior Site.

Key Factors:

- GYM 194 Wood Floor Install to Begin 11/04/2024
- Start of Phase 3A – Future Band and Multi-Purpose Room



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 28th, 2024



Segment A Existing Art Room – Exterior Demolition (Phase 3A)



Segment D – Exterior Site Concrete at Radius Entry




WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 28th, 2024



Segment D Radius Entry – Drywall Taping in-Progress

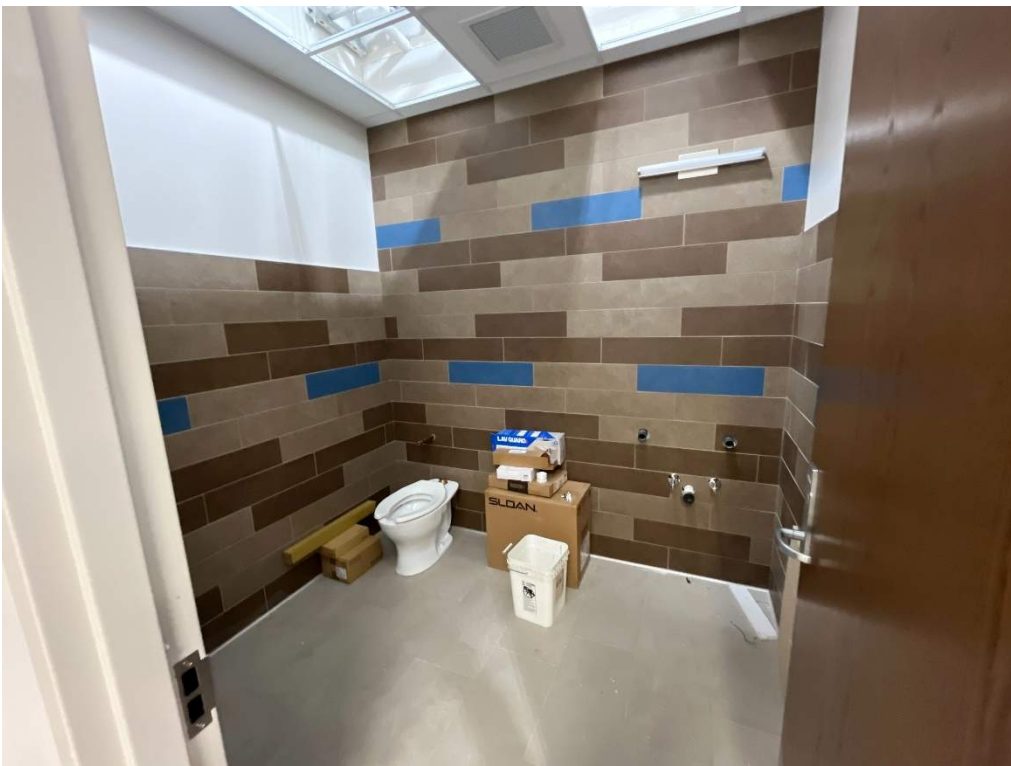

Segment D Admin Area – Tilework In-Progress



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 28th, 2024



Segment D Admin Area – Door and Hardware Install In-Progress



Segment D Admin Area – Reception Area Casework Install In-Progress



WEEKLY SUMMARY

Onalaska Middle School Addition / Renovation

October 28th, 2024



Segment E – LMC Flooring Install



Segment F – ID Room Drywall Taping/Interior Painting in-progress.
