


Completed/Work in Progress:

- Batten Seam Completed on Area B
- > All Exterior Furring, Dense Glass, and metal studs are complete
- Work Continued Ceiling Grid Area A and C, metal studs and soffits in Area C
- Work Continued Window Frame Installation. All frames currently installed have glass. All frames being installed at this time will have glass arriving last week of November. This will include everything except the large entry ways
- Work Continued –Area A 2nd Floor Polishing Terrazzo
- Work Continued Tile C/D Bathrooms
- Finished Area A K-13 install, continuing in Area C
- Finished first coat Area C second floor
- Finished paint on Door frames on C 2nd Floor
- Finished building enclosure All areas have final or temporary enclosures

Upcoming Look Ahead:

- Finish handrail and other related items to stairs. Outside aluminum handrail started on Thursday 11-7-24
- Expecting load of MCM panels at any time
- Complete Permeable pavers
- Finish Unistrut install Scheduled to start back after K-13 and 10 day curing
- Continue HVAC Room Drops
- Install Lighting
- Move into Area B downstairs and Area E with terrazzo
- Sprinkler Rough Locker Room area and Storm Shelter
- Start metal studs and soffit in cafeteria
- Unit start-ups






Area A – Window Glazing Complete






Area B – Drywall Complete

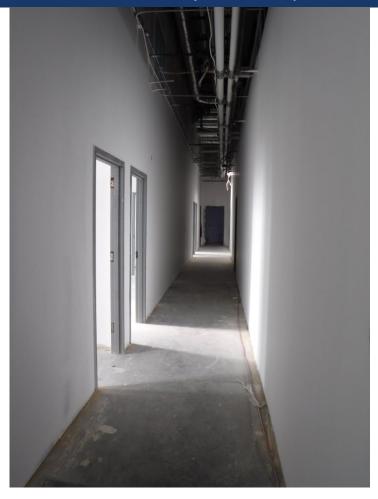




Area D – Media Center Framing Continues

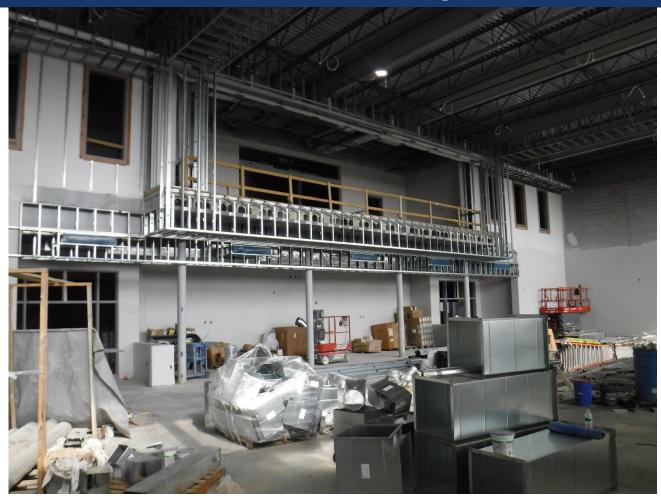



Area D – Soffit Drywall Continues

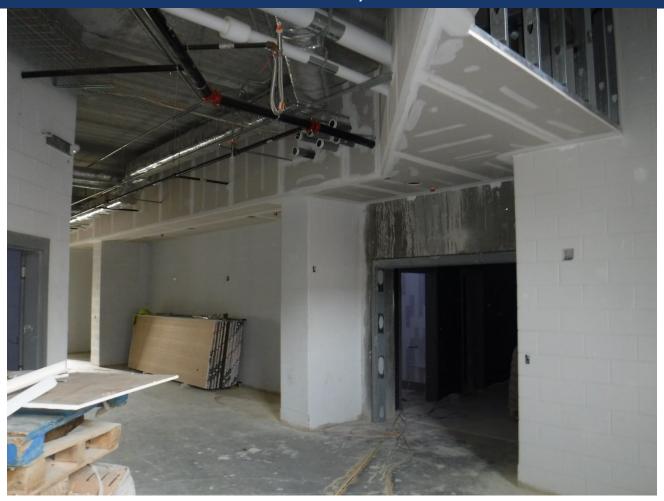



Area E – Canopy Supports Continue





Area F – Kitchen Hood Installed





Site – Permeable Paver Install has Begun



-



Site – Sidewalks at Gym Continue

