School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 11/8/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Level 1 Drywall Install
- level 2 In-Wall MEP
- Exterior Glazing Install
- RTU Installation
- Art/makers Roof Install

2 WEEK LOOK AHEAD

- Drywall Finishing level 1
- Temporary heat will be turned on
- In-Wall MEP Install Level 2
- Roof Completion









First Floor Drywall Install



BUILDINGTHEFUTURE.JEDUNN.COM



Exterior Glazing & Panel Install







SAFETY
EVERYONE.
EVERYWHERE.
ALL THE TIME.



Second Floor Interior MEP





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 10/15/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Second Floor Interior Framing
- Area B Roof Install
- Main Entrance Brick Install
- First Floor In-wall Rough-In
- First Floor Window Install

2 WEEK LOOK AHEAD

- Roof Will Be Completed
- First Floor Interior Drywall
- Second Floor Interior Rough-In
- Kitchen Area Brick Install
- Exterior Metal Panel Install












BUILDINGTHEFUTURE.JEDUNN.COM



Exterior Brick Install Progress





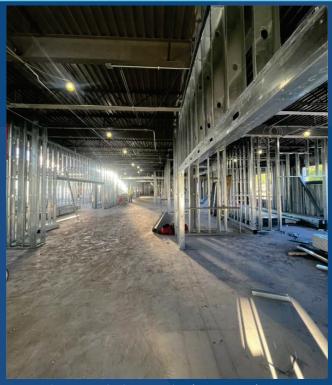

Second Floor Interior Framing

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Roof Install Progress





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 9/18/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- First Floor Interior Framing
- South Parking Lot Asphalt Install
- First Floor Overhead MEP
- Exterior Brick Install
- Area A Roof Install

2 WEEK LOOK AHEAD

- -Area B Roof Install
- Exterior Metal Panel Install
- Exterior Brick Install
- First Floor In-Wall Rough-In
- Second Floor Overhead MEP









Area A Brick Install



BUILDINGTHEFUTURE. JEDUNN. COM



Interior Framing Install








South Lot Asphalt Install

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.

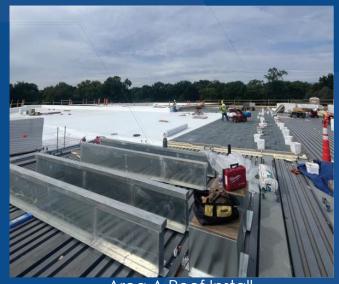

Area A Roof Install





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 8/23/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area B Exterior Stud Framing/Sheathing
- Area A Overhead MEP
- Area A Weatherproofing
- -Gym Roof Install
- -Gym Masonry Wall Install

2 WEEK LOOK AHEAD

- -Area A/B Roof Install
- -Area A Interior Framing
- -Area B Overhead MEP
- -Area B Weatherproofing
- -Exterior Masonry Install









Gym CMU Wall Install





South Radius Wall Progress







Overhead MEP Progress

SAFETY
EVERYONE.
EVERYWHERE.
ALL THE TIME.



Gym Roof Install





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 7/05/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area A Structural Steel Detailing
- Slab On Grade Concrete Complete
- Light Pole Base Layout
- Area B Structural Steel Installation

2 WEEK LOOK AHEAD

- Area B Structural Steel Detailing
- Area A Slab On Metal Deck Concrete Floor
- Exterior Framing









Area A Structural Steel Detailing



BUILDINGTHEFUTURE. JEDUNN. COM



Completed Concrete Slab







Kitchen Structural Steel Erection

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



West Side Site View





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 6/21/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area A Structural Steel Erection
- Kitchen/Gym Slab Install
- Underground MEP Completed

2 WEEK LOOK AHEAD

- Area A Structural Steel Detailing
- Slab On Grade Concrete Complete
- Light Pole Bases Install









Area A Structural Steel Install



BUILDINGTHEFUTURE. JEDUNN. COM



Area A Steel







Kitchen Concrete Slab Preparation

SAFETY
EVERYONE.
EVERYWHERE.
ALL THE TIME.



North West Corner Site View





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 6/7/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area A & B Recessed Slab Install
- Area B South Slab Install
- Kitchen Underground MEP
- Gym Underground MEP

2 WEEK LOOK AHEAD

- Kitchen Slab Install
- Gym Slab Install
- Area A Structural Steel Erection









Area A Slab Install



BUILDINGTHEFUTURE.JEDUNN.COM



Cafeteria Slab Install







Completed FEMA Gym Install

SAFETY
EVERYONE.
EVERYWHERE.
ALL THE TIME.



Kitchen Underground MEP





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 5/24/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area A/B South Underground MEP
- Grouting of Pre-Cast Concrete

2 WEEK LOOK AHEAD

- Area B South Slab Install
- Structural Steel Delivers to Site
- -Kitchen Underground MEP
- Gym Slab Install









Ongoing Underground MEP



BUILDINGTHEFUTURE. JEDUNN. COM



Area B North Slab Install







Installed FEMA Gym

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



FEMA Gym Install





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 4/19/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area B Footing Install
- Area A Underground MEP Install
- Site Utility Install

2 WEEK LOOK AHEAD

- Area B Underground MEP Install
- Area A Concrete Slab Install









Retaining Wall Progress



BUILDINGTHEFUTURE. JEDUNN. COM



Underground MEP Area A







Area B Footing Install

SAFETY
EVERYONE.
EVERYWHERE.
ALL THE TIME.



Admin Area Concrete Install





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 4/5/2024

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Area A Footing Install
- Underground MEP Install
- Retaining Wall Install

2 WEEK LOOK AHEAD

- Area A Concrete Slab Install
- Area B Footings Install









Retaining Wall Install



BUILDINGTHEFUTURE. JEDUNN. COM



Radius Storefront Footings







Gym Footing Install

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Site Utilities Install








Tomahawk Elementary School

Site Plan

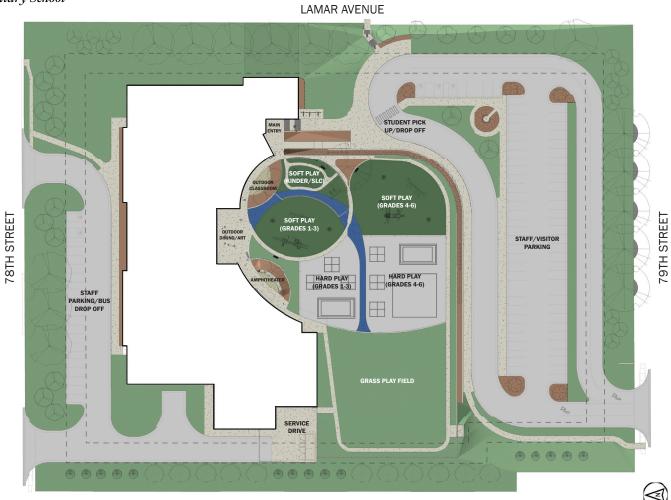











Tomahawk Elementary School

Floor Plan: Level 01



Tomahawk Elementary School

Floor Plan: Level 02









