



PROGRESS UPDATE

GREENPORT UNION FREE SCHOOL DISTRICT

DATES: 1/12/2022-6/2/2023

GREENPORT SCHOOL PROJECT-A, B & C

Renu GC:

- Completed cmu and brick at the new addition
- Completed watertight roofing at the new addition
- Completed installing 85% of the new doors installed with temp locks- working on door hardware
- Completed 3rd floor library additional window caulking
- Completed installing window louvers for upcoming summer work
- Completed OT/PT new ceiling
- Completed new exterior concrete pads/ ramps at the new addition
- Completed pouring concrete pad in the new addition
- Completed new steel in girl's locker room (Bathroom area) and storage room
- Steel erected in the basement below elementary library
- Framing, sheetrock, and door installed for additional closet in rm 117
- 85% of roof curbs cut in for upcoming summer work
- Installing act tiles in girl's locker room ceiling

Bana Electrical:

- Completed new lights in girl's locker room
- Completed new lights in OT/PT
- Completed new power pedestals in the 3rd floor library

D & S Mechanical:

- Completing dampers and duct work in ceilings for upcoming summer work
- Completed duct work at new gym addition- waiting on RTU's (lead times)


WHM Plumbing:

- Completed piping elements at new addition



GREENPORT UNION FREE SCHOOL DISTRICT

DATES: 1/12/2022-6/2/2023

GREENPORT SCHOOL PROJECT-A, B & C

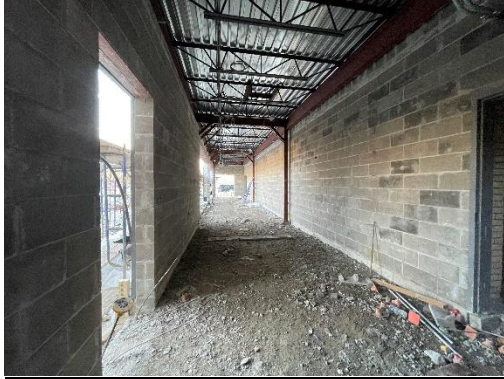

GREENPORT SCHOOL PROJECT-A, B & C

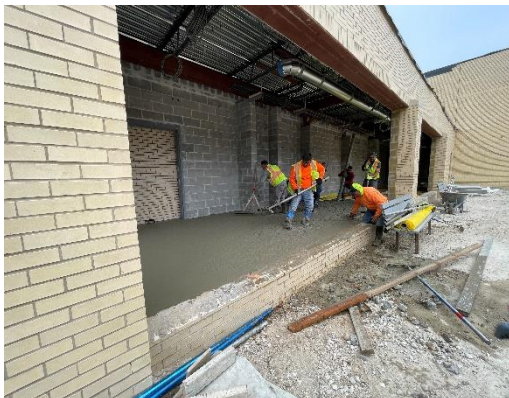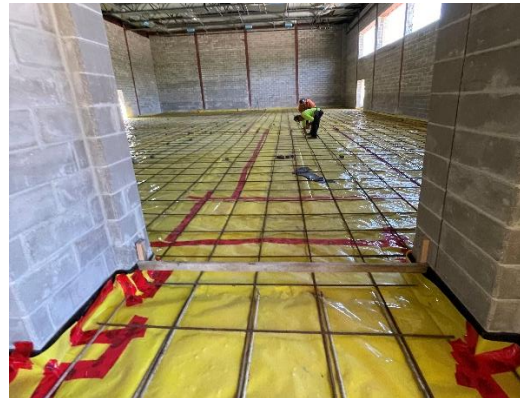

GREENPORT UNION FREE SCHOOL DISTRICT

DATES: 1/12/2022-6/2/2023

GREENPORT SCHOOL PROJECT-A, B & C

