




New Construction

PROGRESS UPDATE
November 2024

Fairport Harbor New Pre K-12 School



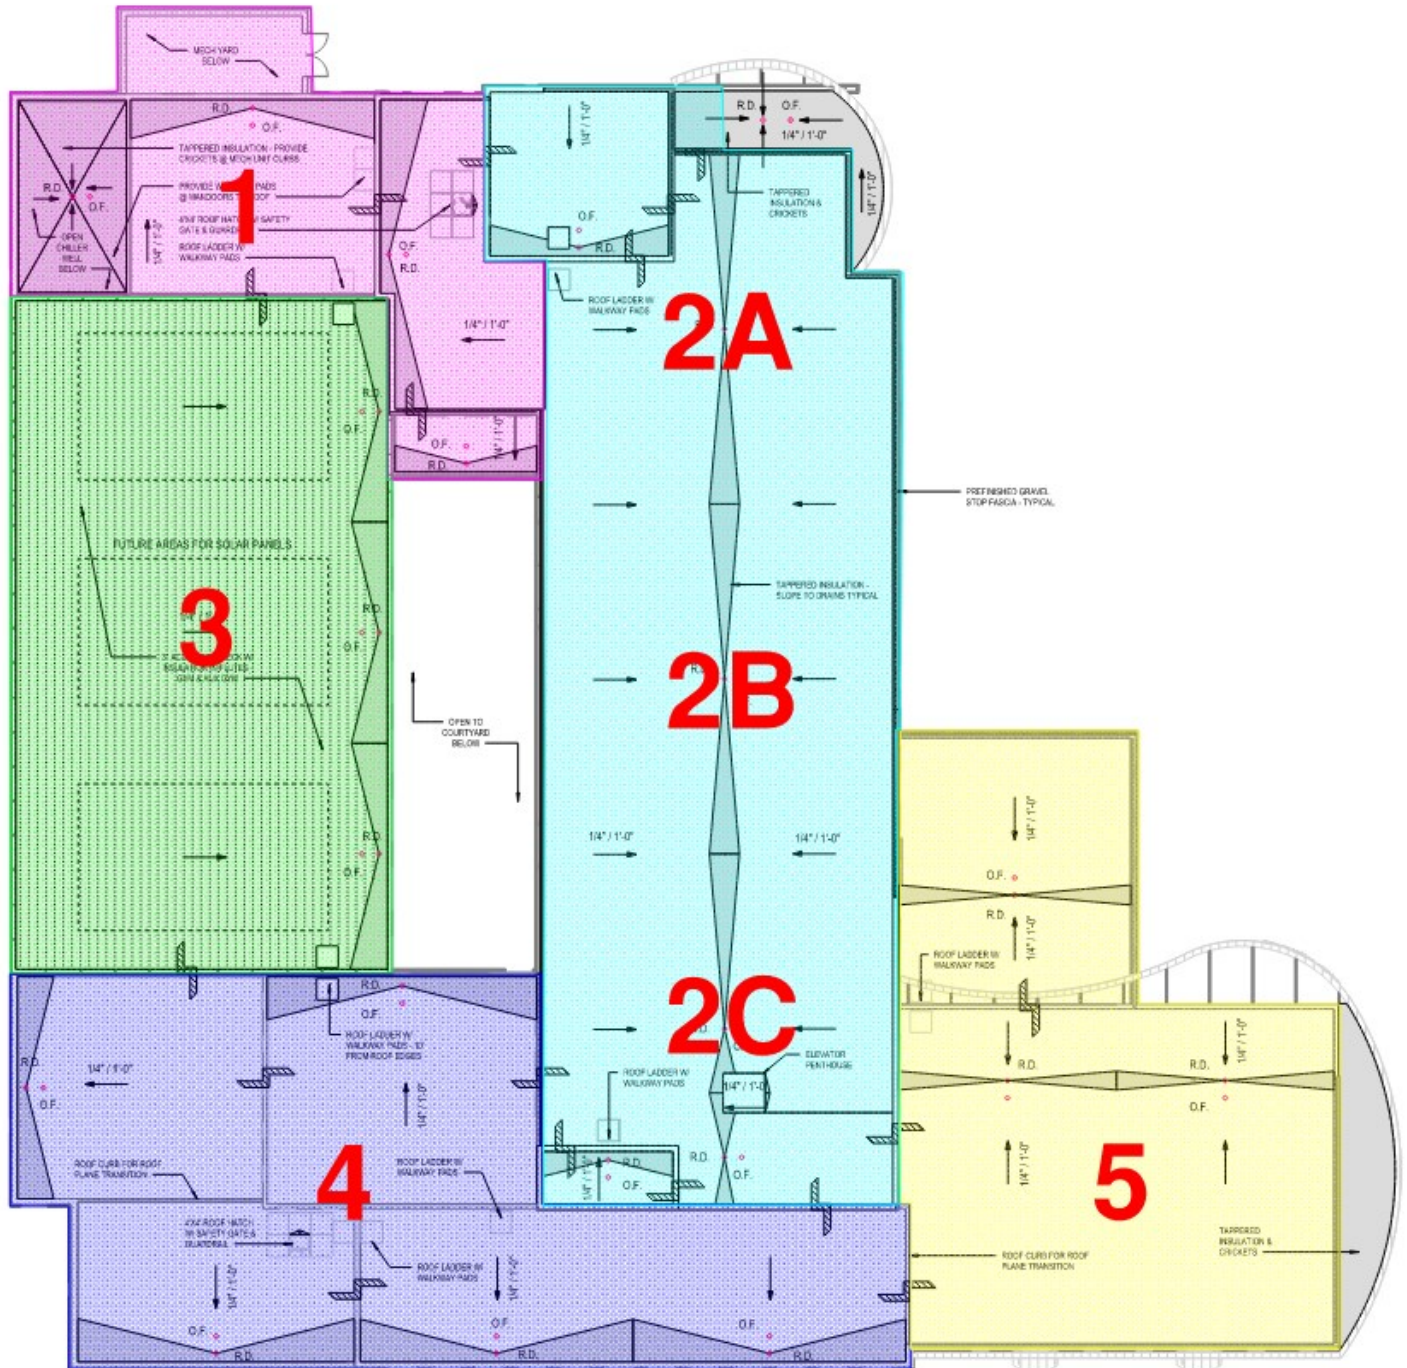

PROJECT SUMMARY

Phase 1


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

November 2024 Progress


- Frost Slabs—Complete
- Sprinkler Line—In Progress
- Duct and Pipe Insulation—In Progress
- Framing Ceilings—In Progress

Upcoming Progress

- Install Windows
- Install Temporary Doors

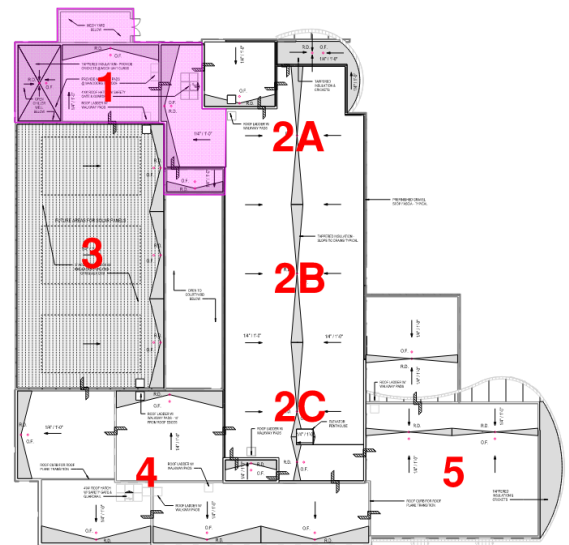

PROJECT SUMMARY

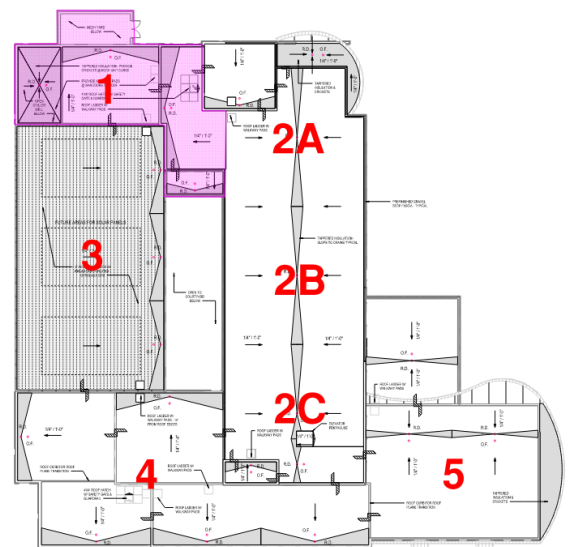

PROJECT SUMMARY

Phase 2A


- Educational Classrooms

November 2024 Progress


- Brick Veneer—In Progress
- Roof Membrane—In Progress
- Mechanical—Complete
- Soffit and Ceiling Framing—In Progress

Upcoming Progress

- Temporary Dry In
- Install Windows

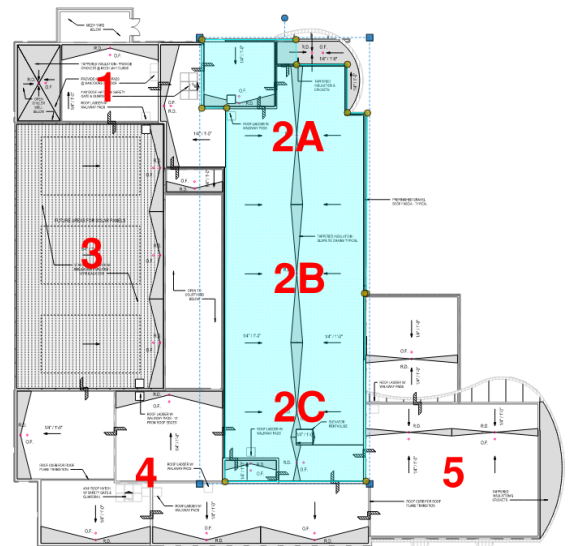

PROJECT SUMMARY

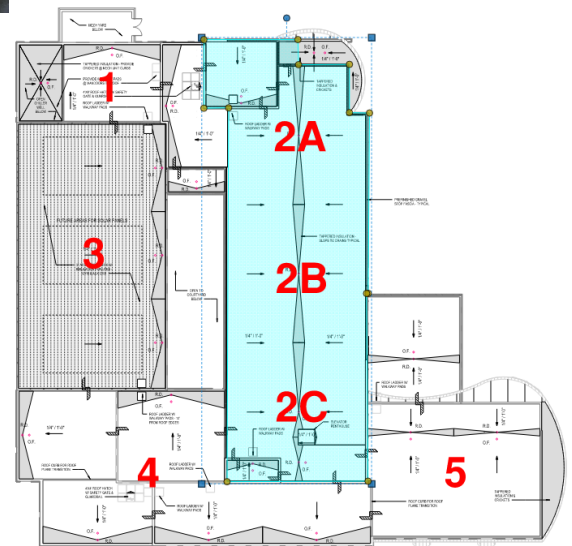

PROJECT SUMMARY

Phase 2B and 2C


- Educational Classrooms

November 2024 Progress


- Structural Steel for Roof—Complete
- Masonry Bearing for 3rd Floor—Complete
- Precast Plank 3rd Floor—Complete
- Concrete Topping 3rd Floor—Complete
- Masonry Bearing for Roof—In Progress
- Overhead Plumbing Rough In—In Progress
- Overhead Electrical Rough In—In Progress

Upcoming Progress

- In wall Rough In's 3rd Floor
- Roof Joist
- Roof Decking
- Non Bearing Walls 3rd Floor

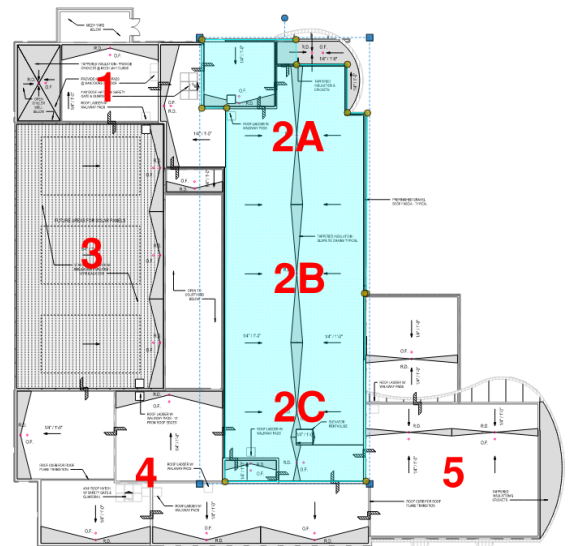

PROJECT SUMMARY

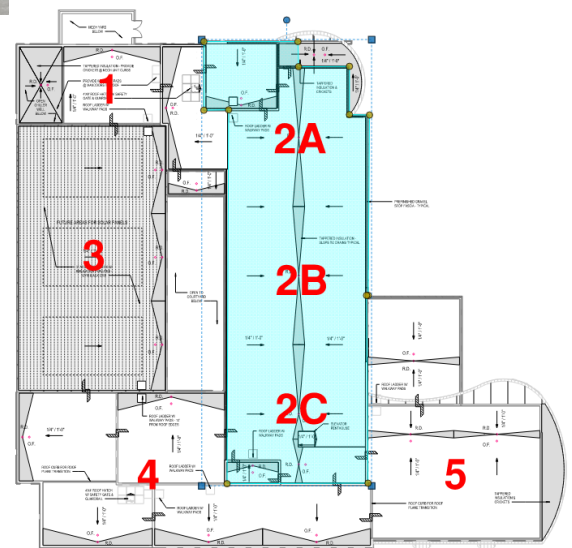

PROJECT SUMMARY

Phase 3


- **Auxiliary GYM**
- **Gymnasium**

November 2024 Progress


- **Roof Membrane—90% Complete**
- **Demising Wall—In Progress**
- **Slab on Grade Main GYM—90% Complete**
- **Overhead Mechanical—In Progress**
- **Roof Drain Piping—In Progress**

Upcoming Progress

- **Overhead Electrical**
- **Remainder of Precast Wall Panels**
- **Remainder of Roof Decking**
- **Remainder of Roof Membrane**
- **Remainder of Slab on Grade**

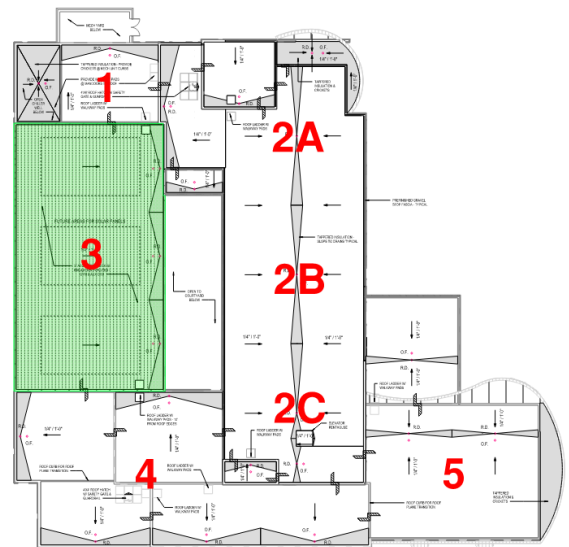

PROJECT SUMMARY

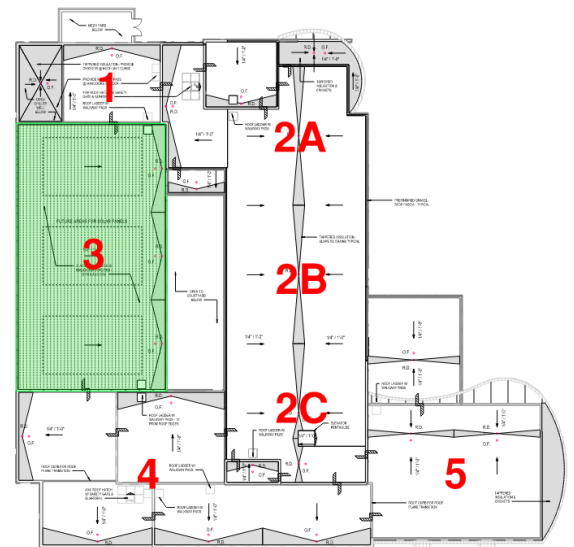

PROJECT SUMMARY

Phase 4 (West Half)


- Kitchen
- Locker Room

November 2024 Progress

- Footers—Complete
- Underground Plumbing—Complete
- Underground Electrical—In Progress
- Masonry to Grade—Complete

Upcoming Progress

- Slab On Grade
- Masonry to Bearing
- In Wall Electrical Rough In
- In Wall Plumbing Rough In

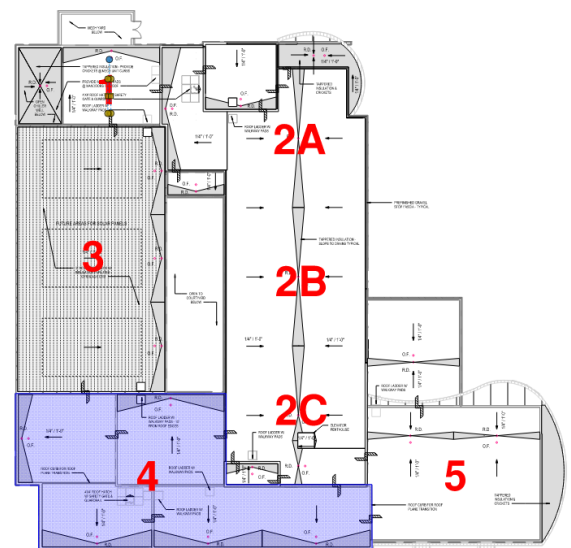

PROJECT SUMMARY

