


TimberQuest - Golden West Middle School

ID	Task Name	Duration	Start	Finish	October	November	December	January	February	March	April	May	June	July	August	September	October
					9/29/24	10/30/24	11/30/24	12/31/24	1/31/25	2/28/25	3/31/25	4/30/25	5/31/25	6/30/25	7/31/25	8/31/25	9/30/25

19	MASS TIMBER FABRICATION	105 days	Tue 12/3/24	Tue 4/29/25
20	Secure Fabrication Slot	0 days	Tue 12/3/24	Tue 12/3/24
21	Model Validation	8 wks	Wed 12/4/24	Tue 1/28/25
22	Press	10 days	Wed 1/29/25	Tue 2/11/25
23	Ship wall CLT	2 wks	Wed 2/12/25	Tue 2/25/25
24	Roof panel assembly (3 panels / dday) - Bldg A	10 days	Wed 2/12/25	Tue 2/25/25

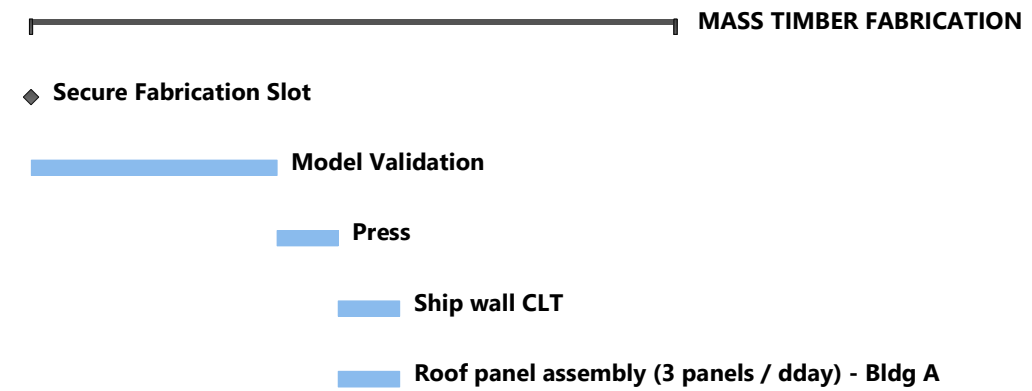

TimberQuest - Golden West Middle School

ID	Task Name	Duration	Start	Finish	October	November	December	January	February	March	April	May	June	July	August	September	October
49	Roof	3 wks	Tue 4/22/25	Mon 5/12/25													
50	Glass	2 wks	Tue 4/22/25	Mon 5/5/25													
51	Interiors	5 wks	Tue 4/22/25	Mon 5/26/25													
52	Punchlist / Finals	2 wks	Tue 5/27/25	Mon 6/9/25													
53	BLDH B	70 days	Tue 3/11/25	Mon 6/16/25													
54	Foundations / Slab / UG Utilities	6 wks	Tue 3/11/25	Mon 4/21/25													
55	Panel installation	1 wk	Tue 4/22/25	Mon 4/28/25													
56	Roof	3 wks	Tue 4/29/25	Mon 5/19/25													
57	Glass	2 wks	Tue 4/29/25	Mon 5/12/25													
58	Interiors	5 wks	Tue 4/29/25	Mon 6/2/25													
59	Punchlist / Finals	2 wks	Tue 6/3/25	Mon 6/16/25													
60	BLDH C	70 days	Tue 3/18/25	Mon 6/23/25													
61	Foundations / Slab / UG Utilities	6 wks	Tue 3/18/25	Mon 4/28/25													
62	Panel installation	1 wk	Tue 4/29/25	Mon 5/5/25													
63	Roof	3 wks	Tue 5/6/25	Mon 5/26/25													
64	Glass	2 wks	Tue 5/6/25	Mon 5/19/25													
65	Interiors	5 wks	Tue 5/6/25	Mon 6/9/25													
66	Punchlist / Finals	2 wks	Tue 6/10/25	Mon 6/23/25													
67	BLDH D	70 days	Tue 4/29/25	Mon 8/4/25													
68	Foundations / Slab / UG Utilities	6 wks	Tue 4/29/25	Mon 6/9/25													
69	Panel installation	1 wk	Tue 6/10/25	Mon 6/16/25													
70	Roof	3 wks	Tue 6/17/25	Mon 7/7/25													
71	Glass	2 wks	Tue 6/17/25	Mon 6/30/25													
72	Interiors	5 wks	Tue 6/17/25	Mon 7/21/25													

