



South Orange-Maplewood Schools Renovations to Maplewood Middle School

Week of the 22nd of July Construction Activities:


- Fire Alarm, PA and controls wiring now happening during 1st shift.
- Legacy UV openings in classrooms patching & boxing out continues.
- VUV louver installation continues.
- VUV Extension & Sleeves Installation underway.
- Interior electrical & mechanical conduit, piping runs continue.
- Non-Friable Floor abatement completed. Floors being prepped for Vinyl Tiles.
- More rooftop equipment lifted into place, i.e., ERU 6- 10.
- Area B slate roof shingle removal and new installation continues.
- Boiler piping & valve installation underway.
- **Averaging over 50 workers on site per day (peaked at like 65 this week). 7 to 5 pm weekly. Plus, weekend OT to stay on schedule.**




Site Map for Reference Only



New Floor Tiles- 2nd Floor Installation Classrooms 288, 287 & underway 295

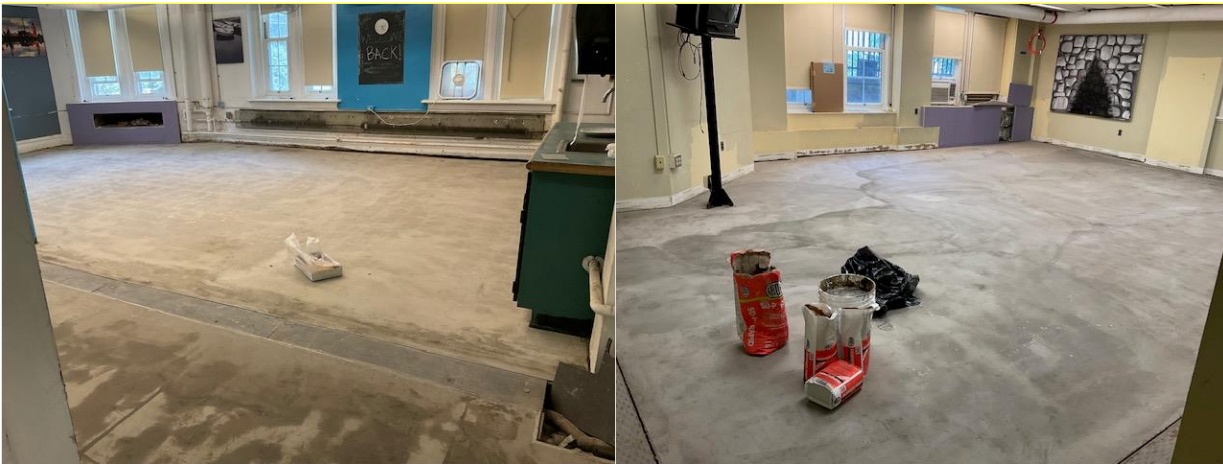

Basement- **Left-: Teacher's Lounge floor prep & legacy UV openings boxed out for new UV. **Right**- Classroom 017 floor prep and here too legacy UV opening is boxed out for new UV. (Vinyl Tile Flooring on site. Installation expected to begin next week.)**

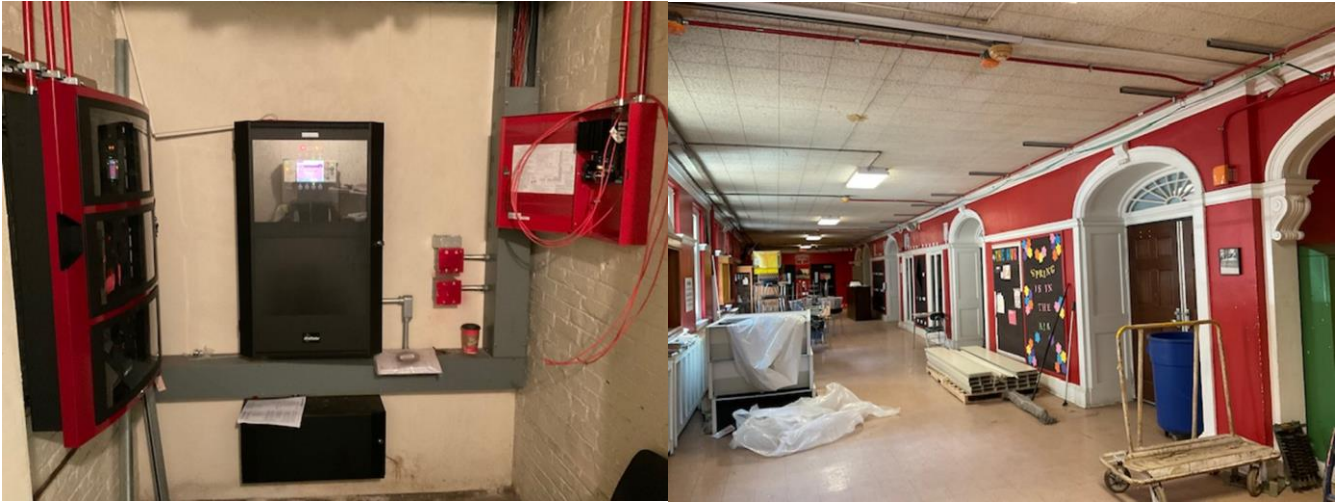

Fire Alarm Panel Fit-Up Underway & Devices Being Wired out in the Spaces (Estimated @ 80% completed on 2nd floor, 70% completed 1st Floor; 80% Completed in Basement.)

PA System: Wiring the same % completions as FA system on a per floor basis. Coordinating system requirements with IT. Expecting all equipment delivery next week.



Aux Gym- Left: Energy Recovery Unit Hoisted into place. Right: Utility Piping Underway




Left- Gym AC Units Lifted into place. **Right-** Gym ductwork underway. Demo of legacy AHUs started.



Area B facing Dunnell Road Slate Roof Replacement with Asphalt Shingles- continues. (Roofing 80% or more completed)



Courtyard Heat Pumps: Conduit runs for wiring underway (not all shown).

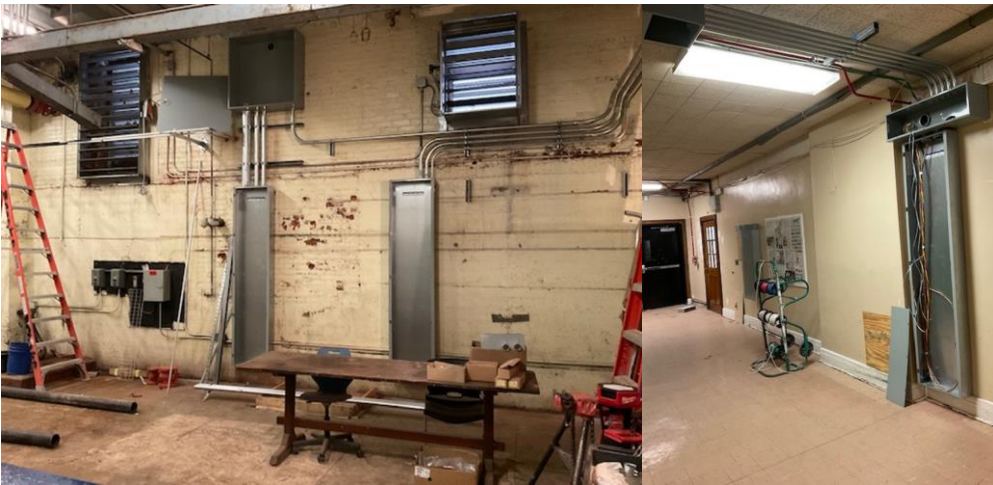

Left: Boiler Room Electrical Panels
Right: 1st Floor Electrical Panels Outside Auditorium




Cafeteria ductwork underway.



Girls & Boys Locker Rooms- Ductwork underway



Library: Conduit runs, Duct hangers & Duct staged in space.

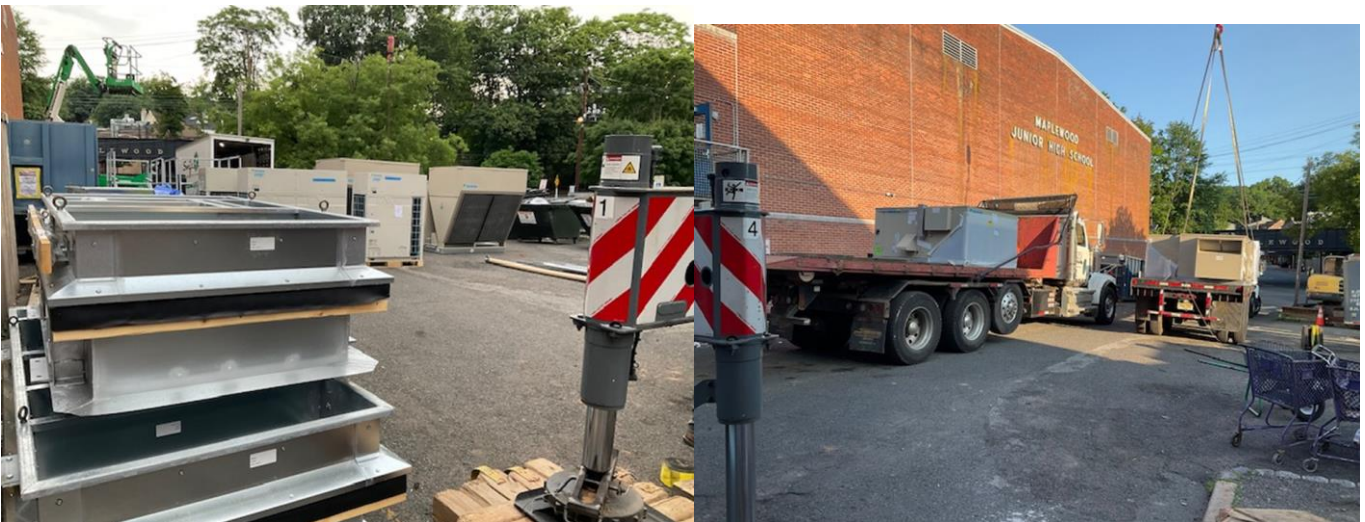

Crane Equipment Lifts: Left: 1st lift ~ week ago; Right #2 (today), final lift scheduled for next week.



Boiler Room piping & valving installation underway. Estimate @ 30% Complete.
