

2024 Bond Program Update Jeffrey Brogden, Associate Superintendent, Facilities & Bond Programs – January 21, 2025

January Update & Considerations

Board Approvals

- **Purchase additional Buses**
- Police and Safety & Security Building DDs (Design) **Development Drawings)**

Early Learners Academy Schematic Design (SD) approved at **December 2024 Board Meeting** Design Development Drawings (DD) -**February 2025 Board Meeting** Substantial Completion July 2026


Total Estimated Project Budget \$47.5 M

Police and Security Building

 Design Development Drawings (DD) -January 2025 Board Meeting
Substantial Completion July 2026
Total Estimated Project Budget \$31.4 M

Police and Security Building Site Review

MANSFIELD INDEPENDENT SCHOOL DISTRICT POLICE AND SAFETY OPERATIONS CENTER

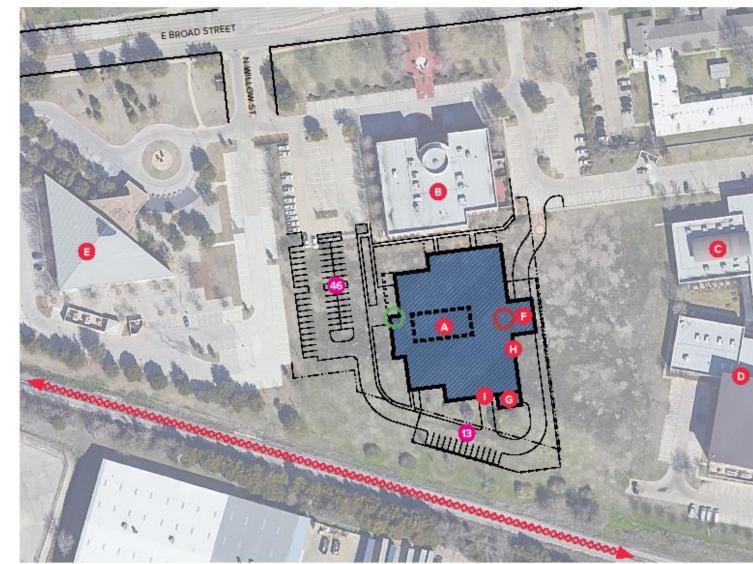

Huckabee

POLICE AND SAFETY OPERATIONS CENTER I MANSFIELD INDEPENDENT SCHOOL DISTRICT DRAFT COPY ONLY NOT FOR REGULATORY APPROVAL, PERMITTING OR CONSTRUCTION. JOSHUA COGBURN TX - 28423



Main Entry



Existing Tarrant County Tax Office

Sally Port

Wash Bay
Custodial Receiving
Camera / Fire Alarm Unloading

Camera / Pire Alarm Unio

Tornado Shelter Boundary

Parking Space Count

B--- Fence Line


Existing Railroad Track

BO PROPOSED SITE PLAN

Middle School Orchestra Additions

Design Development Drawings (DD) - February 2025 Board Meeting

Substantial Completion June 2027

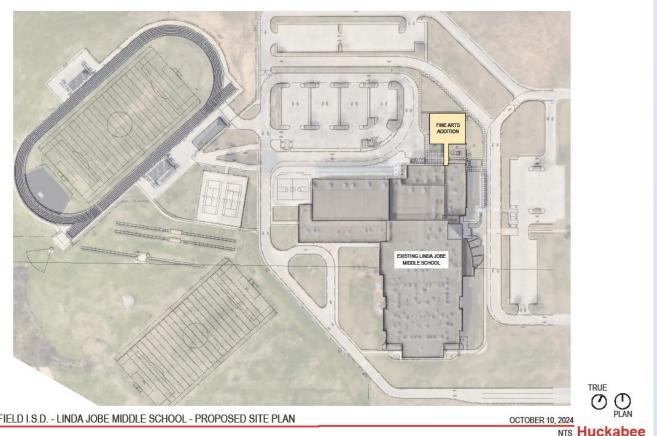


Ben Barber Innovation Academy Frontier STEM Academy



 Design Development Drawings (DD) – February 2025 Board Meeting
Substantial Completion June 2027
Total Estimated Project Budget \$22.5 M

BBIA – Frontier Site Concept

MANSFIELD ISD BEN BARBER INNOVATION ACADEMY - ADDITIONS AND RENOVAT

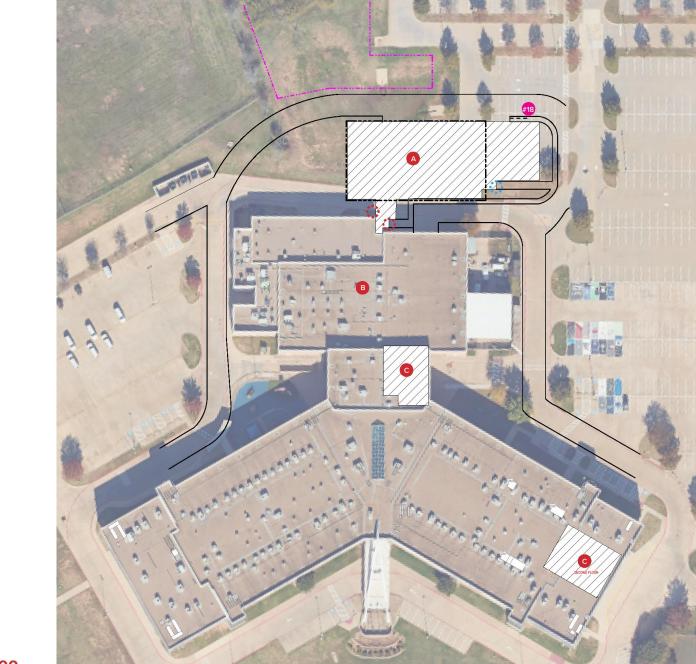



DRAFT COPY ONLY NOT FOR REGULATORY APPROVAL, PERMITTING OR CONSTRUCTION. JOSHUA COGBURN TX - 28423

LEGEND

A	Proposed New CTE Addition
B	Existing Building
C	Proposed Renovation
	Proposed Tornado Shelter
$\langle 0 \rangle$	Proposed Main Entry Entry
\odot	Proposed Secured Entry
#	Parking Space Count (Spaces Removed)
	Existing Detention to be Modified



Baseball – Softball Turf and Covered Batting Cages

Locations within the Sites

Design Development Drawings (DD) -February 2025 Board Meeting Substantial Completion November 2025 Total Estimated Project Budget \$23.9 M

High School Tennis Court Lights

Contractor approved at October 2024 Board Meeting Construction in progress Substantial Completion Early 2025 Summit HS – Complete **Timberview – Light Poles Installed**

Interior Lighting Upgrade **Site Evaluations** (13 Facilities) Contract Approved December 2024 Board Meeting Substantial Completion May 2025 Current Project Budget \$3.4 M Projected kWh Savings 2.3 M kWh per year

Wester MS, Cross Timbers IS, Shepard IS, Morris ES, Gideon ES, Orr IS, RLA Complex, Worley MS, Summit HS, Howard MS, Brown ES, Phoenix Academy, Warehouse

Weapons Detection System – Evolv Middle Schools & Stadiums

Evolv Installation Complete
Installing Additional Cameras
Installation 95% Complete
Programing / Integration 50% Complete

Transportation – Buses Purchase Order Issued for 66 Reg Route Buses & 26 SPED Buses **As of January 1, 2025** >6 Special Pops Buses Rec'd >40 Regular Route Buses Rec'd > Approval to order 37 Additional Buses – January 2025 Board Meeting **Estimated Budget \$26 M**



Replacement Furniture Capital Improvement Plan Furniture Replacement Mary Orr Intermediate (1998) & Summit High School (1995) Donna Shepard Intermediate (2001) & Mansfield High School (2002) Phase 1 Completion – August 2025 Phase 2 Completion – August 2026 **>**Total Estimated Budget \$7.1 M **Vendor Fair October 3rd & 4th Finalizing Feedback from Participants**






Safety & Security – Cameras & Servers > Developing Specifications > Design Meetings – January 2025 > Phase 1 HS & MS

Phase 2 IS & ES

Phase 3 Auxiliary Bldgs.
Total Estimated Budget \$7.1 M

Technology – Fiber Ring

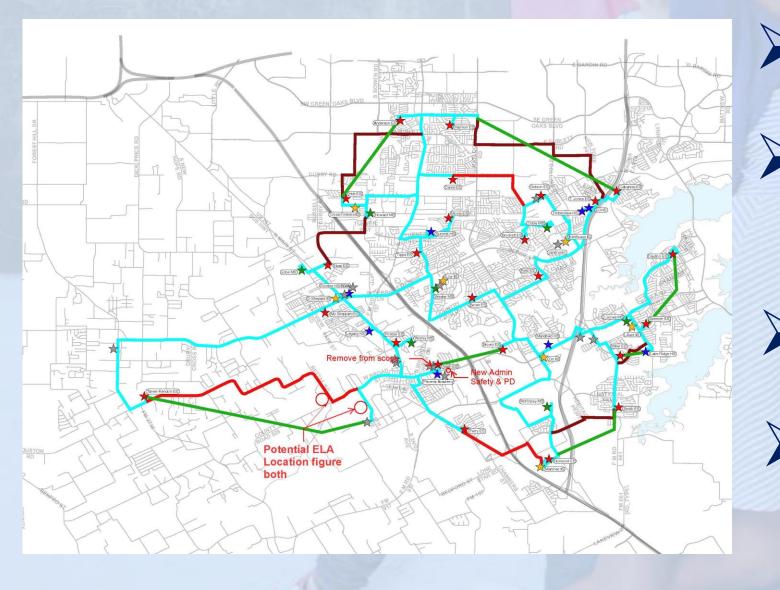

Evaluate Proposals – February 2025 Approve Final Proposal March 2025 **Board Meeting Execute Contract** Substantial Completion September 2025

Technology Infrastructure > Districtwide Phone Upgrade >Hardware Received Configuration underway **Work Complete Wireless Access Points (WAPs) – Aux. Bldgs.** >Network Switches – Aux. Bldgs. **Wireless Access Points (WAPs) – CPA** > Cabling upgrade in progress



Instructional Technology – Prop B



>Interactive Display Panels Installation and training has started



