



Serving Learners, Families, and the Community

CECIL COUNTY PUBLIC SCHOOLS

DIVISION OF ADMINISTRATIVE SERVICES

GEORGE WASHINGTON CARVER EDUCATION LEADERSHIP CENTER
201 BOOTH STREET • ELKTON, MD 21921

phone: 410.996.5034 • fax: 410.996.1082 • www.ccps.org

Jeffrey A. Lawson, Ed.D.
Superintendent of Schools

Diana B. Hawley
President, Board of Education

MEMORANDUM

To: Jeffrey A. Lawson, Ed.D., Superintendent of Schools

From: Theodore Boyer, Ed.D., Executive Director for Administrative Services
Charles C. Simperts, Director of Facilities

Date: February 12, 2025

Re: Construction Progress Report to the Board of Education

North East Middle/High School – Replacement Project

- An award recommendation for the 3rd Party Testing & Inspections services package is being presented to the Board this evening
- Sanitation and storm water pipe installation continues with projected completion mid-April
- Geothermal well site drilling continues with projected completion mid-May
- Building retaining wall footers/wall construction/and waterproofing is ongoing
- Steel has been ordered with an estimated arrival of Mid-April
- Additional survey engineering is needed for reconstruction of Irishtown Rd. in order to accommodate our three (3) new entrances into the site
- *Progress photos attached*

Cecil School of Technology – Chiller Replacement Project

- New concrete pads were poured and chillers have been set
- Pumps are on site
- Installation of unit piping and controls will occur throughout the winter
- *Progress photos attached*

Perryville High School – Field House Project

- Interior underground plumbing is complete, exterior underground plumbing is in process
- Mechanical rough in is in process
- Interior and exterior masonry walls are complete
- Roof work is in process
- *Progress photos attached*

Elk Neck Elementary School – Roof Replacement Project

- Design and documentation are being worked on through the winter
- Project is being advertised February 19, 2025
- An award recommendation is anticipated for the April BOE meeting
- Anticipated project start date of June 16, 2025

Cecilton Elementary School – Boiler Conversion Project

- Project scope is being developed by engineer
- Anticipated bid is mid to late Spring

Rising Sun Elementary School – Parking Lot Pavement Project

- An award recommendation is anticipated for the April BOE meeting
- Anticipated project start date of June 16, 2025







NORTH EAST MIDDLE / HIGH SCHOOL – REPLACEMENT



NORTH EAST MIDDLE / HIGH SCHOOL – REPLACEMENT






CECIL COUNTY SCHOOL OF TECHNOLOGY – CHILLER REPLACEMENT



CECIL COUNTY SCHOOL OF TECHNOLOGY – CHILLER REPLACEMENT

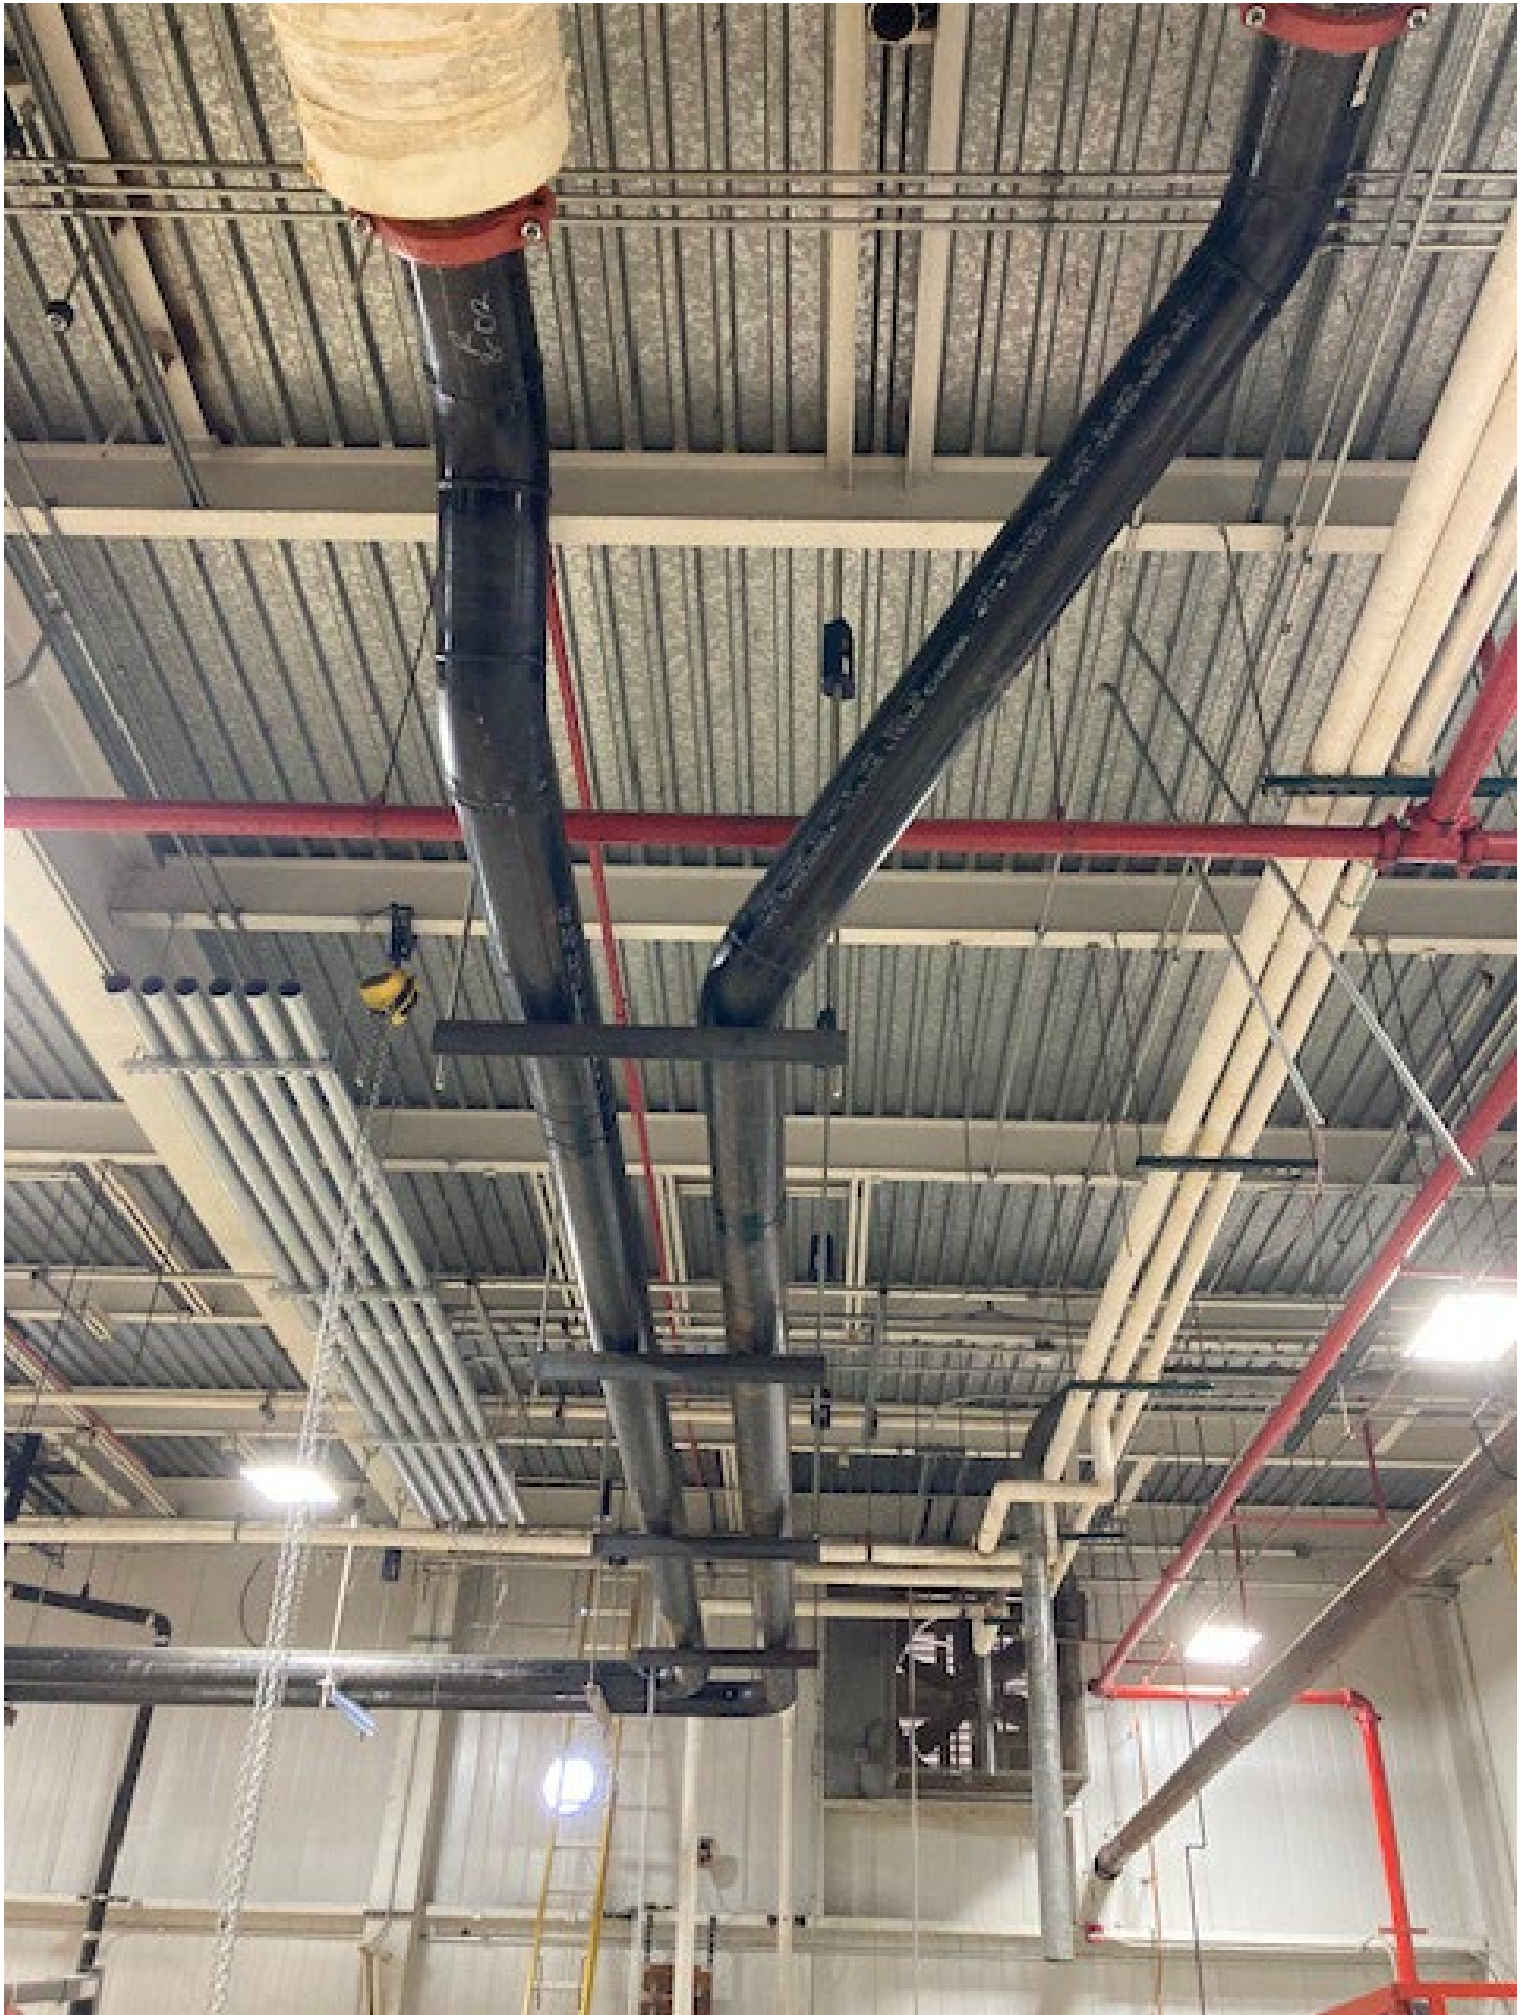



CECIL COUNTY SCHOOL OF TECHNOLOGY – CHILLER REPLACEMENT





PERRYVILLE HIGH SCHOOL – FIELDHOUSE



PERRYVILLE HIGH SCHOOL – FIELDHOUSE



PERRYVILLE HIGH SCHOOL – FIELDHOUSE



PERRYVILLE HIGH SCHOOL – FIELDHOUSE

