




2023 BOND

# MAJOR PROJECTS UPDATE

FEBRUARY 2025



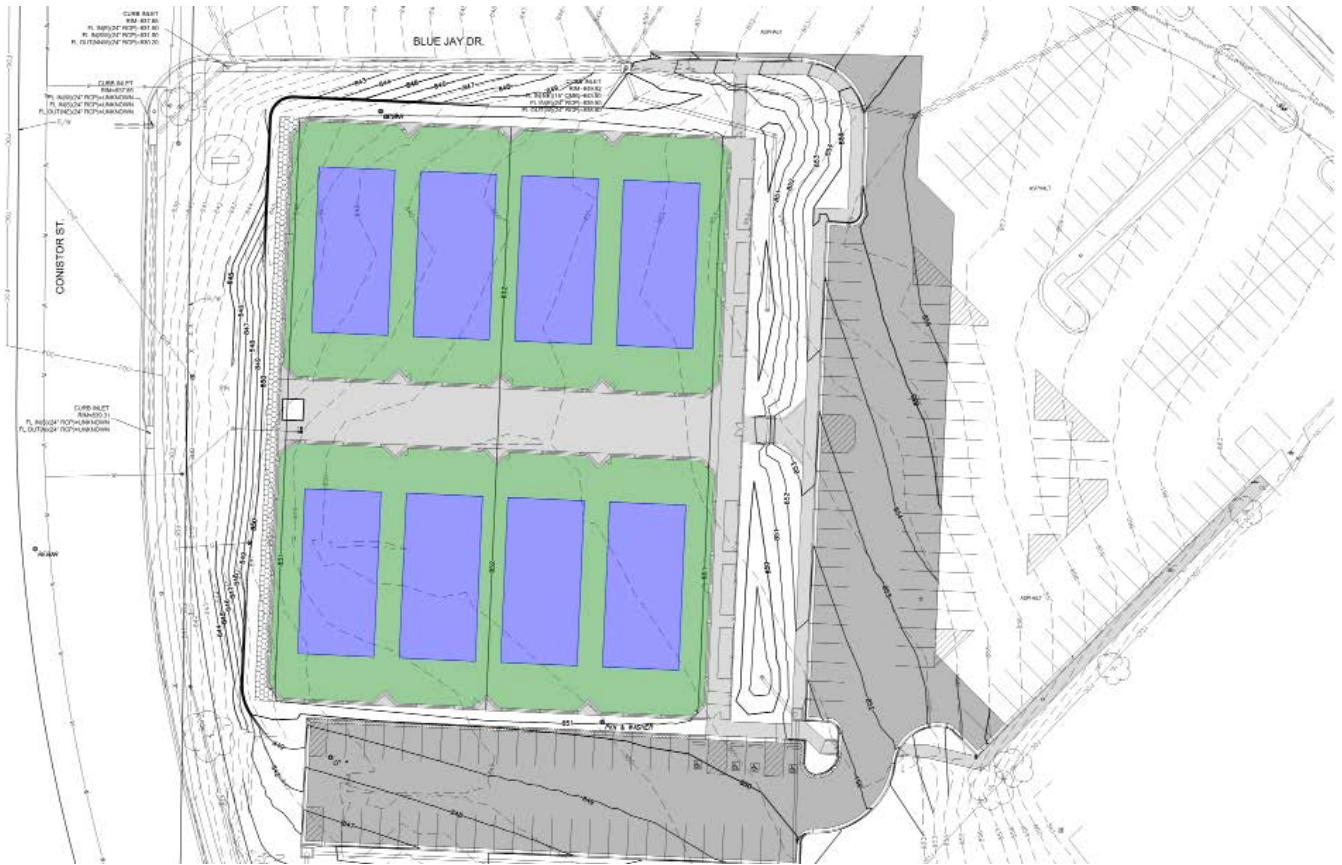

# Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

**Construction Start:** Spring 2023

**Construction Complete:** Fall 2023

**WEEKLY  
PROGRESS  
REPORT**

# Tennis Courts 11/13/2023

Liberty Public Schools



## PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

## UPCOMING


Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest

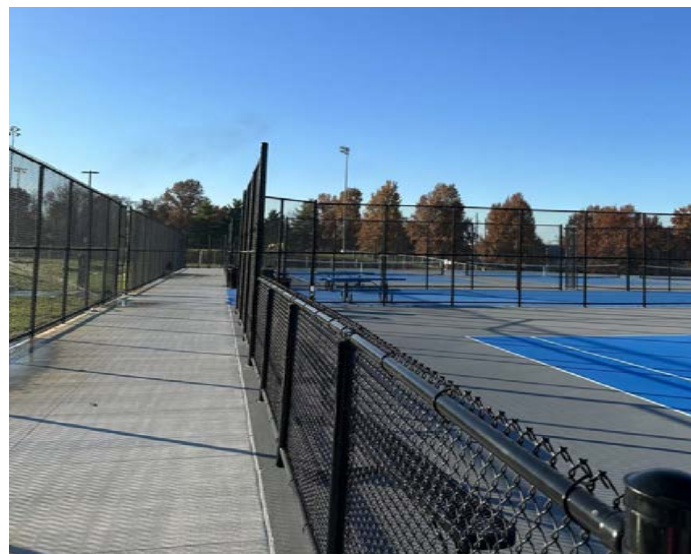

East Concourse Looking South



East Concourse Looking North


# WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

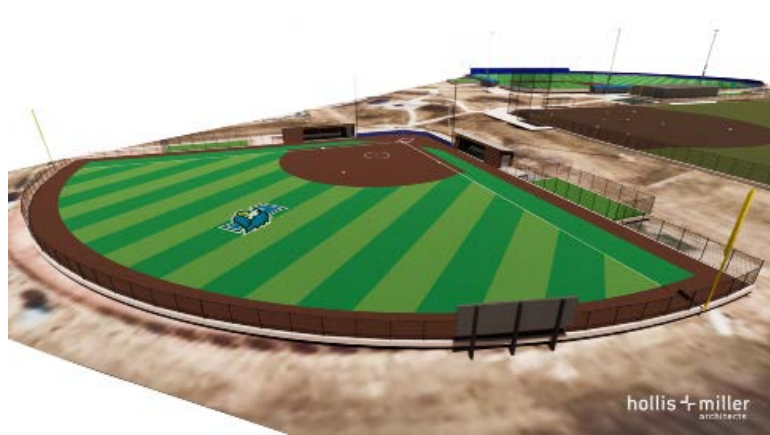

## Liberty High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

### Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024



## Liberty North High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

### Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

WEEKLY  
PROGRESS  
REPORT

# LPS Ball Fields 08/09/2024

Liberty Public Schools



## PROJECT STATUS

### LNHS

- Punch List Completion
- Final Inspection Passed

### LHS

- Punch List Completion
- Retaining Wall Ongoing
- Final Sod Ongoing

## UPCOMING

### LHS

- City Inspection

Project Completion  
Baseball March 2024/Softball May 2024



LHS - Overall Site



LHS - Overall Site



LNHS - Overall Site



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

**WEEKLY  
PROGRESS  
REPORT**

# LED Upgrades 12/11/2023

Liberty Public Schools



## PROJECT STATUS

South Valley MS - Upgrades Complete

Discovery MS - Upgrades Complete

EPiC Elementary - Upgrades Complete

Liberty North High School - Upgrades  
Ongoing

## UPCOMING

Evergy Inspections - All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

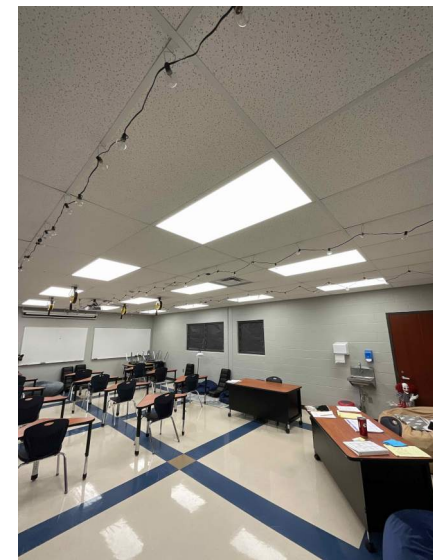

Liberty North HS

**WEEKLY  
PROGRESS  
REPORT**

# LED Upgrades 11/13/2023

Liberty Public Schools



## PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


## UPCOMING

Energy Inspections All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023

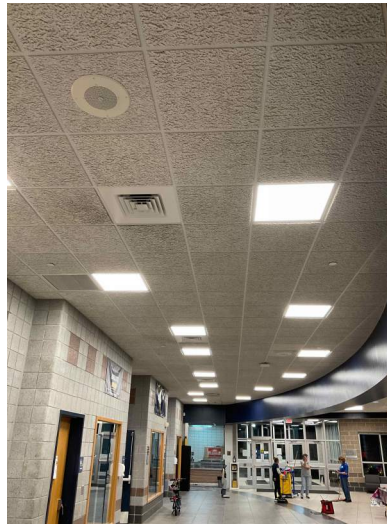


South Valley Middle School

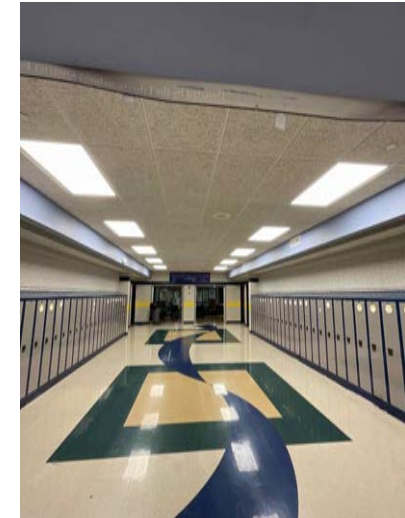

South Valley Middle School



Discovery Middle School

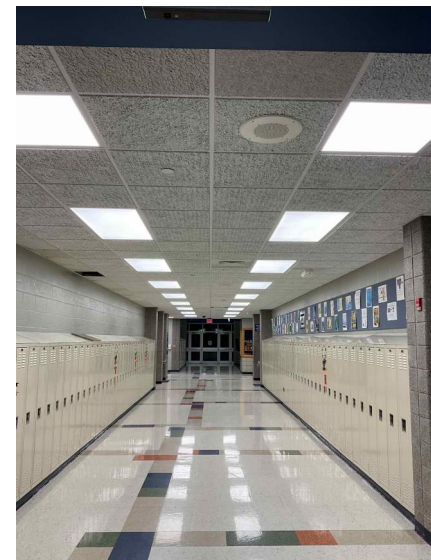

Discovery Middle School

# WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School



## EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

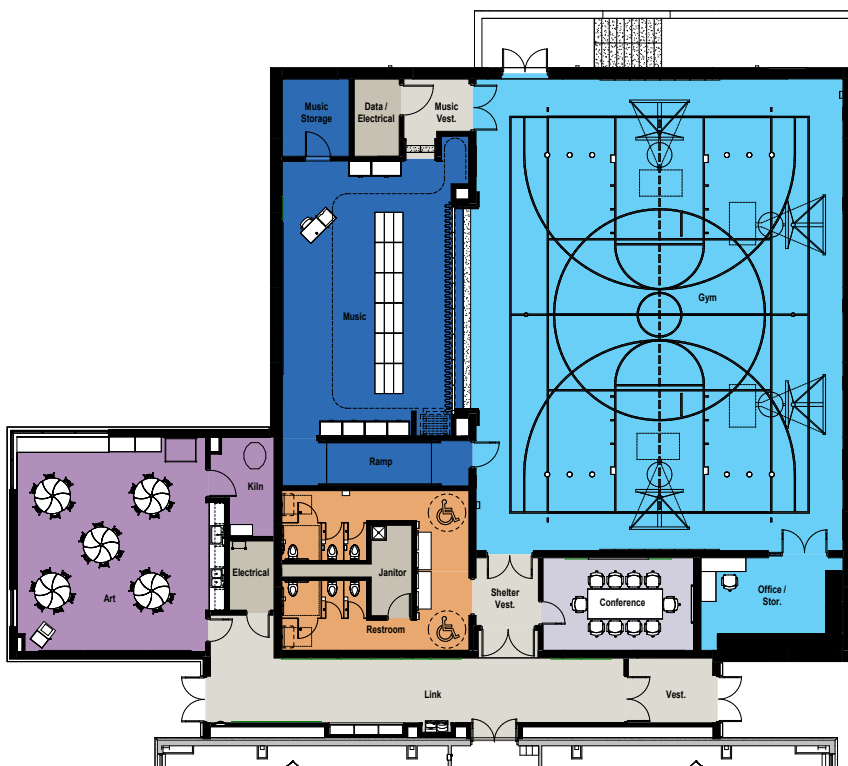

▲ Addition



▲ Renovation Area

WEEKLY  
PROGRESS  
REPORT

# Storm Shelters 02/10/2025

Liberty Public Schools



## PROJECT STATUS

EPiC Elementary

- Carpet done
- Stage wood paneling done
- Fabric Panels done
- Stage curtains installed
- Final Paint complete this week
- Remaining AV Items

## UPCOMING

EPiC Elementary

- Punch Walk
- Final Inspection
- Landscaping once planting season starts

Project Completion  
EPiC February 2025



EPiC Elementary - Gym



EPiC Elementary - Stage



EPiC Elementary - Art Room





EPiC Elementary



## Discovery Middle School

- 11,000 square foot addition
  - ICC 500 rated shelter
  - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
  - Additional storage
- Projected Construction Schedule:  
Spring 2024–Summer 2025

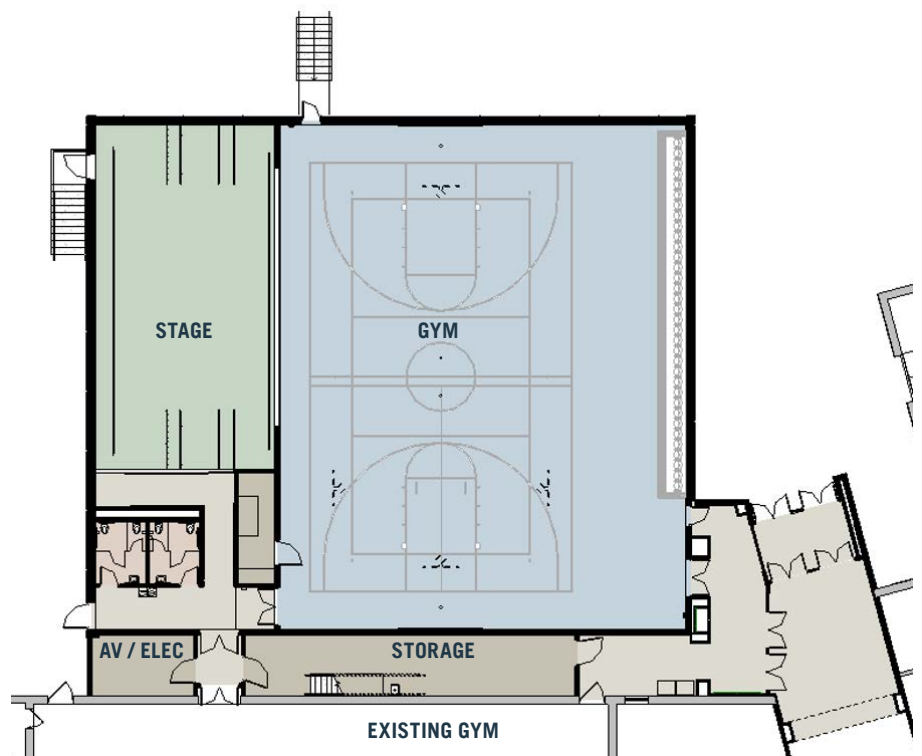

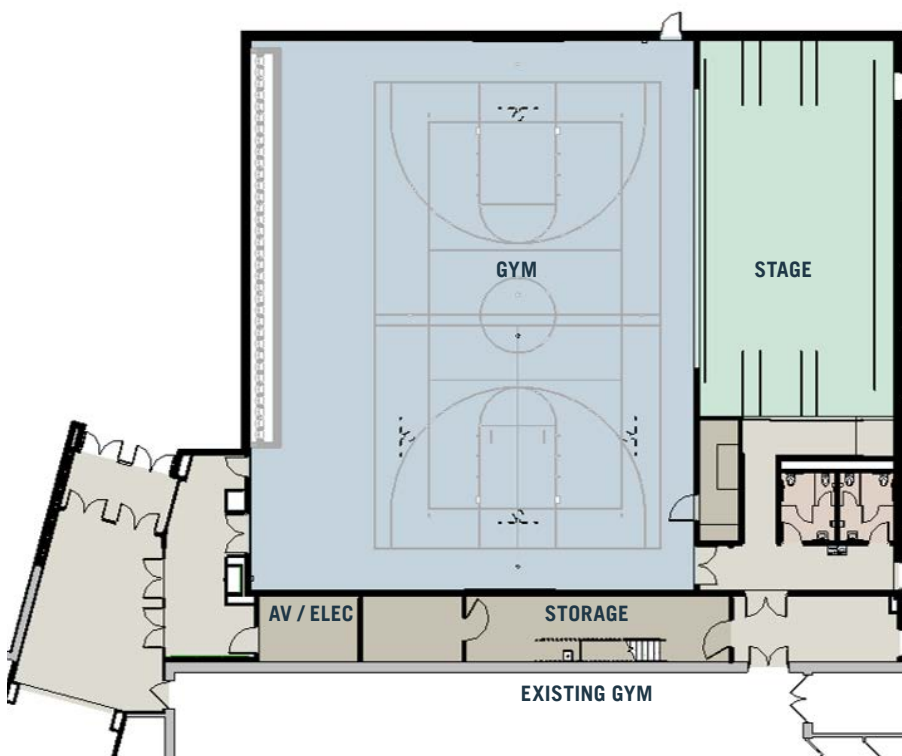

## South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025

WEEKLY  
PROGRESS  
REPORT

# Storm Shelters 02/10/2025

Liberty Public Schools



## PROJECT STATUS

SVMS and DMS

- Drywall ongoing
- MDF board ongoing
- DMS OH MEP rough-in ongoing
- White cap for roofs
- Metal panel install at SVMS

## UPCOMING

SVMS and DMS

- DMS RTU start up
- Tectum
- DMS metal panel
- Tape sand finish drywall


Project Completion  
DMS&SVMS June 2025



SVMS



DMS

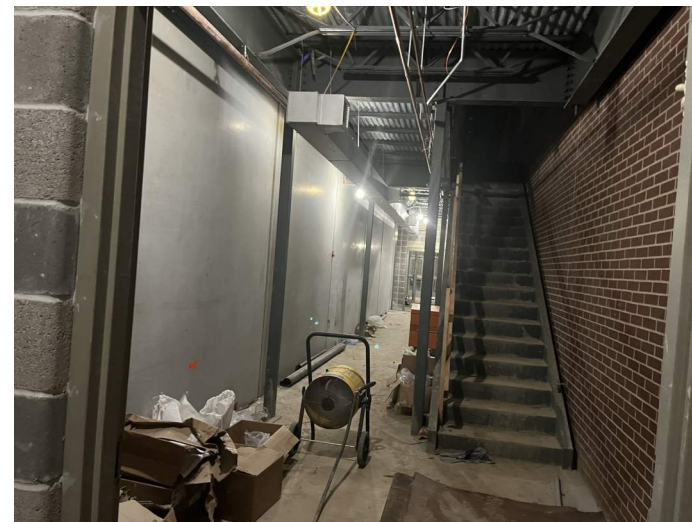

DMS Link



SVMS DMS - Roofing/Dried In



## Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule:  
Fall 2023–Spring 2025



**WEEKLY  
PROGRESS  
REPORT**

# Distribution Center 2/7/25

Liberty Public Schools



**2/7/25**

## PROJECT STATUS

- Interior bollards installed
- Window installation complete
- Dryfall complete
- MEP trim out ongoing
- Paint ongoing
- Freezer detailing ongoing
- Trash enclosure railing complete
- East paving complete


## UPCOMING

- Metal panel rework ongoing
- Punch light poles bases
- Gate and fencing at Eat lot
- Set electrical distribution gear


Project Completion  
June 2025



Warehouse

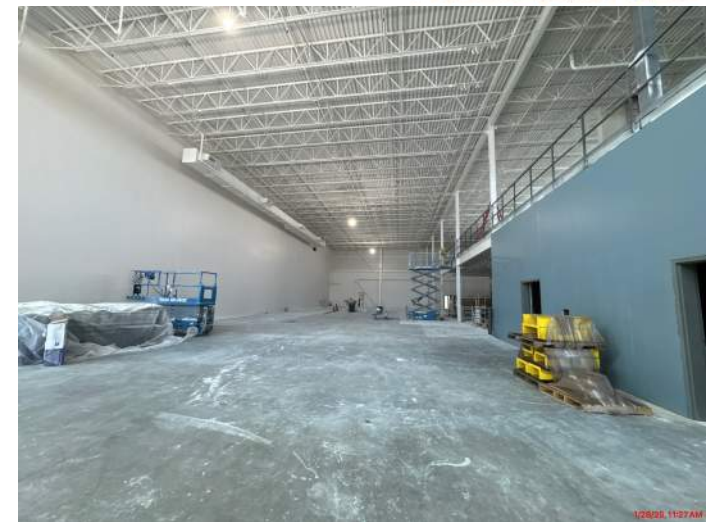

Warehouse

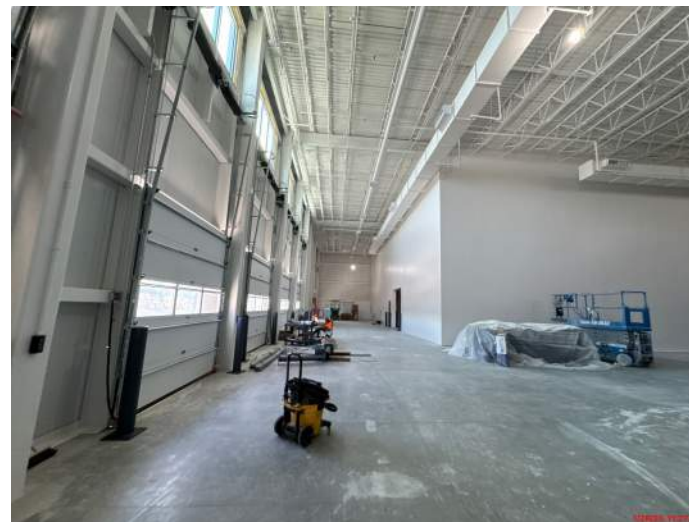

Warehouse



Workstation A105 Area

# WEEKLY PROGRESS REPORT

2/7/25



Bathroom Tile



Freezer/Cooler Door



East lot approach



East Lot paving

Fine Arts  
 Kid's Zone  
 Technology  
 Shared Amenities  
 Building Systems  
 Future Phase



Main Entry

## District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule:  
Fall 2023 - Summer 2024



**WEEKLY  
PROGRESS  
REPORT**

# District Tech Center 7/12/24

Liberty Public Schools



**7/12/24**

## PROJECT STATUS

District Technology Center:

- Completed Communications Install
- Completed Interior Paint
- Completed All Exterior Paint
- Completed Floor Install
- Completed Data Pod Install
- Completed HVAC Equipment Install
- Completed Landscaping/Fence Install
- Completed Generator Install
- Certificate of Occupancy - Received July 9th

## UPCOMING

District Technology Center:

- Complete Punchlist Work
- Complete Furniture Move In
- Server Switchover July 13th
- Staff Move in July 16th

Project Completion July 2024



IT Reception



Exterior



Kid's Zone Open Office



Fine Arts Open Office



Fine Arts Workshop



Restrooms



Breakroom



Data Pod Install

# WEEKLY PROGRESS REPORT

7/12/24



Exterior



Medium Conference Room



Kid's Zone Storage




IT Open Office



## Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
  - Integrated SPED resources
- Renovated cafeteria & scramble
  - Restroom renovations
- Exterior masonry repair & window replacement
  - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

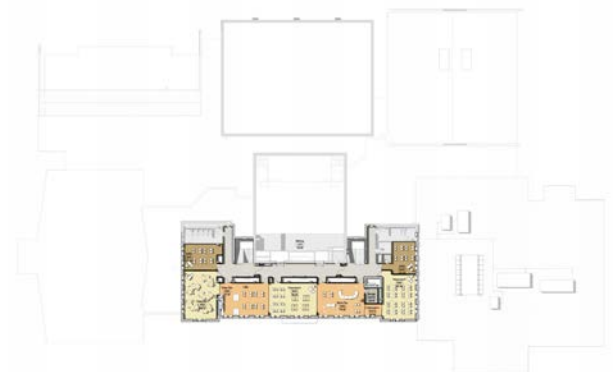

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

**WEEKLY  
PROGRESS  
REPORT**

# Heritage Middle School

Liberty Public Schools



**1/10/25**

## PROJECT STATUS

Heritage Middle School

1964 Wing:

- Completed Floor Install
- Completed MEP Trimout
- Completed Specialty Finish Install
- Completed Owner Move In
- Completed Final Inspections
- Continued Punchlist Work

## UPCOMING

Heritage Middle School

1964 Wing:

- Complete Punchlist Work

Projected Completion: December 2024



1964 (Area A)



1964 (Area A)



1964 (Area A)



1964 (Area A)

# WEEKLY PROGRESS REPORT

1/10/25



1964 (Area A)




1964 (Area A)



1964 (Area A)



1964 (Area A)

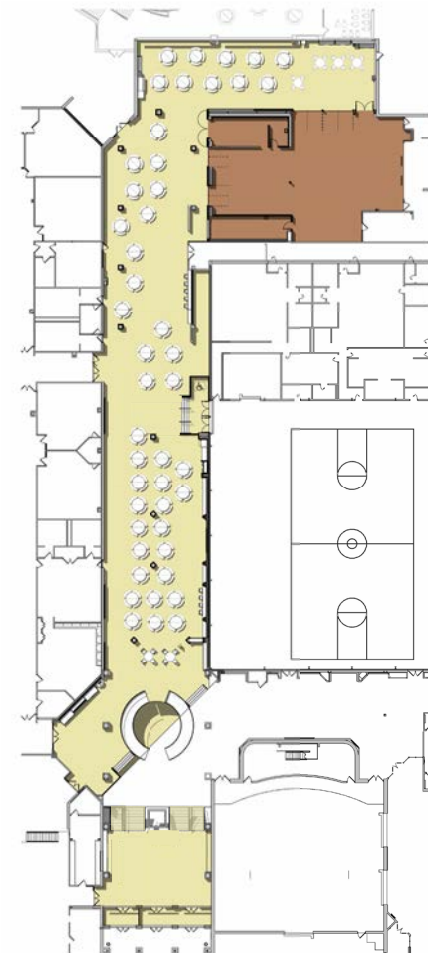

**PHASE 2**

## Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule:  
Summer – Fall 2024 & 2025



**PHASE 1**

WEEKLY  
PROGRESS  
REPORT

# Liberty High School

Liberty Public Schools



1/10/25

## PROJECT STATUS

Liberty High School:

- Continued Punchlist
- Completed Owner Move In
- Completed FACS Room Inspections

## UPCOMING

Liberty High School:

- Complete Punchlist

Project Completion: December 2024



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing

# WEEKLY PROGRESS REPORT

1/10/25



LHS 100's Wing



LHS 100's Wing



LHS 100's Wing




LHS 100's Wing



## Shop Building

- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezeway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

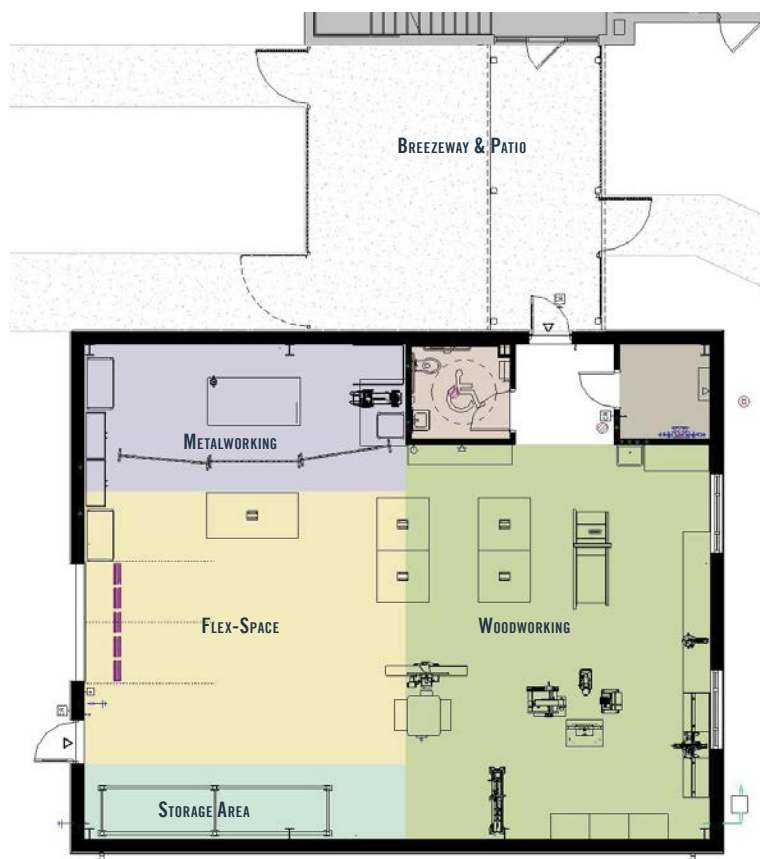

▲ Floor Plan

**WEEKLY  
PROGRESS  
REPORT**

# Academy Shop 2/7/25

Liberty Public Schools



**2/7/25**

## PROJECT STATUS

- IMP complete
- Roofing complete
- Skirt wall framing complete
- Overhead door complete
- MEP rough ongoing

## UPCOMING

- Masonry ongoing
- RTU set
- Drywall
- Plywood walls
- Door frame install
- Paving

Project Completion  
June 2025



PEMB



Overhead Door




Overall Interior




Masonry Wall

## Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:  
Spring 2024–Spring 2025

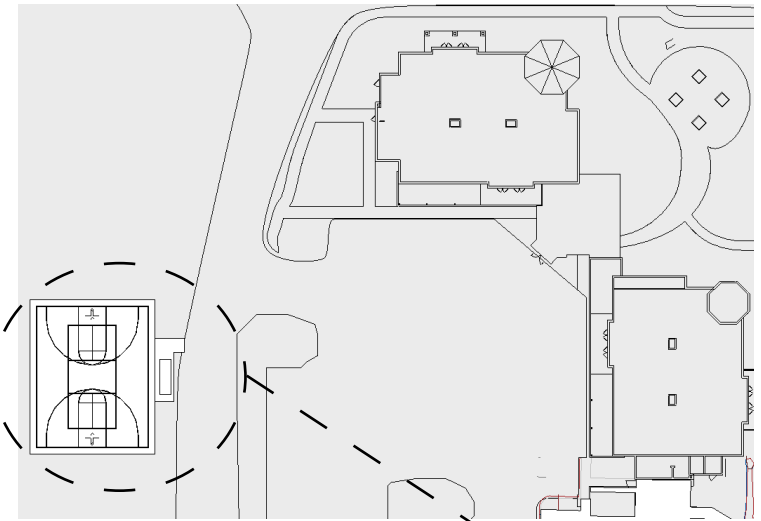

Overall Site Plan

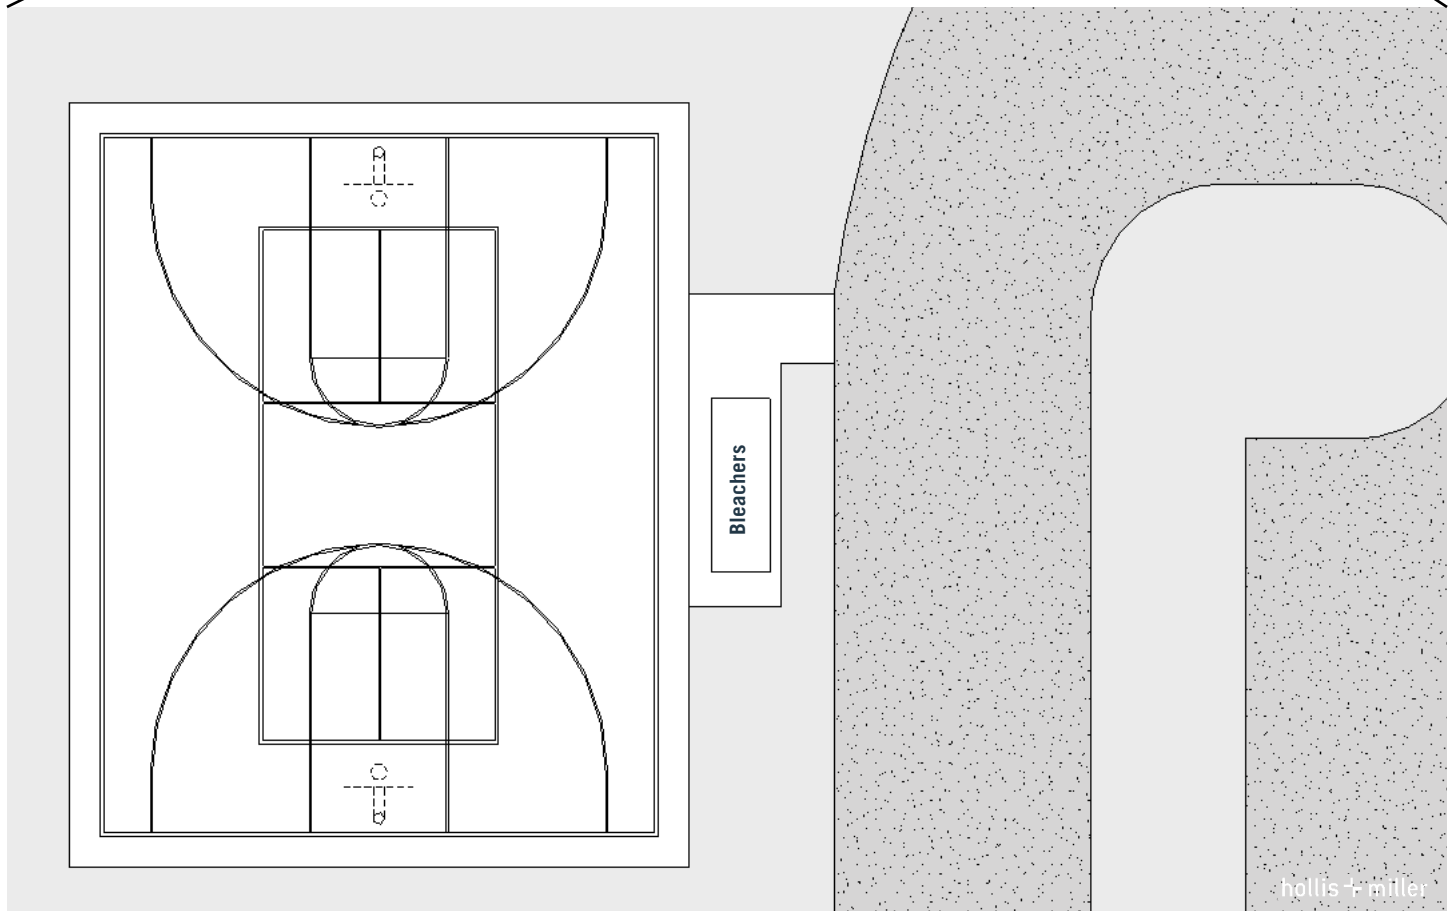

Enlarged Site Plan

## Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:  
May 2024 - August 2025



▲ Enlarged Floor Plan




▲ Overall Floor Plan

## Interior Renovation

- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

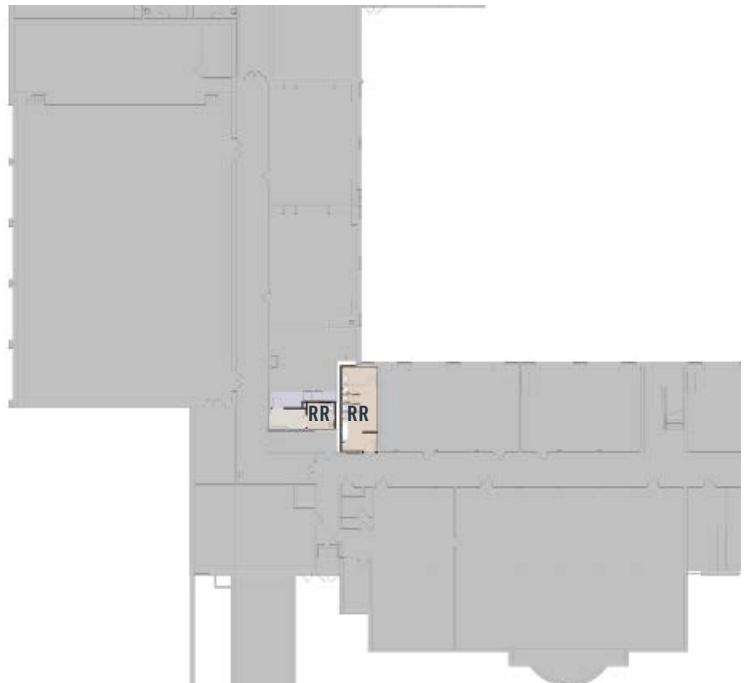

Partial First Level Floor Plan



Overall Second Level Floor Plan

## Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:  
May 2024 - August 2025



Administration



Overall Floor Plan

**WEEKLY  
PROGRESS  
REPORT**

# Doniphan, Franklin, and Ridgeview Summer Renovation Projects

Liberty Public Schools



**8/9/24**

## PROJECT STATUS

Doniphan, Franklin, and Ridgeview:

- Completed MEP Install
- Completed Drywall Install
- Completed Ceiling Grid Install
- Completed Paint
- Completed Tile
- Completed Casework Install
- Completed Flooring Install
- Completed Epoxy Install
- Completed Specialties Install
- Began Punch List Work

## UPCOMING


Doniphan, Franklin, and Ridgeview:

- Complete Punch List Work
- Complete Final Inspections
- Furniture Move-In

Project Completion: August 2024



Franklin - Main Office

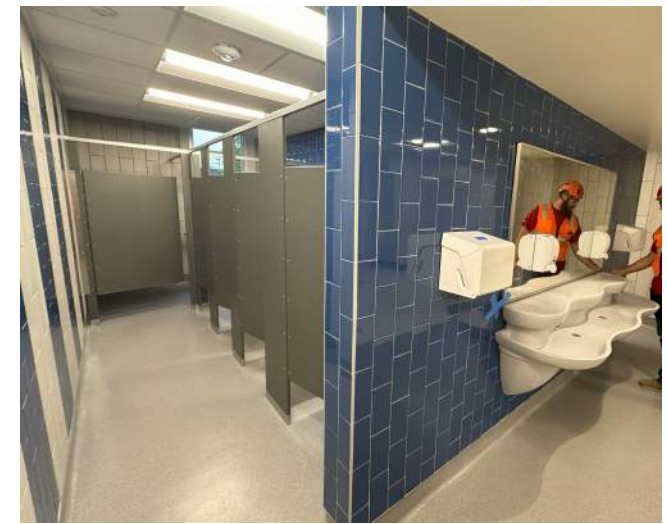

Franklin - Restrooms



Franklin - Workroom



Ridgeview - Level 2 Restroom

# WEEKLY PROGRESS REPORT

8/9/24



Ridgeview - Main Office



Doniphan - Main Office



Doniphan - Assistant Principal Office



Doniphan - Teacher's Lounge



## Liberty Middle School - Track & Field

- 6-lane track
- 195' x 360' natural turf soccer field
- Field events including high jump, long jump, shot put, and discus
- Updated lighting
- Concessions and restroom refresh
- New onsite storage



## Playground Upgrades - Locations

- EPiC Elementary School
- Alexander Doniphan Elementary School
- Lillian Schumacher Elementary School
- Manor Hill Elementary School
- Ridgeview Elementary School
- Lewis & Clark Elementary School
- Liberty Oaks Elementary School
- Shoal Creek Elementary School
- Franklin Elementary School
- Warren Hills Elementary School
- Kellybrook Elementary School
- Early Childhood Center
