




New Construction

PROGRESS UPDATE
January 2025

Fairport Harbor New Pre K-12 School



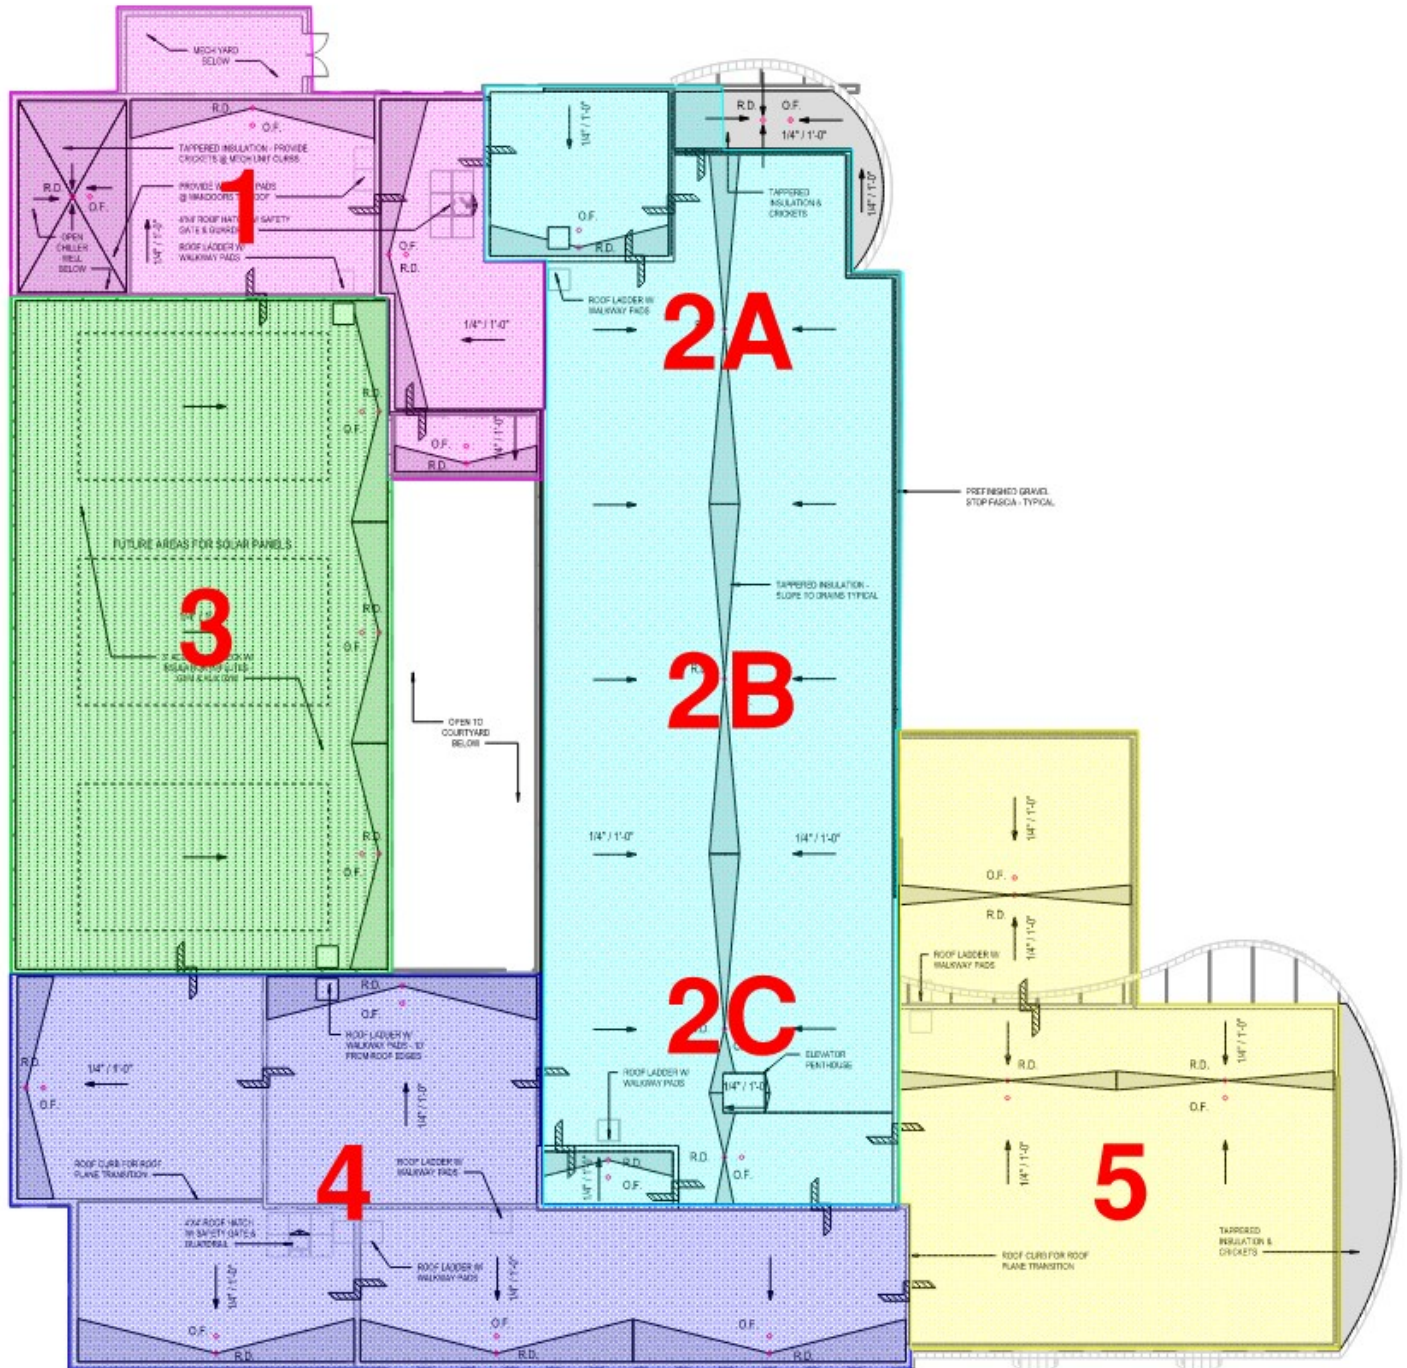

PROJECT SUMMARY

Phase 1


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

January 2025 Progress


- Sprinkler Line—Complete
- Duct and Pipe Insulation—Complete
- Framing Ceilings—Complete
- Building Locker Bench Bases—In Progress

Upcoming Progress

- Hanging Drywall Ceiling in Locker Rooms and Bathrooms

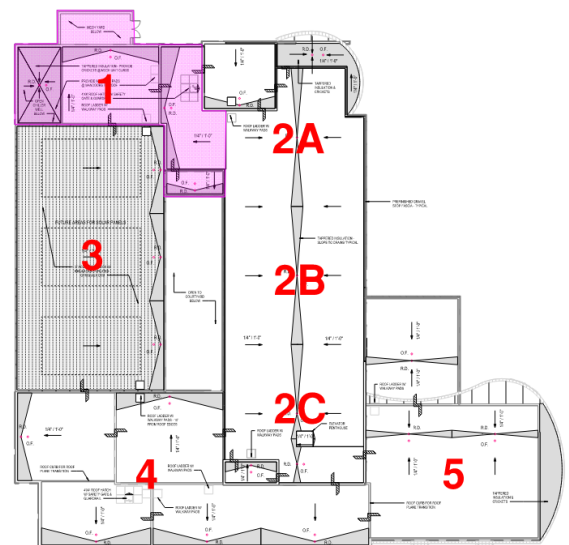

PROJECT SUMMARY

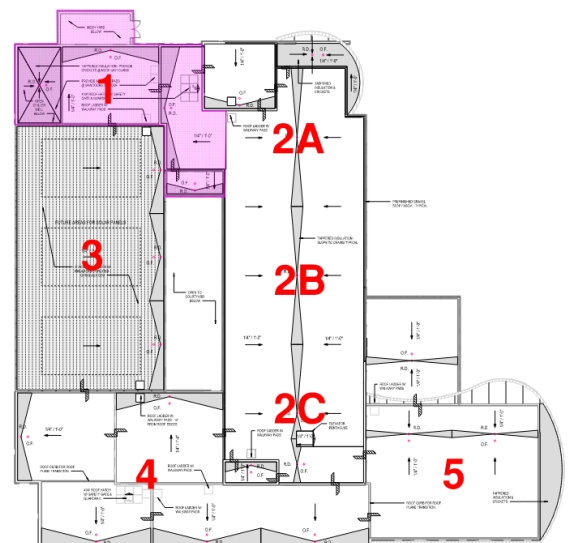

PROJECT SUMMARY

Phase 2


- **Educational Classrooms**

January 2025 Progress


- Masonry Bearing for Roof—Complete
- Overhead Plumbing Rough In—In Progress
- Overhead Electrical Rough In—In Progress
- Roof Joist and Deck in 2C—In Progress
- Hanging Drywall 1st and 2nd Floors—In Progress
- Framing Soffits and Ceilings on 2nd Floor—In Progress
- Pulling Fire Alarm Wires on 2nd Floor—In Progress
- Stair Tower 1—In progress
- Veneer in 2C—In Progress

Upcoming Progress

- In wall Rough In's 3rd Floor
- Non Bearing Walls 3rd Floor
- Veneer in 2B
- Roof Membrane
- Sprinkler Piping on 2nd Floor

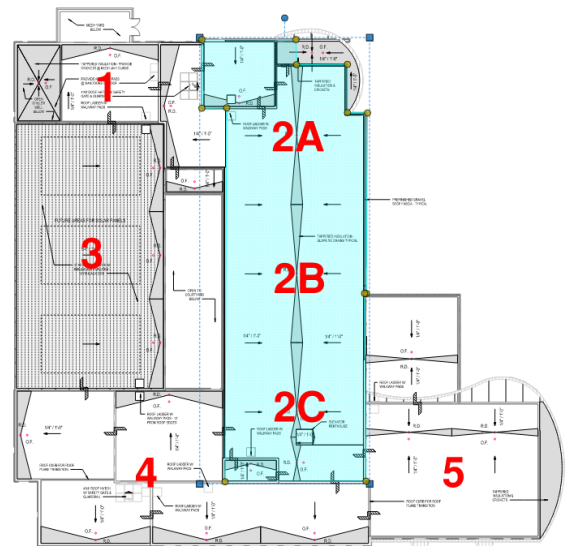

PROJECT SUMMARY

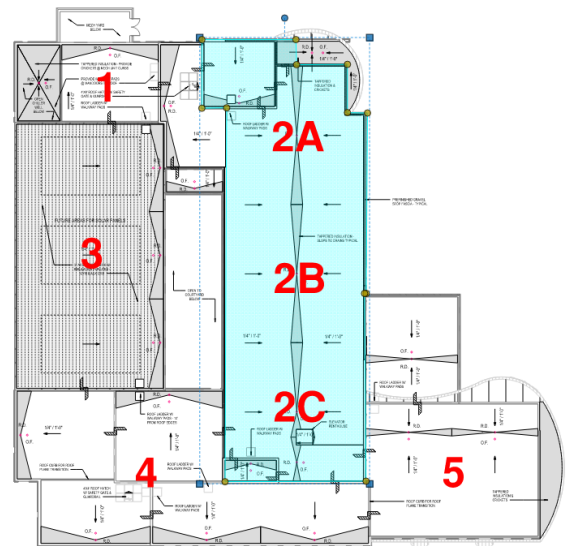

PROJECT SUMMARY

Phase 3


- Auxiliary GYM
- Gymnasium

January 2025 Progress


- Roof Membrane—Complete
- Slab on Grade Main GYM—Complete
- Overhead Mechanical—Complete
- Sprinkler Piping—In Progress
- Overhead Electrical—In Progress

Upcoming Progress

- Overhead Technology Rough-Ins
- Framing Top of Demising Wall

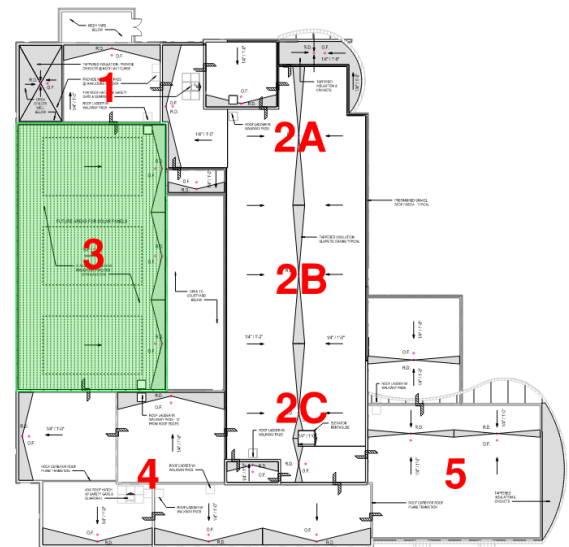

PROJECT SUMMARY

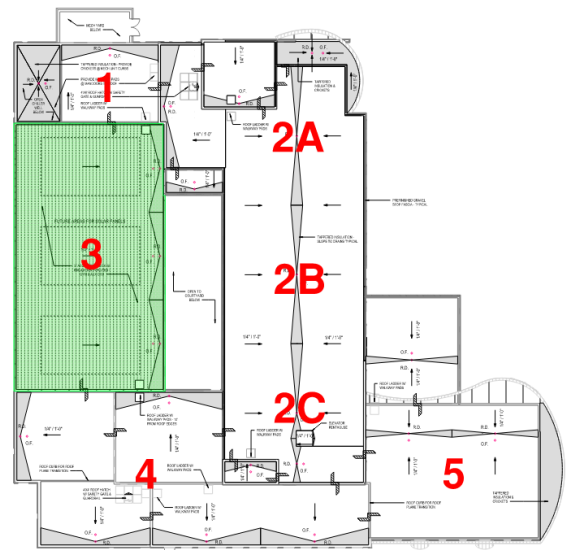

PROJECT SUMMARY

Phase 4 (West Half)


- Kitchen
- Locker Room

January 2025 Progress

- Underground Electrical—Complete
- Slab On Grade—Complete
- Masonry to Bearing—In Progress

Upcoming Progress

- In Wall Electrical Rough In
- In Wall Plumbing Rough In
- Joist and Decking

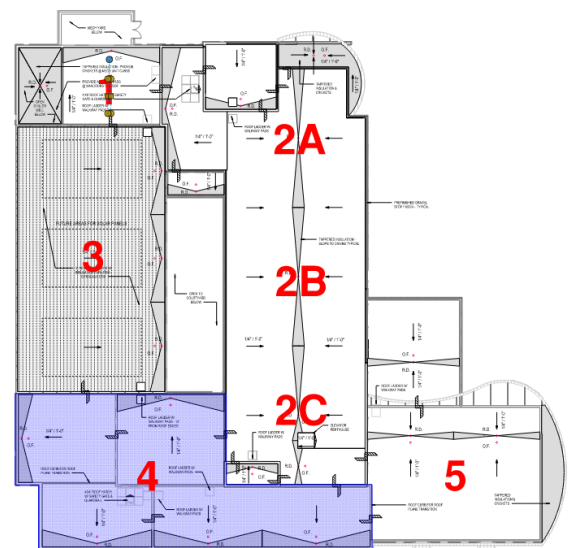

PROJECT SUMMARY

