FEBRUARY 26, 2025

UPDATE
NORTH SPRINGS HIGH SCHOOL

NOEL MALOOF
CHIEF OPERATIONS OFFICER
CAPITAL PROGRAMS TEAM






#### **Current Status**

- Update
- Design Status
- Site Work Status
- Next Milestone





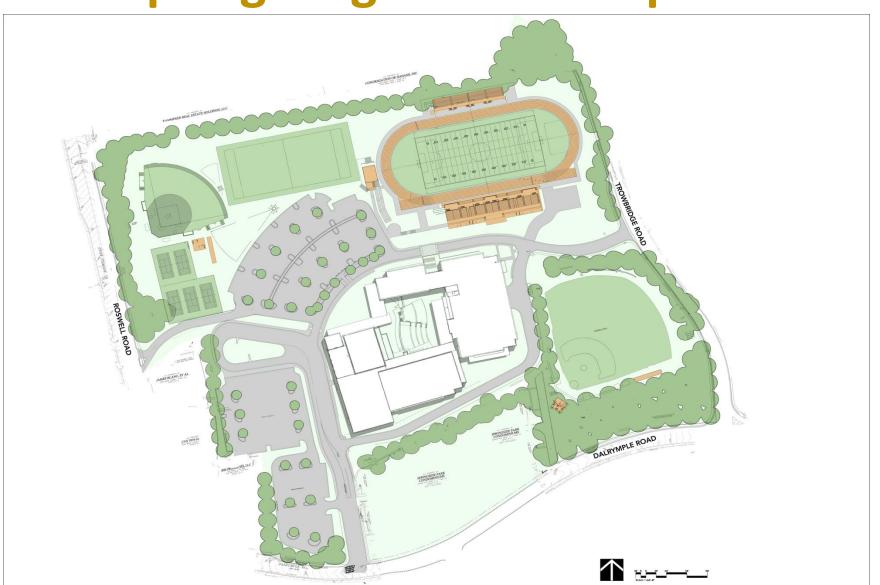

Future Site Plan





Rendering: Northwest aerial view





Rendering: Northeast aerial view





Stadium






Auditorium



Auditorium Lobby



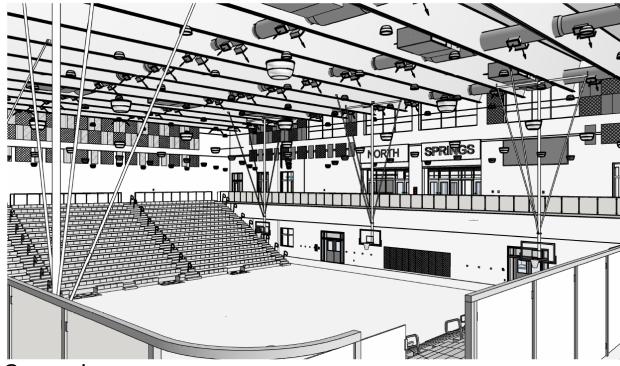

Gymnasium



**Gym Lobby** 

2



### Site Work (Phase 1 Status)

- Underground Detention Storage is installed
- Retaining walls are installed
- Underground utilities (Storm/Sanitary/Water) will soon be complete
- Final grading and building pad placement are being impacted due to cold & rainy weather
- Work is on track for completion in April (a month before Phase 2 is scheduled to start)

# County Schools Where Students Come First

#### **Site Work in Progress**















#### **Weather Impact on Site Work Progress**












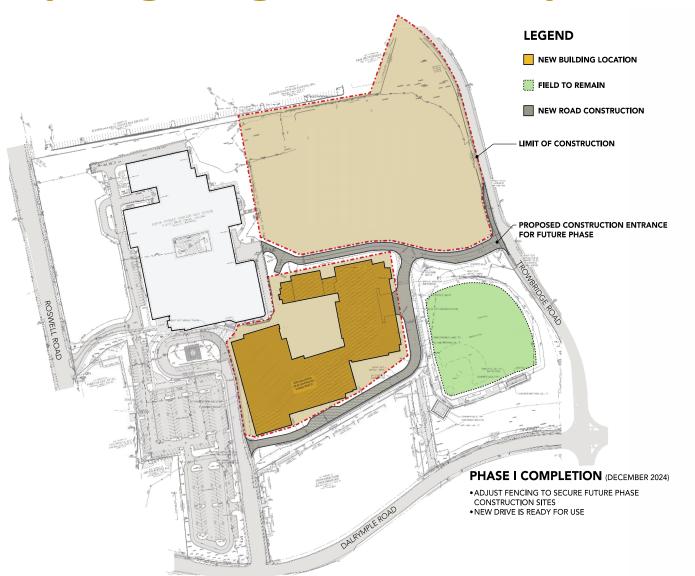

Phase I Completion



### **Phase 2 Site logistics**

- School access will remain via Dalrymple Road and Roswell Road
- Construction access will be via Trowbridge Road
- Baseball field will be back online January 2026
  - Students access will be via a protected walkway adjacent to the soil-nail wall
  - ADA access (drop-off/pick-up) will be via Trowbridge Road
- Contractor will not be allowed to use school parking



### **Additional Scope Discussion**

- Athletic Facilities enhancements by boosters
  - Enhance stadium scoreboard is an alternate in bid documents
  - Baseball batting cages foundation sized to accommodate a future light frame roof structure
  - New sponsor sign(s) at baseball field
  - A future locker room at Softball Field would have to be a separate project





#### **Milestones**

- Site Package (phase 1) construction is schedule to be completed in April
- Building package (phase 2) was advertised for bid on February 14<sup>th</sup>
- Building package (phase 2) contractor is expected to be awarded at April board
- Building package (phase 2) contractor is expected to be on site by June
