School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 02/28/2025

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Elevator Install
- Exterior Metal Wall Panels
- Exterior Site Work
- Painting Ceiling in Commons
- Second Floor Casework
- Interior/Exterior Storefront Install

2 WEEK LOOK AHEAD

- Gym Equipment Install
- Paint Commons
- First Floor Carpet Install
- Prep Area B Topping Slab
- Epoxy Flooring/Walls in Kitchen
- Wall Tile in Gym Bathrooms












BUILDINGTHEFUTURE. JEDUNN. COM



Epoxy Floor in Bathrooms





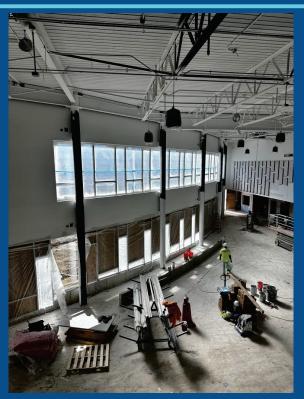

Commons Painting Progress

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.







School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 01/31/2025

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- Gym Wall Tectum Panels Install
- Second Floor Painting in Classrooms
- Exterior Concrete Entrances
- Bathroom Tile Install
- Drywall Complete
- First Floor Casework Install

2 WEEK LOOK AHEAD

- MEP in Ceiling Grid
- Second Floor Casework Install
- Exterior Radius Storefront
- Grand Stair Concrete
- Exterior Metal Wall Panels









Gym Wall Tectum Panels



BUILDINGTHEFUTURE.JEDUNN.COM



First Floor Classroom Casework







First Floor Bathroom Tile

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



First Floor Commons Soffit Install





School

6301 W 78th St. Shawnee Mission KS, 66204

CONSTRUCTION UPDATE 01/17/2025

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- First floor drywall Finishing
- Second Floor Drywall Finishing
- First Floor Light Fixture Install
- Ceiling Grid Install
- MEP In-Grid Install


2 WEEK LOOK AHEAD

- Drywall Complete Commons/Kitchen
- First Floor Ceiling and Wall Paint
- Second Floor Painting in Classrooms
- Exterior Radius Storefront
- Exterior Concrete Entrances







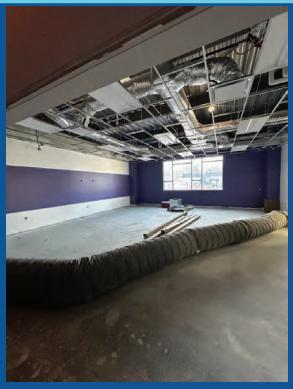

First Floor Painting





First Floor Painting







Media Center Drywall Finished

SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.



Grand Stair Install





School

6301 W 78th St. Shawnee Mission KS. 66204

CONSTRUCTION UPDATE 1/03/2025

OWNER: Shawnee Mission School

District

ARCHITECT: DLR Group

CM: JE DUNN

CURRENT PROGRESS

- First Floor Painting
- Admin Area Drywall Finishing
- Specialty Kitchen Appliance MEP Rough-In
- Second Floor Drywall Finishing
- HVAC Unit Commissioning
- Interior Storefront Install

2 WEEK LOOK AHEAD

- Begin Painting on Second Floor
- Ceiling Grid Install on First Floor
- Turn on Permanent HVAC Units
- Exterior Storefront Completion
- Grand Stair Install









Commons Area Progress



BUILDINGTHEFUTURE.JEDUNN.COM



First Floor Paint Progress








Second Floor Drywall Progress


SAFETY EVERYONE. EVERYWHERE. ALL THE TIME.

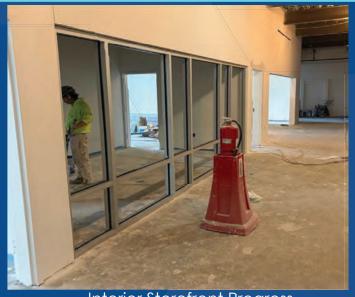



Interior Storefront Progress







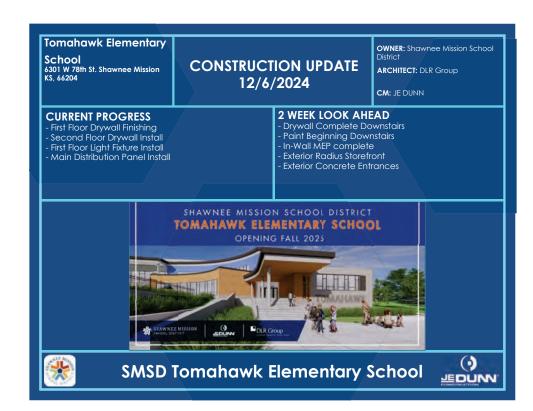


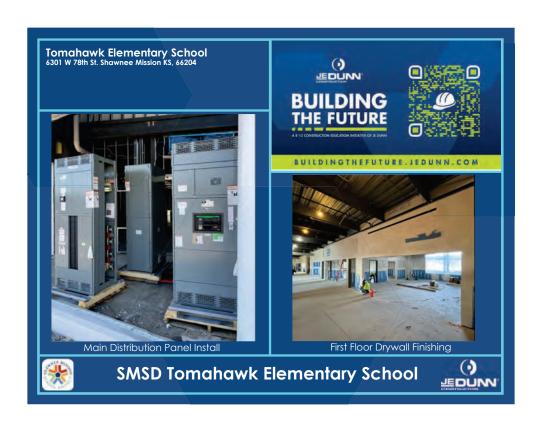


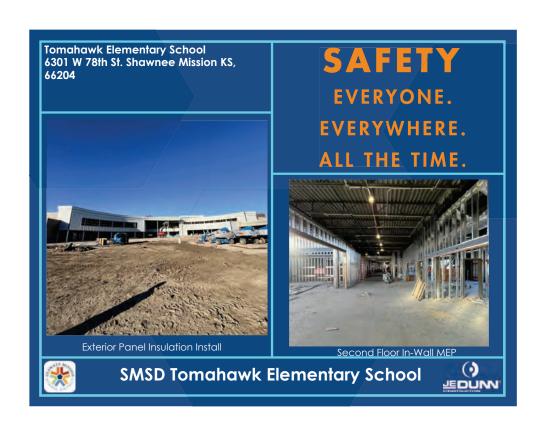


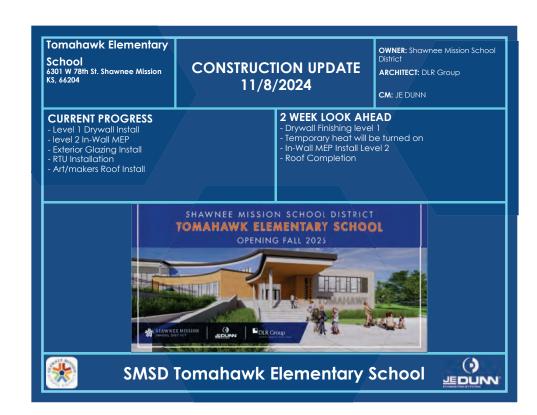


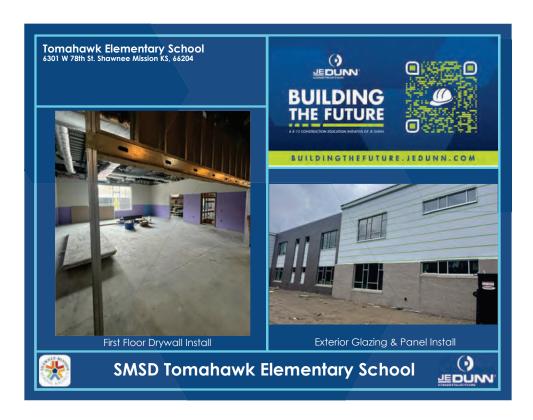

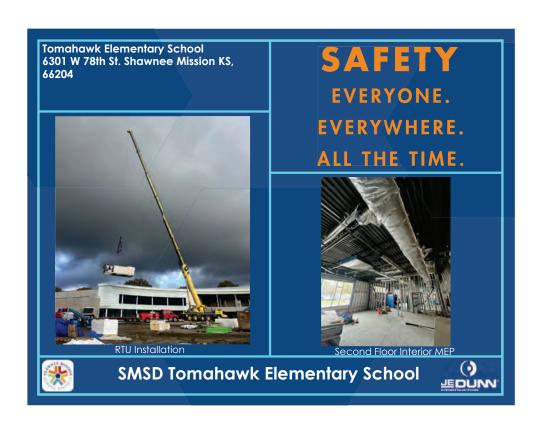


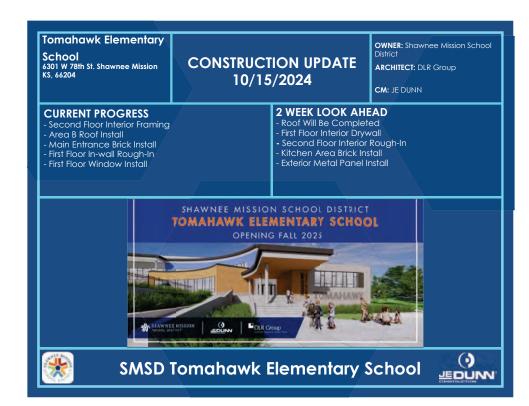


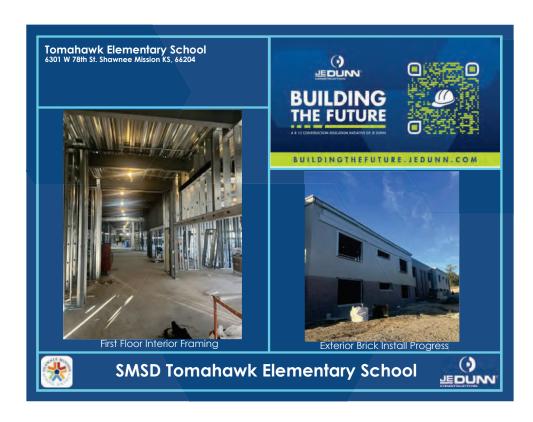

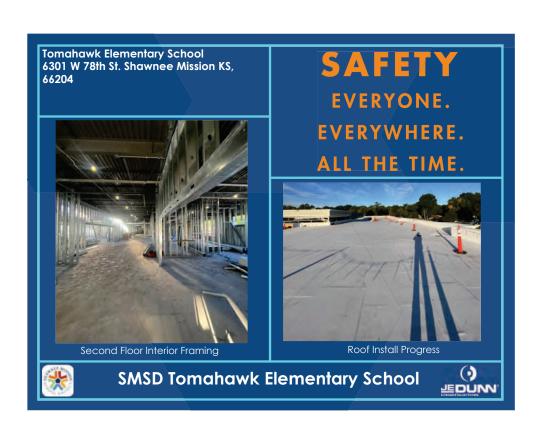





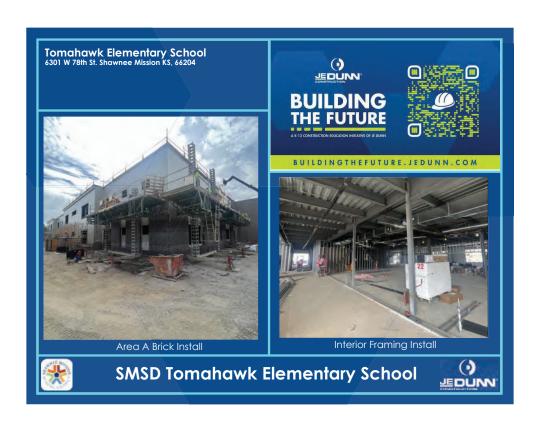


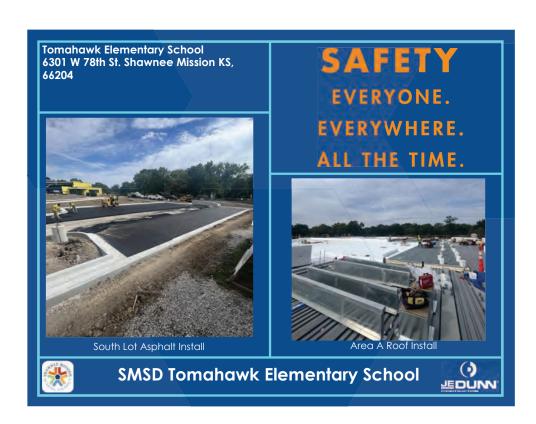





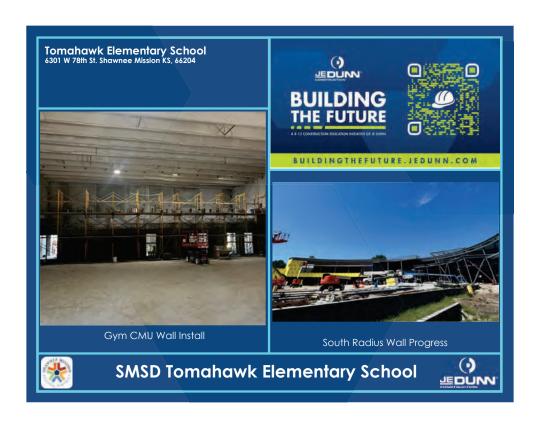


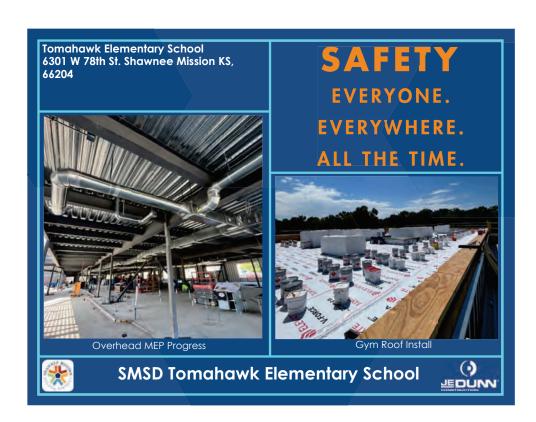


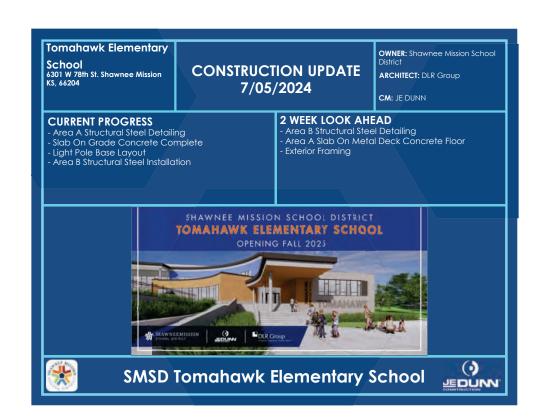


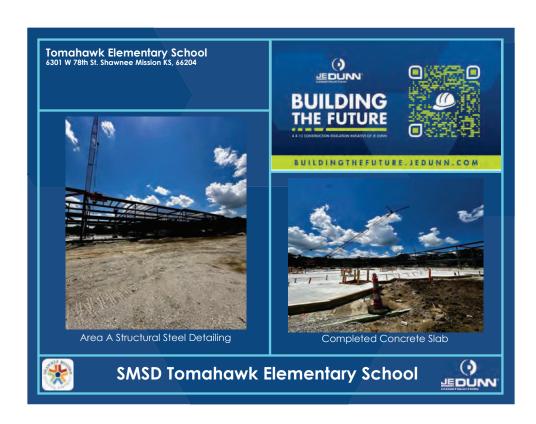


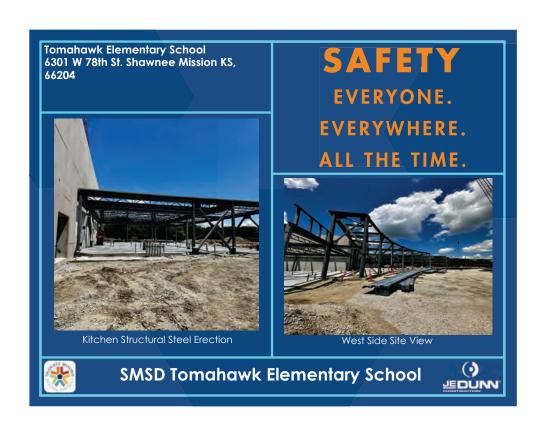


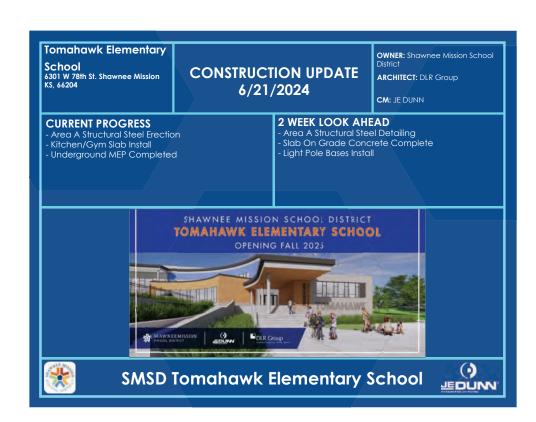


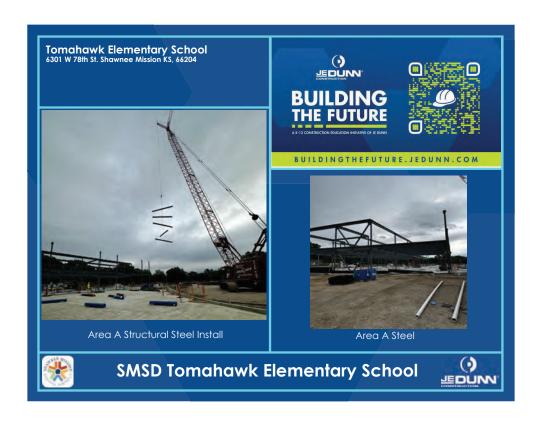


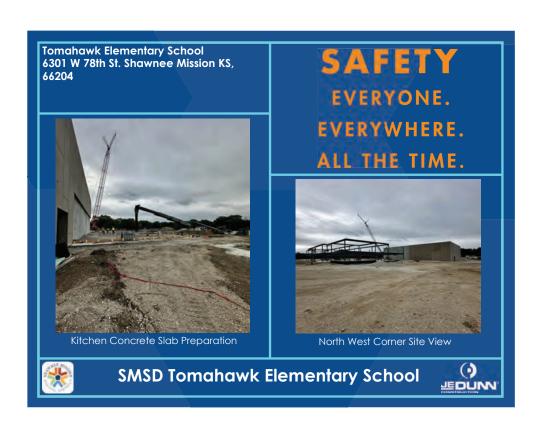


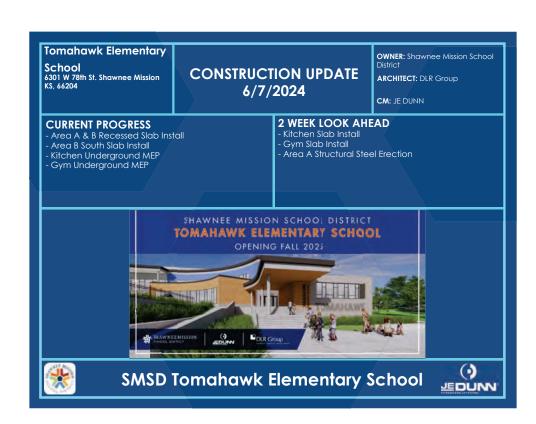


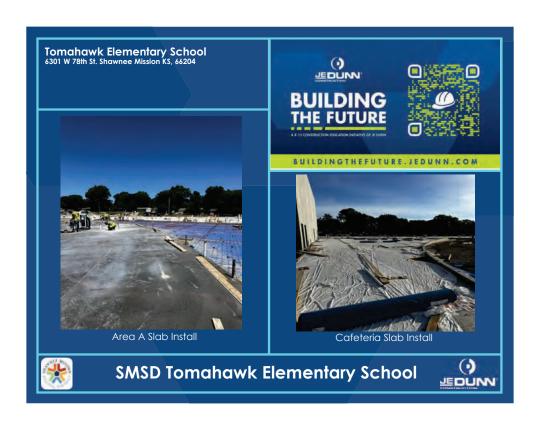


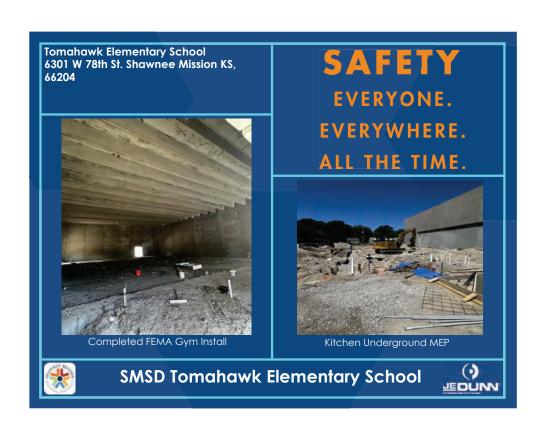


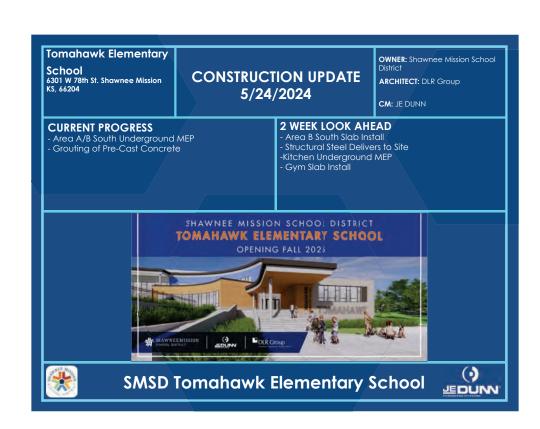


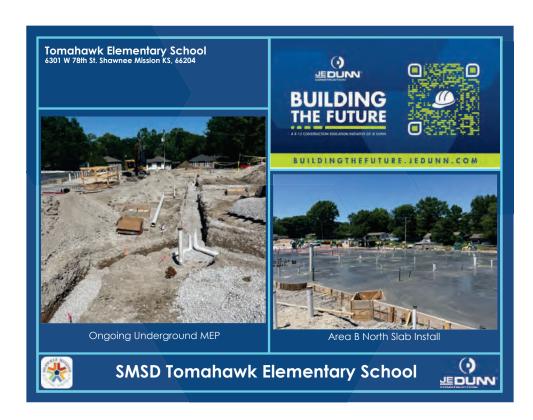

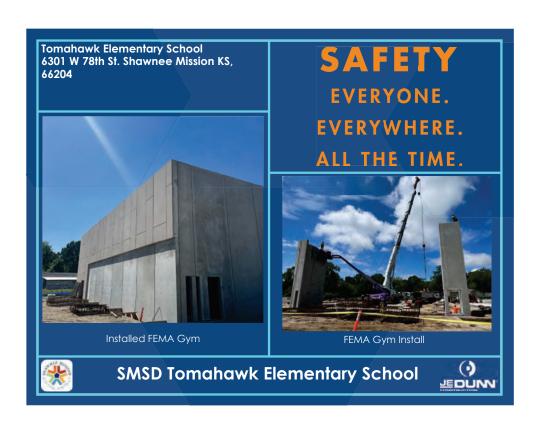


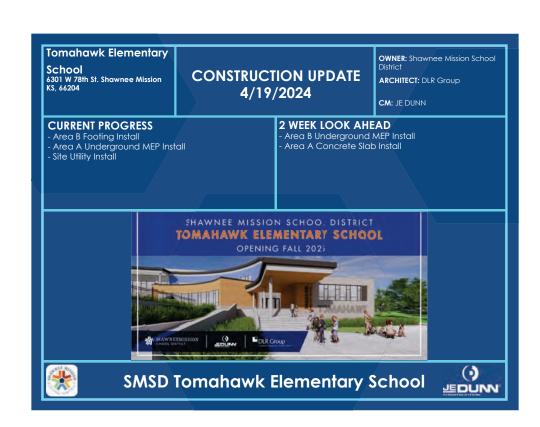


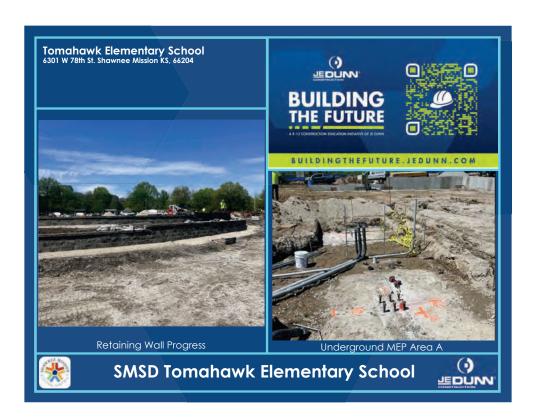

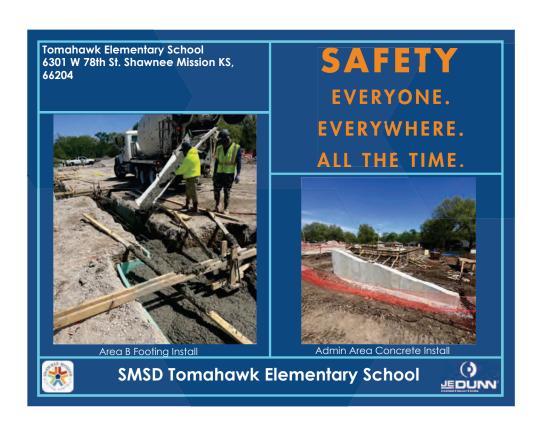



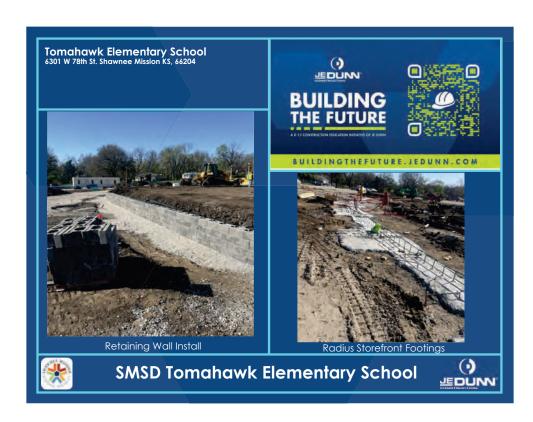

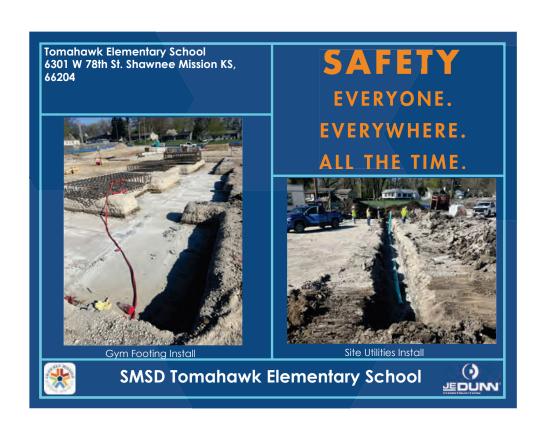



Site Plan LAMAR AVENUE Site Plan LAMAR AVENUE SIMPLY MISSING BURNER LAMAR AVENUE SIMPLY MISSING BURNER DESPRESS LAMAR AVENUE SIMPLY MISS LAMAR AVENUE LAMAR A

Tomahawk Elementary School Floor Plan: Level 01



Tomahawk Elementary School Floor Plan: Level 02









