

BOND CONSTRUCTION UPDATE

January 2025

#ThankYouVoters

2019 - \$295 M BOND



2019 BOND SUMMARY

- New Large-Capacity High School - COMPLETE
- Waller Junior High Addition & Renovation - COMPLETE
- Renovate WHS to Schultz Junior High - COMPLETE
- Renovate SJH to Holleman Elementary - COMPLETE
- Land, Buses, Technology, Security - COMPLETE
- Stadium LED lighting Upgrade - COMPLETE
- Stadium Video Board & Sound System - COMPLETE
- * Stadium Replacement Turf - March-May 2025
- * Stadium HVAC Upgrades - Summer 2025

2022 - \$363 M BOND



- Lowe Elementary (#6) - COMPLETE
- McReavy Elementary (#7) - COMPLETE
- Cure Elementary (#8) - Opening Summer 2025
- Smith Andrews Ag Science Complex - COMPLETE, Opening Feb 2025
- Education Service Center and Transportation - Opening summer-fall 2025
- Priority 1 District Facility Upgrades - In progress, Complete in fall 2025.
- District HVAC upgrades - completing design for summer 2025 work.

LOWE AND MCREAVY ELEMENTARY SCHOOLS



- Both campuses opened in August 2024.
- Punch List work is ongoing and close to completion.
- HVAC test & balance and Building Commissioning are nearing completion.
- Interior graphics package is in production.

SMITH ANDREWS AG SCIENCE COMPLEX




- Punch list is being completed.
- Furniture and equipment has been installed.
- Animal paneling has been installed.
- Final walkthroughs are being conducted.
- City of Waller has issued TCO.

Ag Barn




Front Elevation

Ag Barn

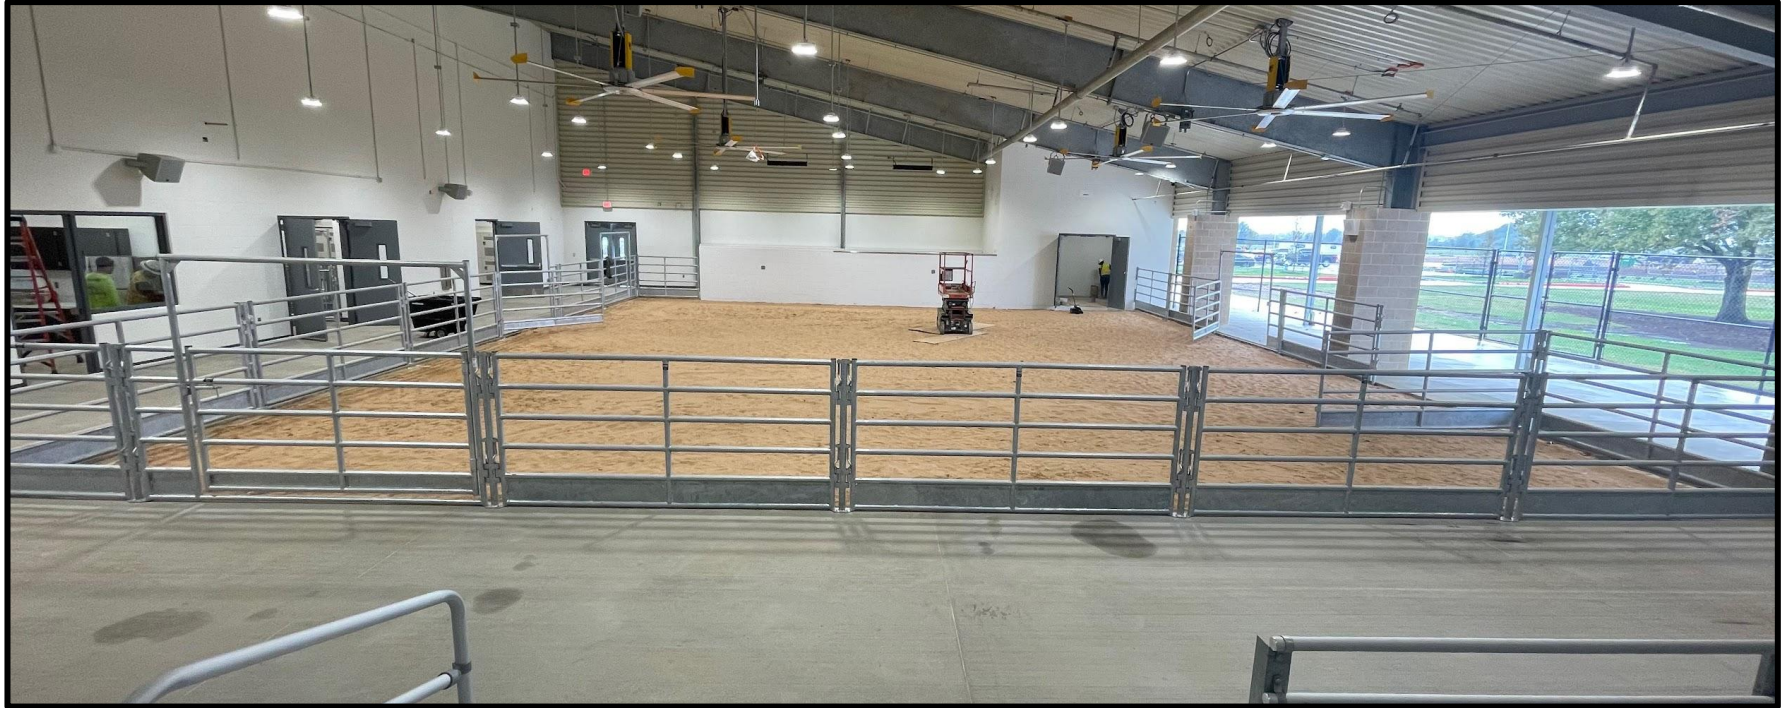

Show Arena

Ag Barn

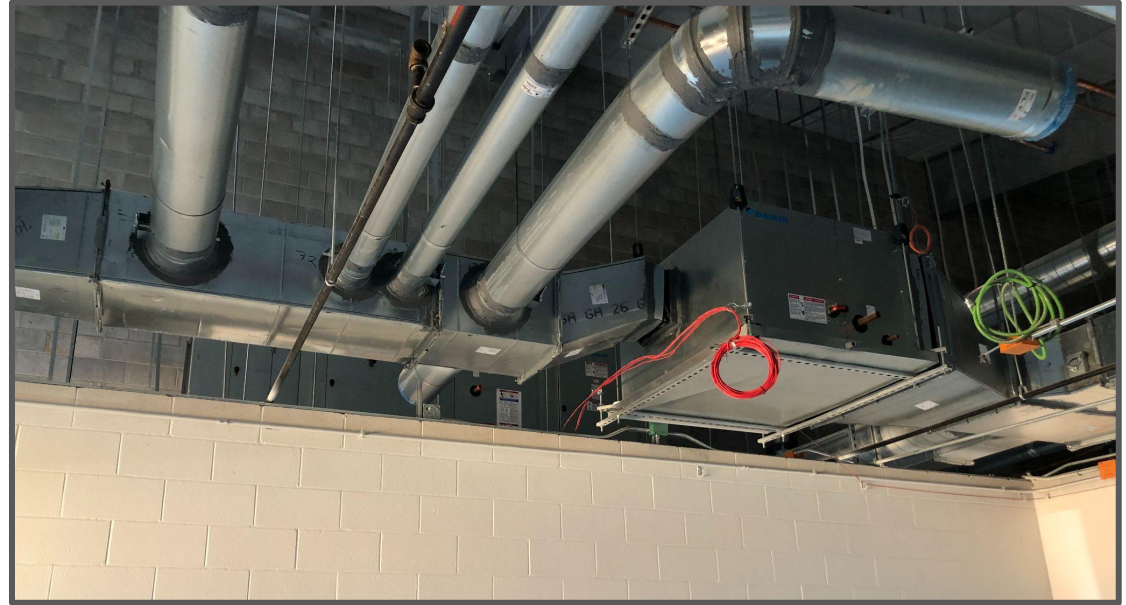

MEP above ceiling

Ag Barn




Vet Tech & Animal Science Classrooms

WALLER ISD
CONSTRUCTION



Practice Arena


Ag Barn

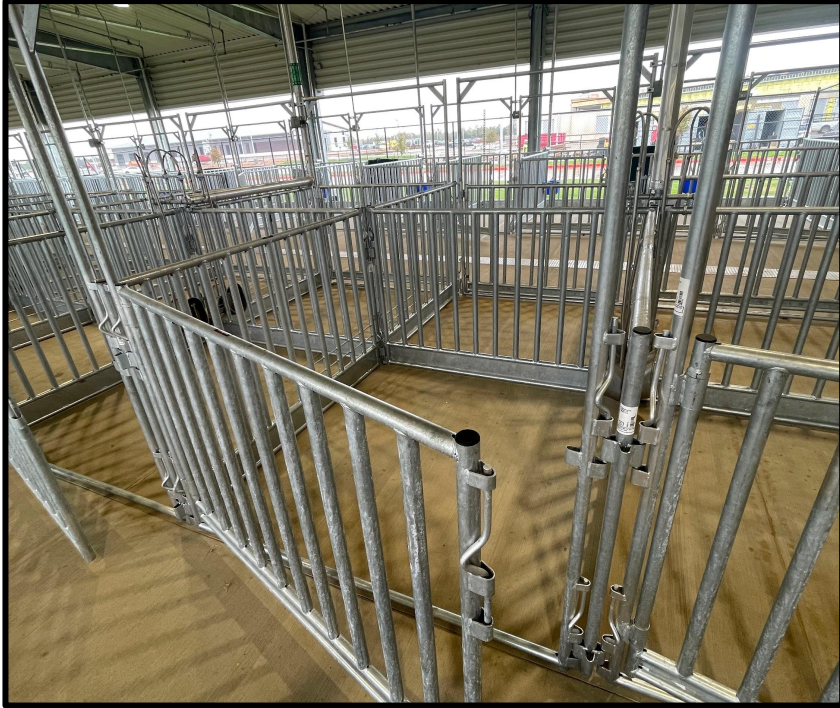

Animal Pens



Ag Barn

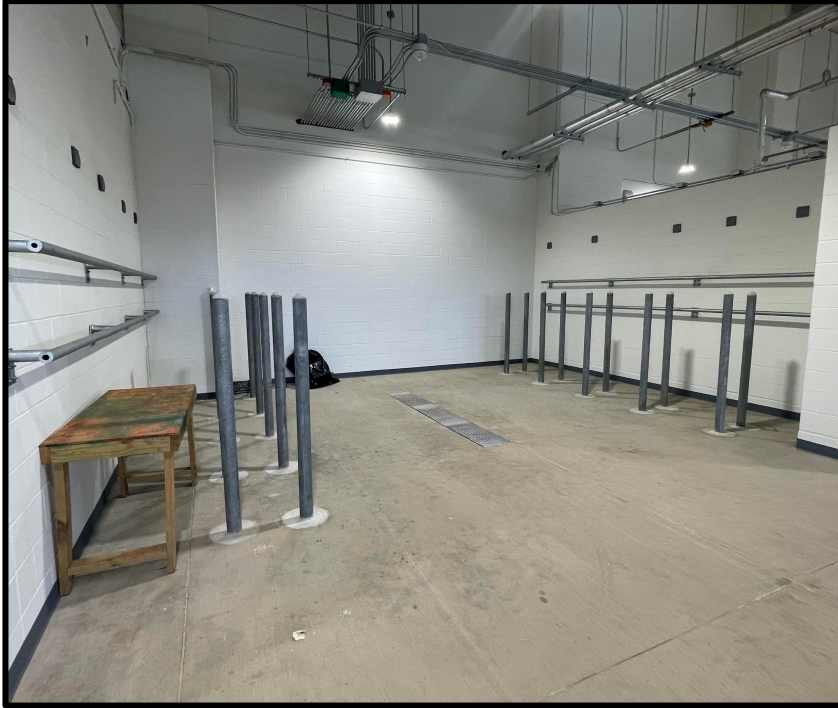

Animal Wash & Grooming Spaces



Ag Barn



Pet Relief and Arena Viewing Areas

CURE ELEMENTARY



- Exterior brick and stone is nearing completion.
- Tile installation is ongoing.
- MEP overhead installations are ongoing.
- Exterior glazing is nearing completion.
- Door Frame installations are in progress and doors are onsite.
- Restroom partition installations have started.
- Linear ceiling is onsite and installation is started.
- Playground and landscape installations are in progress.

Cure Elementary



Front Elevation

Cure Elementary



Front Entry Wall Tile

Cure Elementary



Corridors




Cure Elementary



Classrooms



Cure Elementary

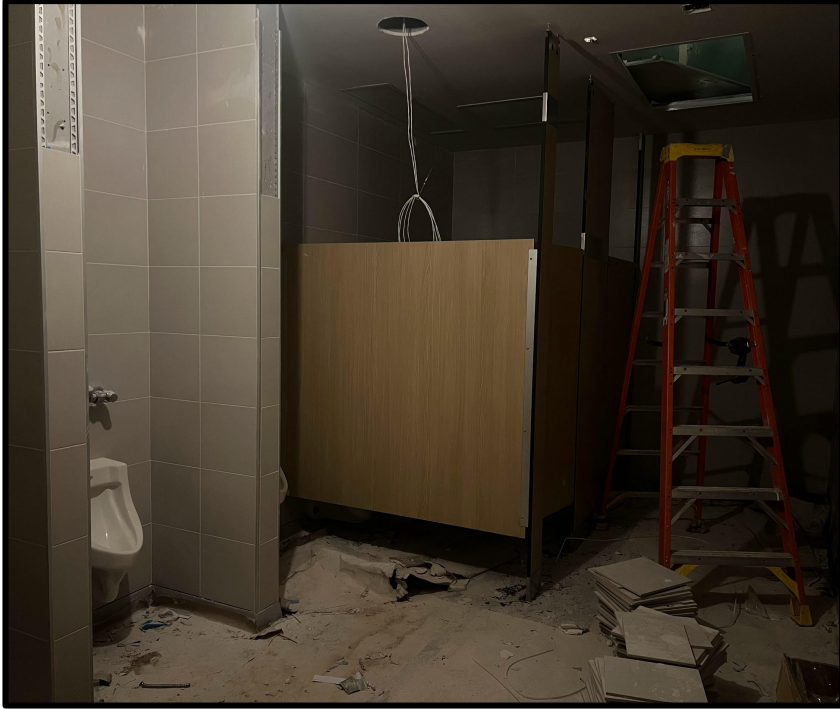

Restrooms and Drinking Fountain

Cure Elementary



Library

Cure Elementary



Kitchen




Cure Elementary



Playground and Landscaping

EDUCATION SERVICE CENTER

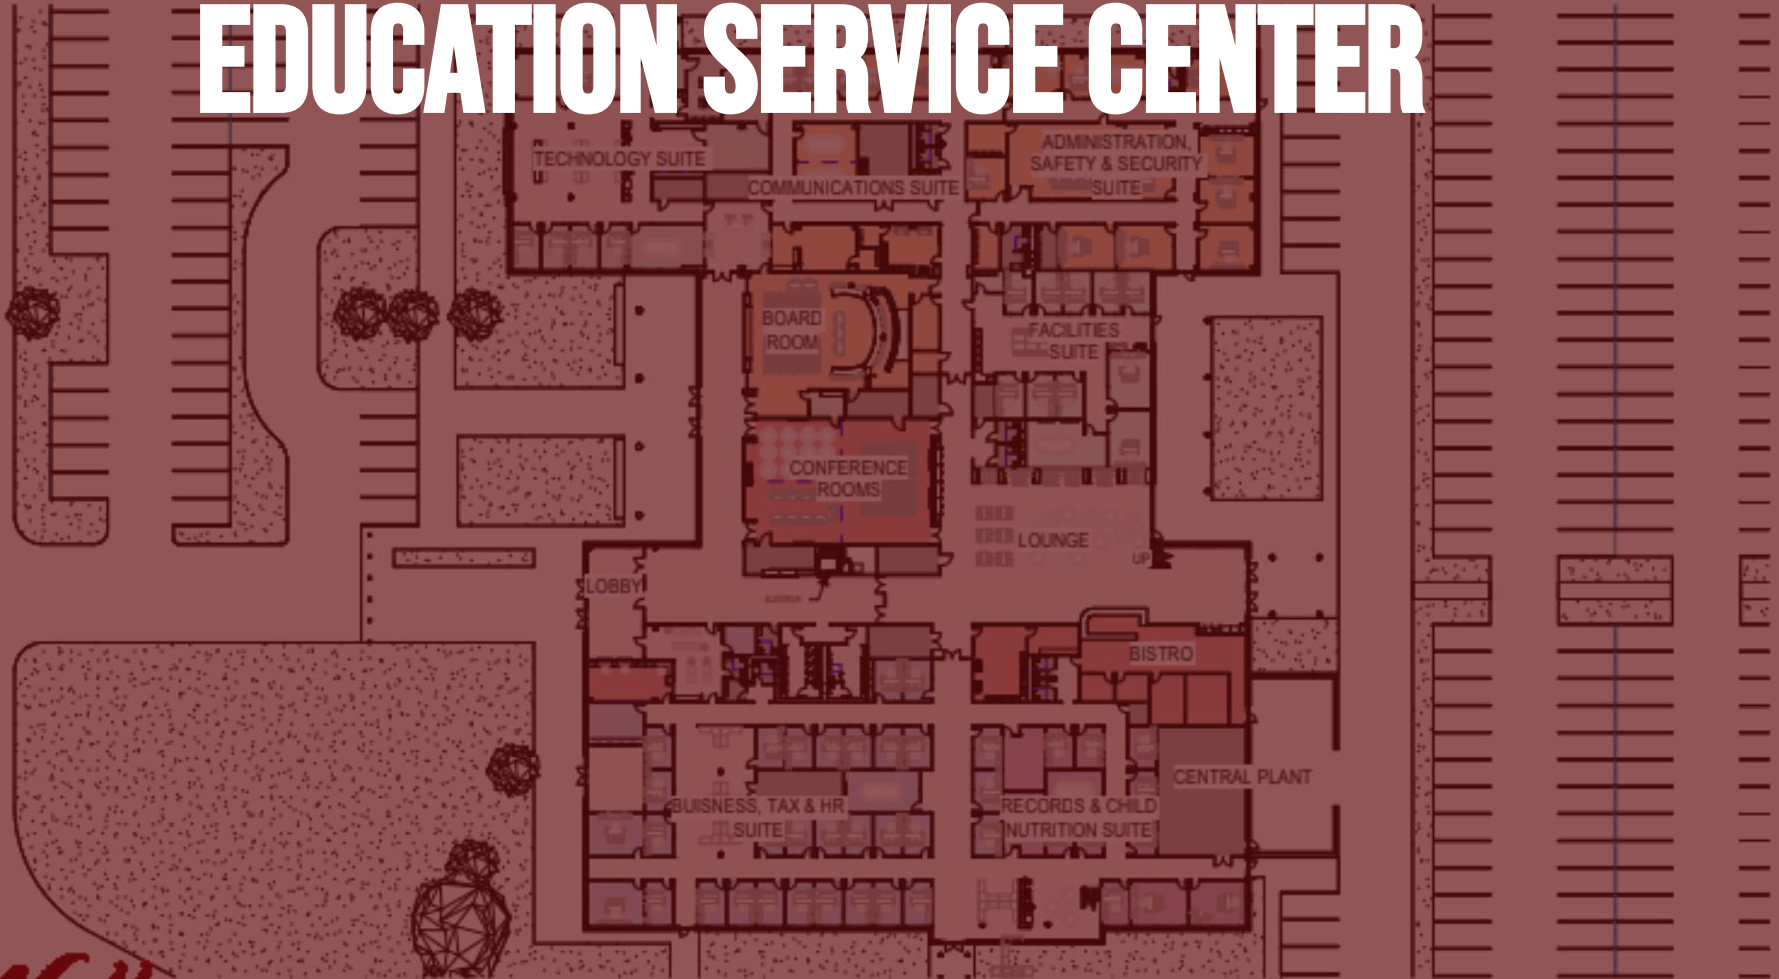

- Exterior masonry is nearing completion and glazing is in progress.
- MEP overhead installations continue to progress.
- Interior wall framing is complete and drywall is nearing completion.
- Interior masonry at the board room is in progress.
- Tiling in restrooms is ongoing.
- Installation of the canopy between the ESC and Transportation has started.
- Fuel pumps are installed at the Fueling Station.

ESC-Ag-Cure Elementary



Aerial View - Southwest Corner

Education Service Center



Exterior





Exterior Glazing

Education Service Center



Boardroom



Education Service Center



Large Conference Rooms



Education Service Center



Bistro

Education Service Center



Offices



Education Service Center



East Elevation and Canopy to Transportation



Front entry and Side Elevations



Dispatch and Bus Driver Lounge



Offices



Bay Area



Fueling Station



PRIORITY 1 PROJECTS



Priority 1 Improvement

- Reroof of Schultz, Holleman, and Roberts Road are due to be completed in early February.
- Security fencing fabric installation has been completed at P1 campuses with gate hardware on order.
- Sliding marker boards installation at Jones ES have been completed.
- Security Signage installation has started at all the P1 campuses.
- Roberts Road front office demolition plan has begun.
- Interior lighting upgrades will begin in January.
- Package 2 GMP, Summer 2025 work, is being finalized for approval.

Priority 1 Improvement



Schultz JH Roofing

Priority 1 Improvement



RRE Wall Panels

Priority 1 Improvement



Roberts Road Elem. Demolition

Priority 1 Improvement




Roberts Road Elem. Demolition

Priority 1 Improvement



WJH Field House Demolition

Priority 1 Improvement

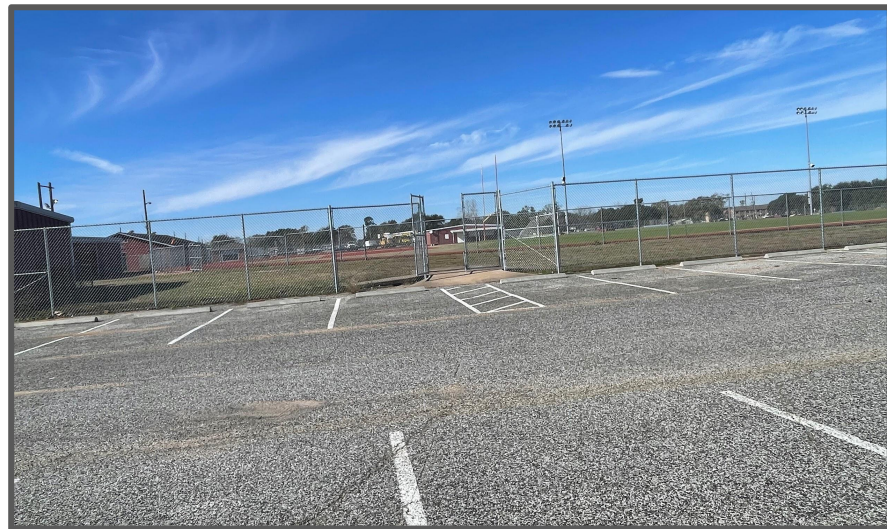

Fencing and Gates

2024 - \$702 M BOND



- Warren Ranch High School (#2) - Design starting, opens in summer 2028
- Johnson Junior High School (#3) - Planned opening 2029
- Elementary #9 - Planned opening 2027
- Elementary #10 - Planned opening 2028

A photograph of a classroom filled with children of various ages, from young children to teenagers. They are all expressing excitement, with many having their arms raised in the air. The children are seated at small, light-colored tables with blue chairs. The classroom has white walls, a tiled ceiling, and various educational posters and supplies visible in the background. The entire image is overlaid with a semi-transparent red filter.

#ThankYouVoters

Waller
Independent School District
