

BOND CONSTRUCTION UPDATE

March 2025

#ThankYouVoters

2019 - \$295 M BOND



2019 BOND SUMMARY

- New Large-Capacity High School - COMPLETE
- Waller Junior High Addition & Renovation - COMPLETE
- Renovate WHS to Schultz Junior High - COMPLETE
- Renovate SJH to Holleman Elementary - COMPLETE
- Land, Buses, Technology, Security - COMPLETE
- Stadium LED lighting Upgrade - COMPLETE
- Stadium Video Board & Sound System - COMPLETE
- * Stadium Replacement Turf - March-May 2025
- * Stadium HVAC Upgrades - Summer 2025

2022 - \$363 M BOND



- Lowe Elementary (#6) - COMPLETE
- McReavy Elementary (#7) - COMPLETE
- Cure Elementary (#8) - Opening Summer 2025
- Smith Andrews Ag Science Complex - COMPLETE, Opening Feb 2025
- Education Service Center and Transportation - Opening summer-fall 2025
- Priority 1 District Facility Upgrades - In progress, Complete in fall 2025.
- District HVAC upgrades - completing design for summer 2025 work.

LOWE AND MCREAVY ELEMENTARY SCHOOLS



- Both campuses opened in August 2024.
- Punch List work is complete.
- HVAC Building Commissioning punch lists are complete and the final reports are in progress.
- Interior graphics package is complete at MES and in production at LES.

SMITH ANDREWS AG SCIENCE COMPLEX



- Punch list is being completed.
- Furniture and equipment has been installed.
- Animal paneling has been installed.
- Final walkthroughs are being conducted.
- City of Waller has issued TCO.

Ag Barn



Front Elevation



February 24th Shows

WALLER ISD
CONSTRUCTION



February 24th Shows

Ag Barn



February 24th Shows

Ag Barn



February 24th Shows





February 25th Shows



February 25th Shows

WALLER ISD
CONSTRUCTION

Ag Barn



February 25th Shows

WALLER ISD
CONSTRUCTION

Ag Barn



February 25th Shows

WALLER ISD
CONSTRUCTION

Ag Barn



February 25th Shows

WALLER ISD
CONSTRUCTION

CURE ELEMENTARY



- Permanent power is on and the generator is installed.
- Casework, markerboards and carpet are being installed in classrooms.
- Vinyl wall covering installation is in progress.
- Storefront frame installations are in progress.
- Tile installation is nearing completion at restrooms.
- MEP overhead has been inspected and ceiling tiles are being installed.
- Restroom partitions are installed.
- Playground installation is almost complete.
- Landscaping is in progress.

Cure Elementary



Front Elevation



Cure Elementary




Front Entry Corridor

Cure Elementary



Corridors

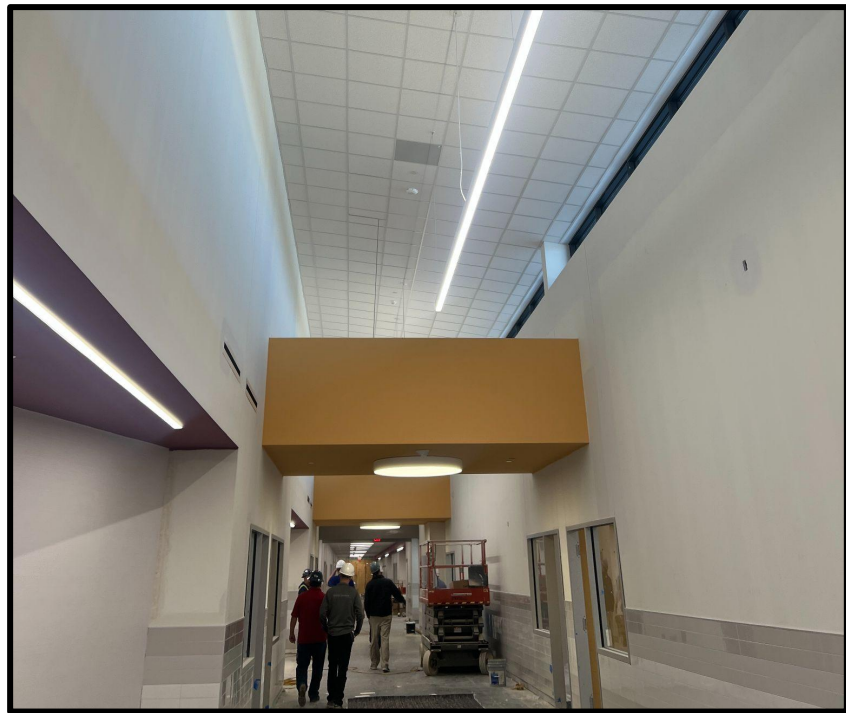

Cure Elementary



Classrooms



Cure Elementary



Restrooms and Drinking Fountain

Cure Elementary




Library

Cure Elementary



Cafeteria and Gym

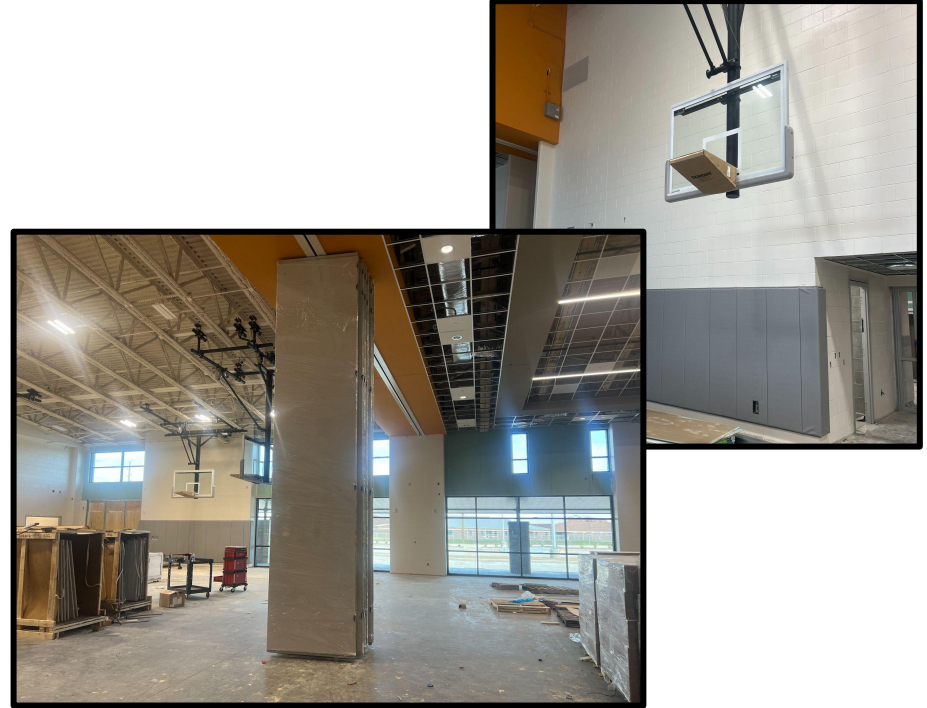

Cure Elementary



Playground and Landscaping


Cure Elementary



Central Plant



EDUCATION SERVICE CENTER

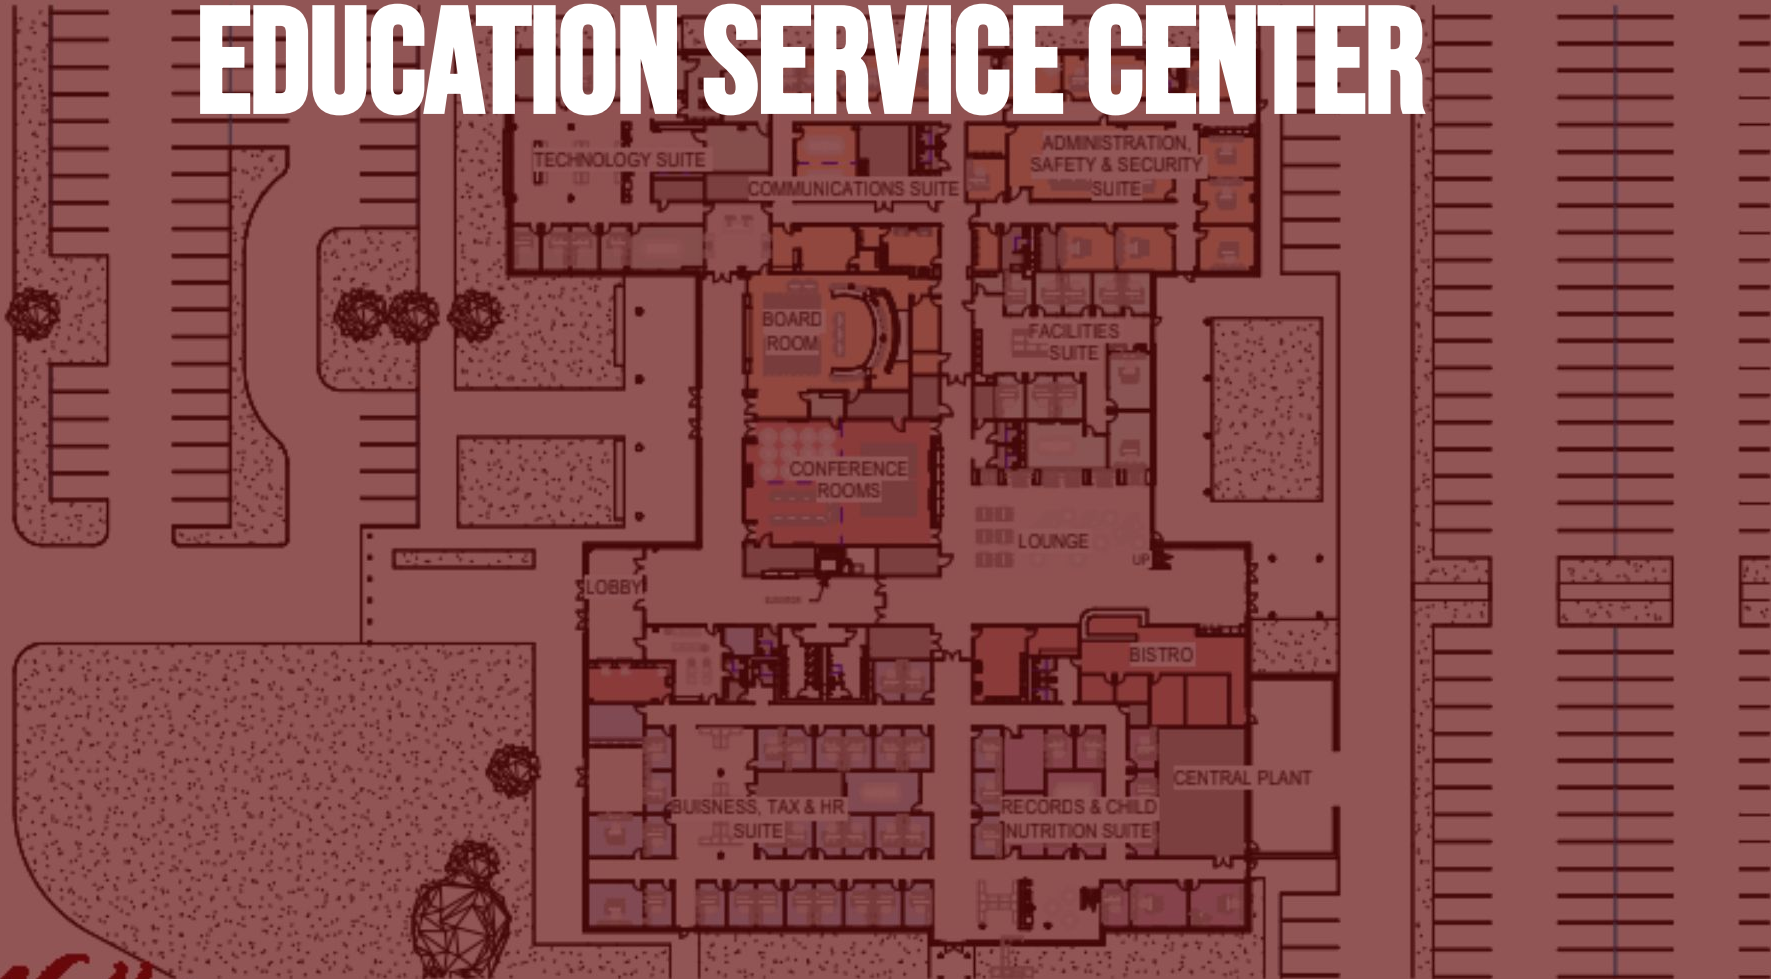

- Ceiling installations are in progress.
- Storefront framing is in progress at offices.
- Tiling in restrooms and the bistros is nearing completion.
- Elevator is installed.
- Painting is in progress.
- Installation of the canopy between the ESC and Transportation is ongoing.
- Lighting is in progress.
- Overhead doors are installed at Transportation bays.

ESC-Ag-Cure Elementary



Aerial View - Southwest Corner (February 2025)



Front Elevation

Education Service Center



Exterior



Education Service Center



Main Entry Corridor and Reception




Education Service Center




Boardroom



Education Service Center

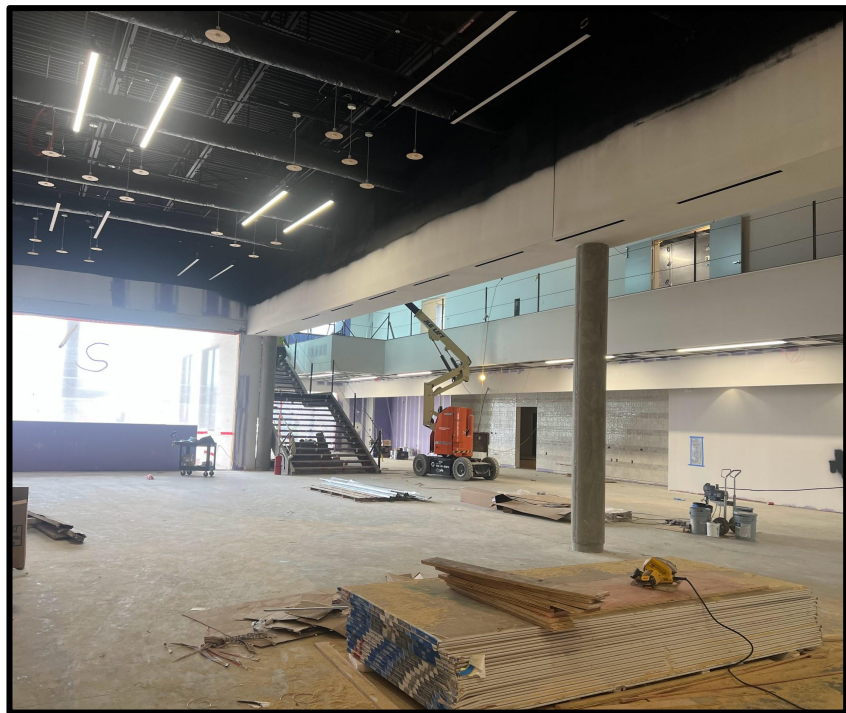


Bistro

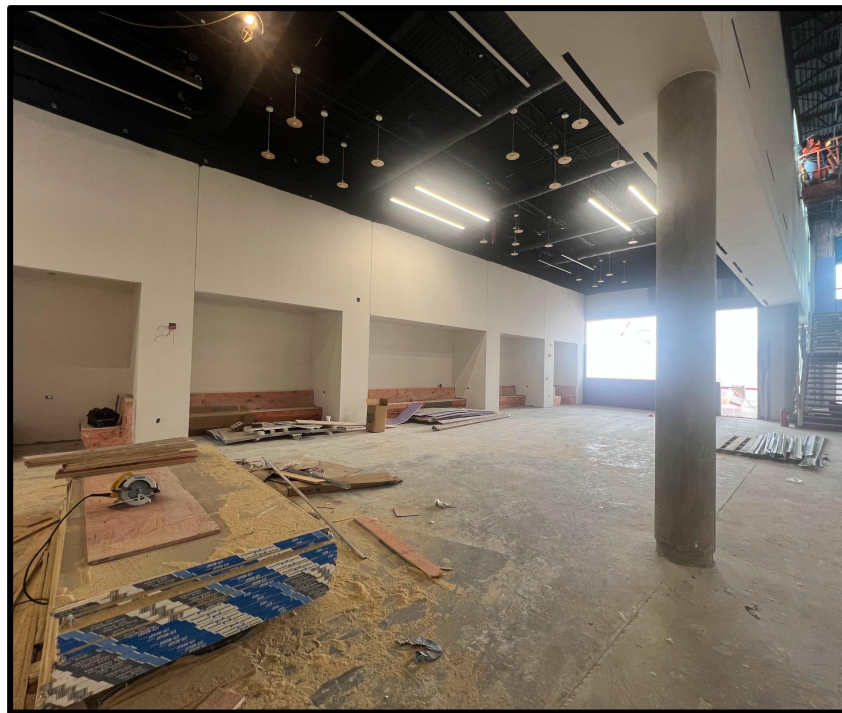



Offices



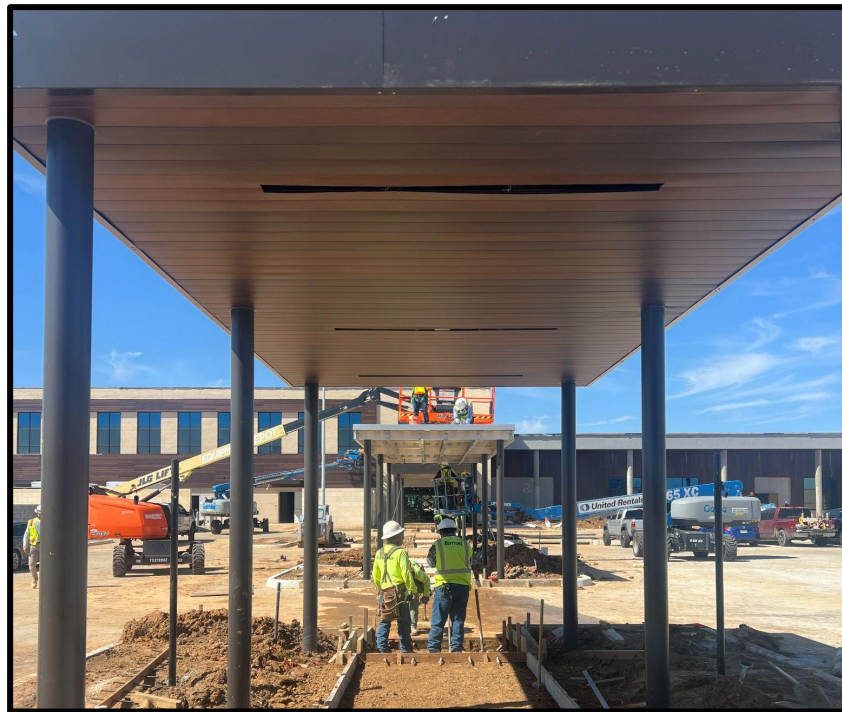

Canopy from ESC to Transportation



Front entry and Side Elevations



Offices





Bus Driver Lounge



Transportation Shop



PRIORITY 1 PROJECTS



Priority 1 Improvement

- Reroof of Schultz, Holleman, and Roberts Road are all 95% completed with mostly trim, gutters, and downspouts left.
- Security fencing, gates, and hardware has been completed.
- Jones ES library enclosure has begun with completion during spring break.
- WHS safety film has begun with installation to be completed during spring break.
- Roberts Road front office demolition is completed with walls beginning to be framed out. Track relocation to rear of the building will begin shortly.
- Interior lighting, Front Row, intrusion and fire alarm upgrades have begun at multiple campuses with all campuses set to be completed by summer.

Priority 1 Improvement



Roberts Road Admin Reno

WALLER ISD
CONSTRUCTION


Priority 1 Improvement



Roberts Road Admin Reno

WALLER ISD
CONSTRUCTION

Priority 1 Improvement

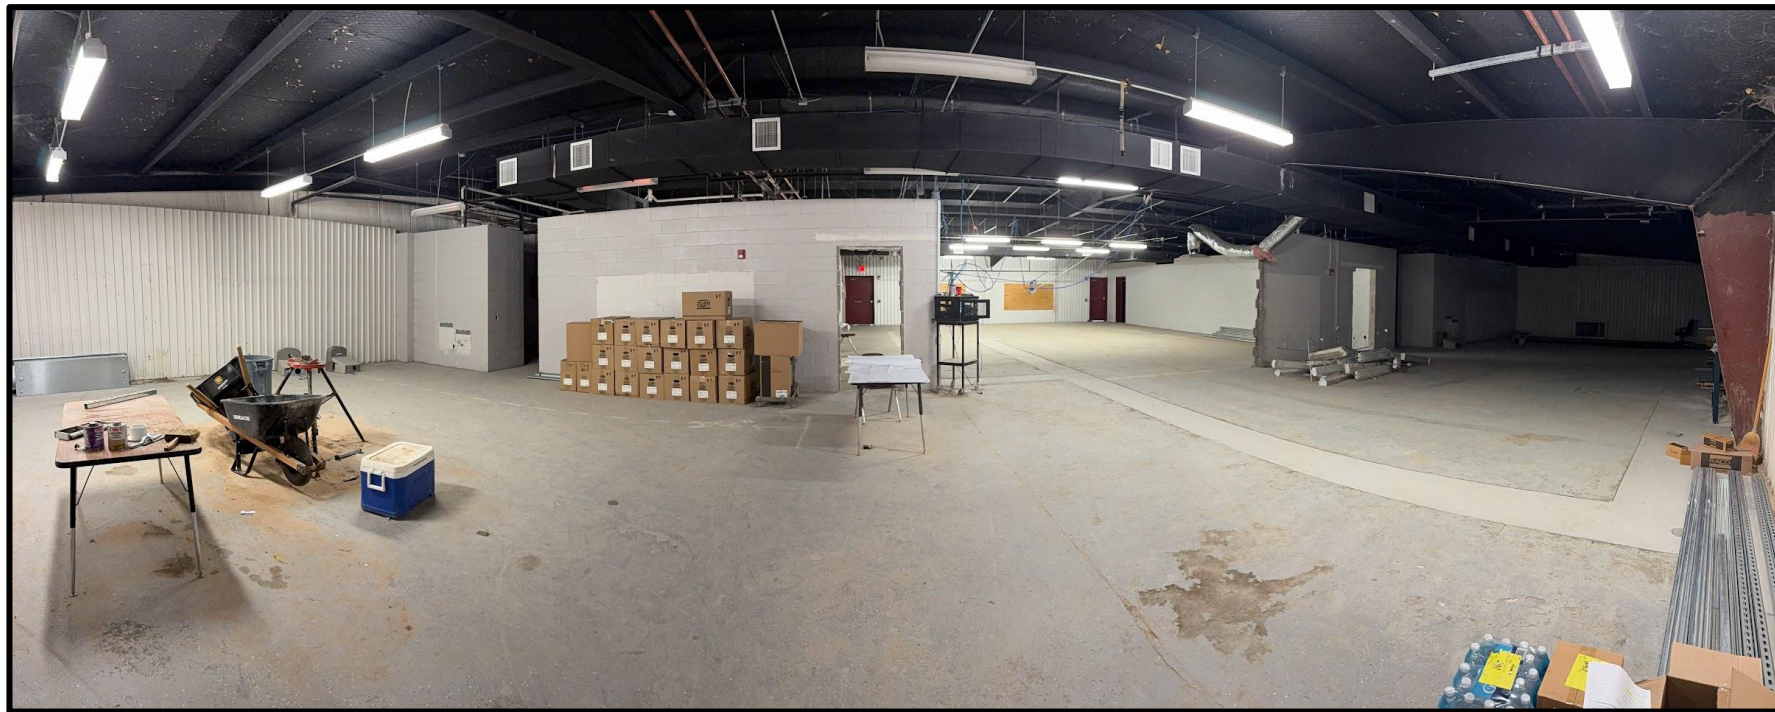

WJH Field House Reno

WALLER ISD
CONSTRUCTION

Priority 1 Improvement



WJH Field House Reno

Priority 1 Improvement



Jones Library Enclosure



2024 - \$702 M BOND



- Warren Ranch High School (#2) - Design starting, opens in summer 2028
- Johnson Junior High School (#3) - Planned opening 2029
- Elementary #9 - Planned opening 2027. Kick off meeting set for March 3rd.
- Elementary #10 - Planned opening 2028

A photograph of a classroom filled with children of various ages, from young children to teenagers. They are all expressing excitement, with many having their arms raised in the air. The children are seated at small, light-colored tables with blue chairs. The classroom has white walls, a tiled ceiling with recessed lights, and various educational posters and supplies visible in the background. The entire image is overlaid with a semi-transparent red filter.

#ThankYouVoters

Waller
Independent School District
