




New Construction

PROGRESS UPDATE
April 2025

Fairport Harbor New Pre K-12 School



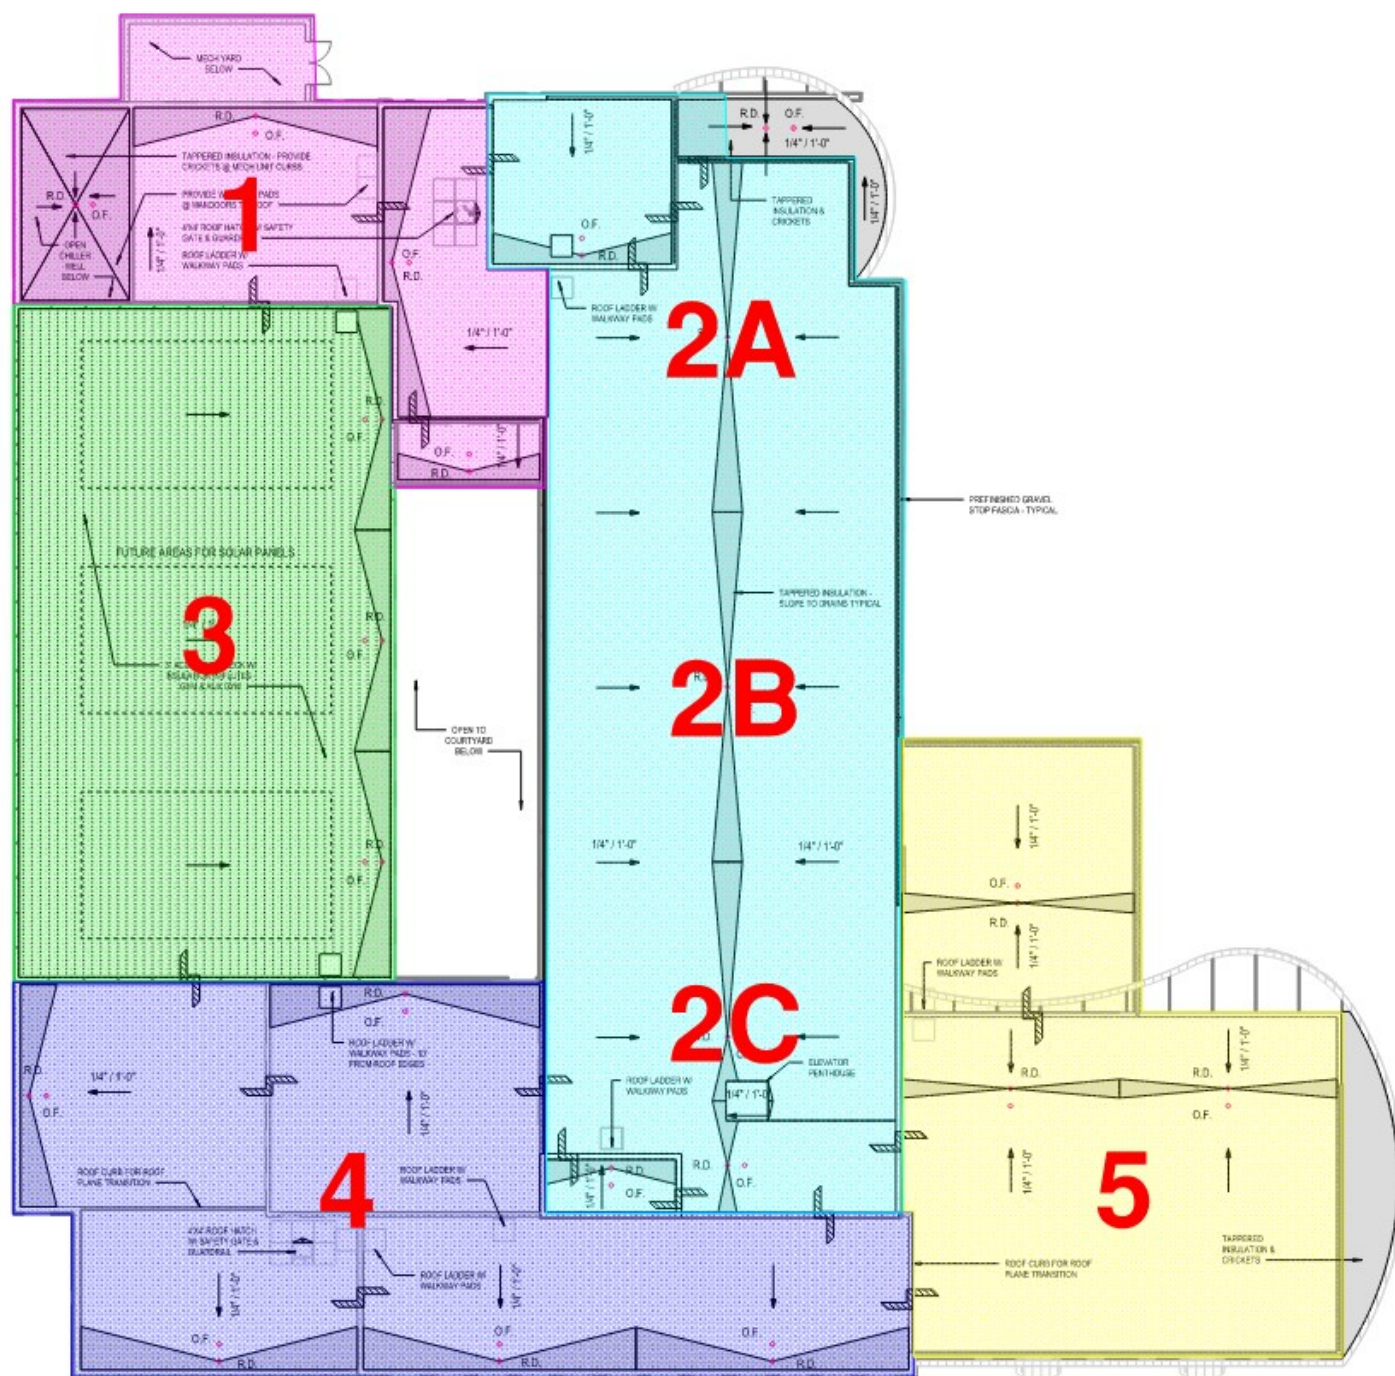

PROJECT SUMMARY

Phase 1


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

April 2025 Progress


- Duct Insulation—Complete
- Drywall Taping—Complete
- Wall Priming—In Progress
- Wall Painting—In Progress

Upcoming Progress

- Storefront Windows

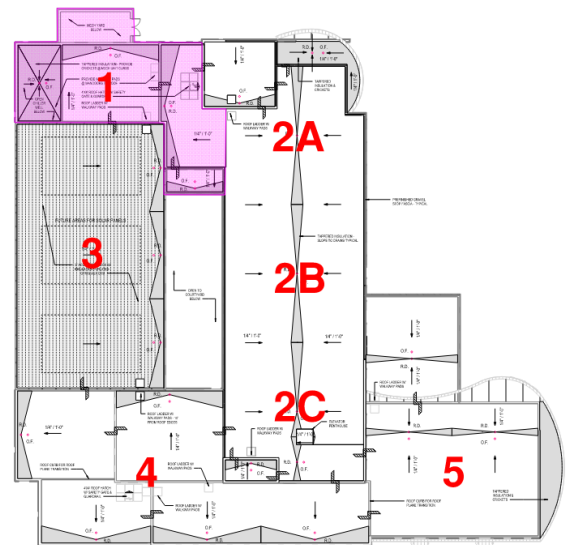

PROJECT SUMMARY

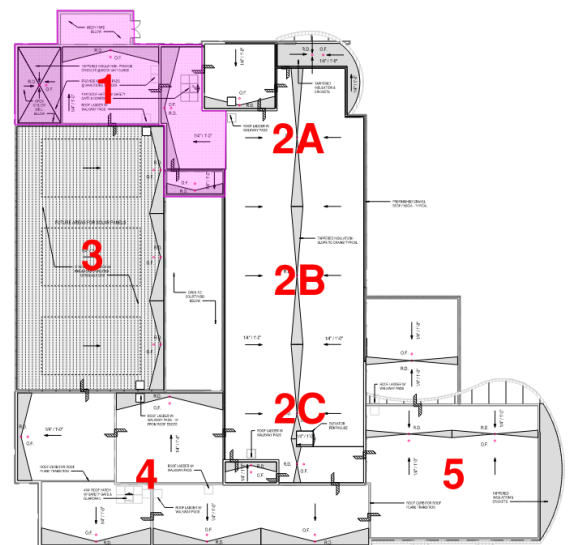

PROJECT SUMMARY

Phase 2


- **Educational Classrooms**

April 2025 Progress



- Overhead Plumbing Rough In on 3rd Floor—Complete
- Hanging Drywall 2nd and 3rd Floor—Complete
- Stair Tower 1 Joist and Roof Deck—Complete
- Sprinkler Piping on 2nd Floor—In Progress
- Duct and Pipe Insulation—In Progress
- In Wall Rough In's on 3rd Floor—Complete
- Veneer on Eastside—Complete
- Wall Priming 1st Floor—In Progress
- Wall Painting 1st Floor—In Progress
- Temperature Control Wiring—In Progress

Upcoming Progress

- Drywall Taping 2nd and 3rd Floor
- Sprinkler Pipe on 3rd Floor
- Windows

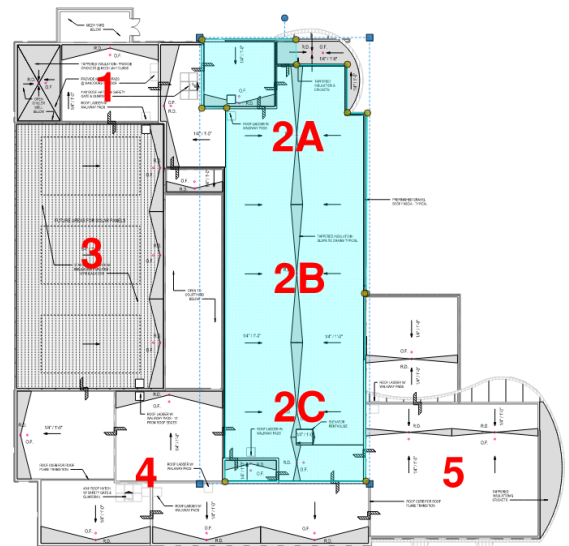

PROJECT SUMMARY

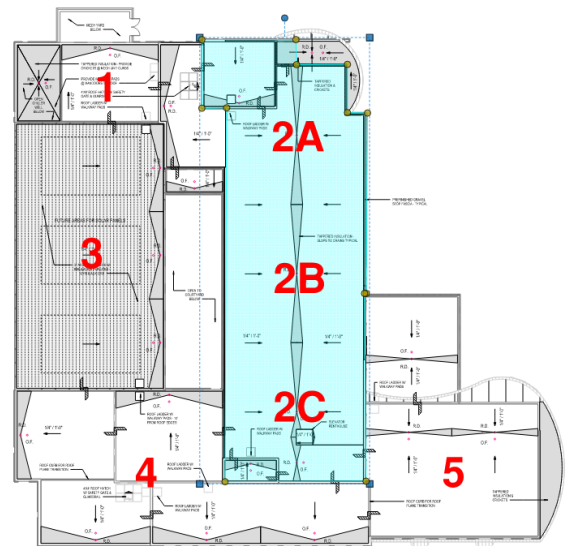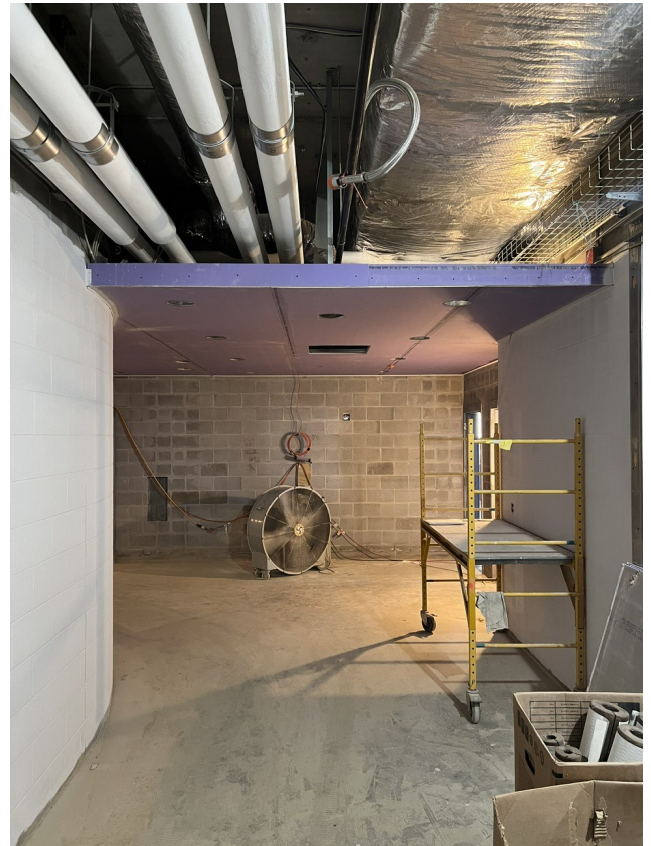

PROJECT SUMMARY

Phase 3


- Auxiliary GYM
- Gymnasium

April 2025 Progress



- Aux Gym Overhead Electrical—Complete
- Aux Gym Drywall Finishing at Demising Wall—Complete
- Wall Priming Aux Gym—Complete
- Wall Painting Aux Gym—In Progress
- Overhead Technology Rough Ins—Complete
- Wall Priming Main gym—In Progress
- Main Gym Electrical Rough In—In Progress
- Main Gym Technology Rough In—In Progress

Upcoming Progress

- Exterior Patch Work
- Wall Paint

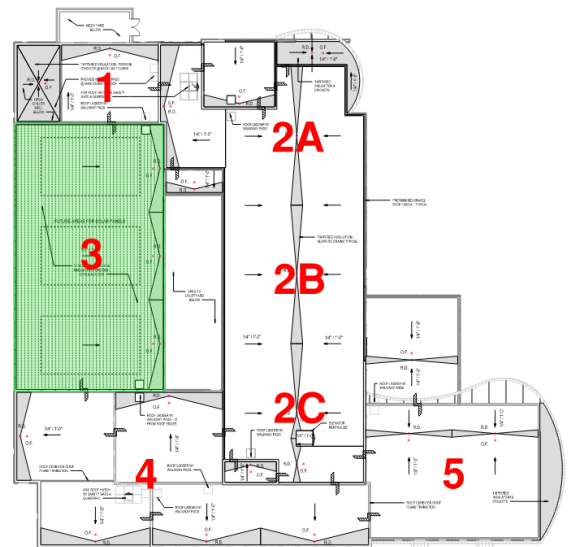

PROJECT SUMMARY

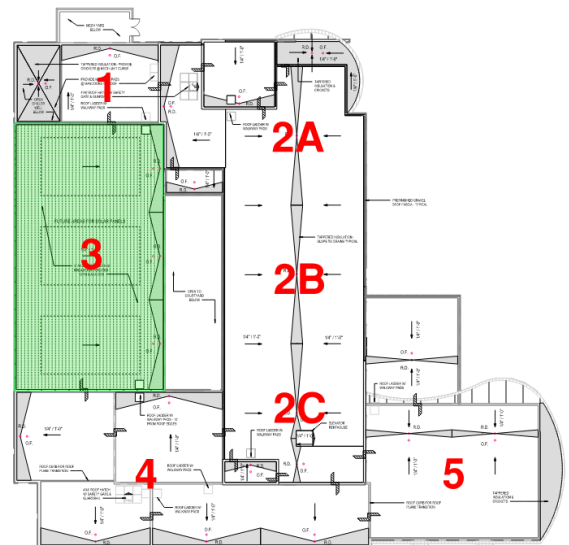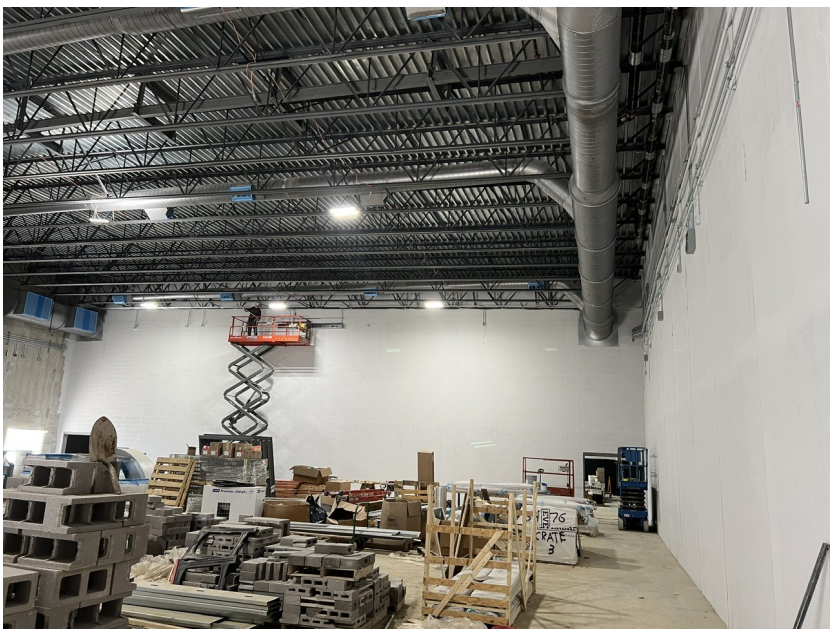

PROJECT SUMMARY

Phase 4


- Kitchen
- Locker Room

April 2025 Progress


- Interior Nonbearing Walls—In Progress
- Joist and Deck—Complete
- In Wall Electrical Rough In—In Progress
- In Wall Plumbing Rough In—In Progress
- Underground Plumbing—Complete
- Underground Electrical East Half—In Progress
- Bearing Masonry East Half—In Progress

Upcoming Progress

- Slab on Grade prep and Pour East Half
- Joist and Deck East Half
- Roof Membrane

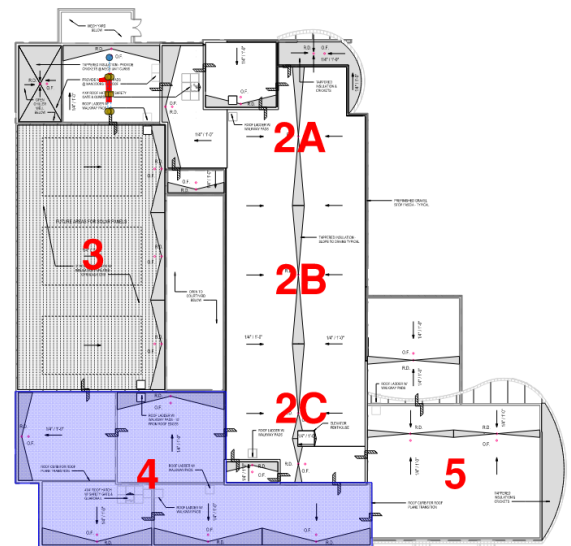

PROJECT SUMMARY

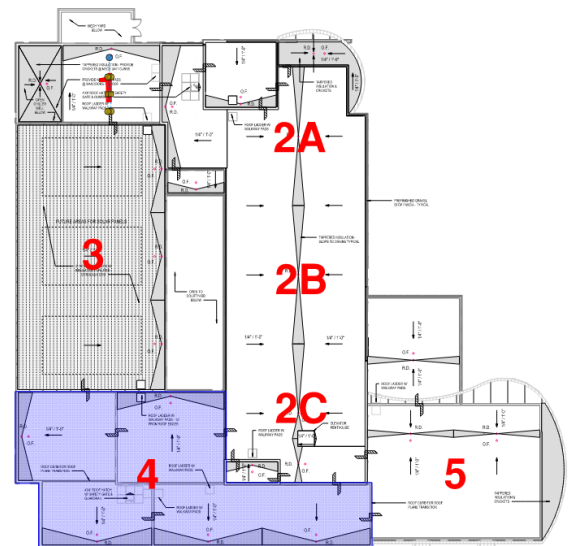

PROJECT SUMMARY

Phase 5

- Administration
- Library

April 2025 Progress

- Foundations—Complete
- Underground Plumbing—In Progress

Upcoming Progress

- Underground Electrical
- Masonry to Grade
- Slab on Grade Prep

