




New Construction

PROGRESS UPDATE
May 2025

Fairport Harbor New Pre K-12 School



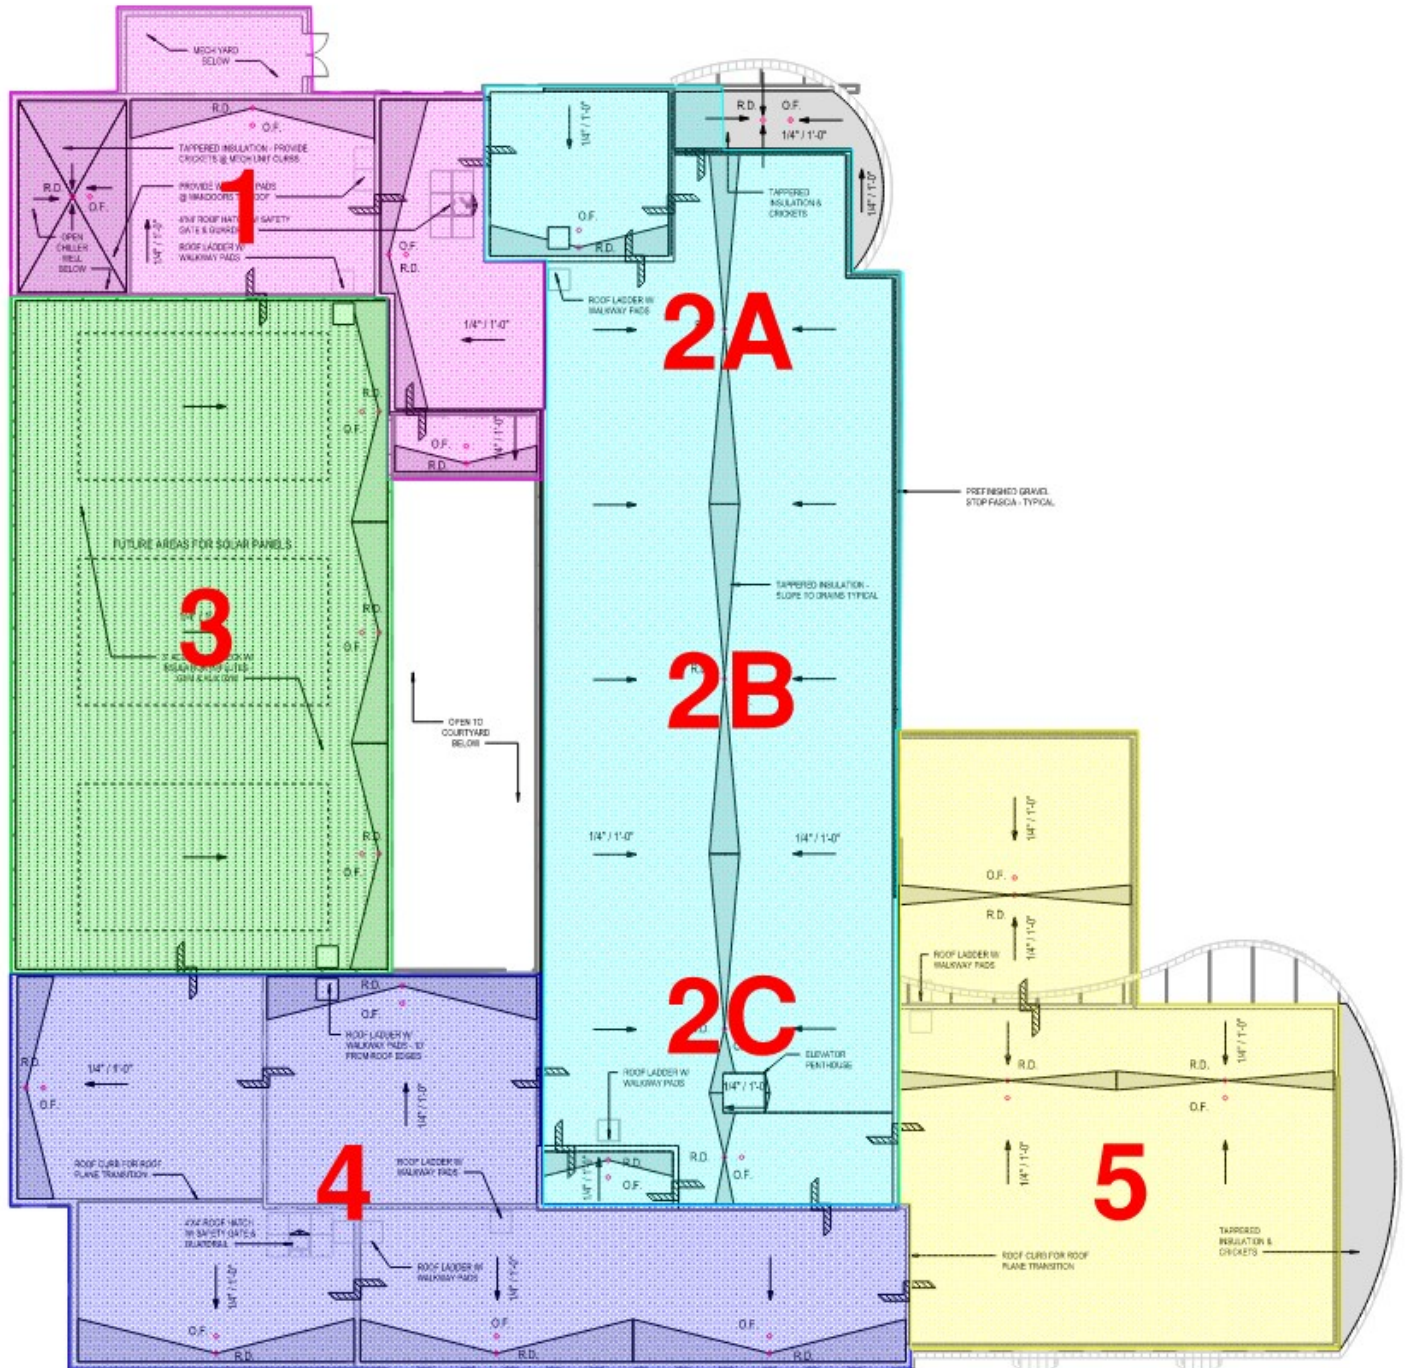


PROJECT SUMMARY

Phase 1


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

May 2025 Progress

- Wall Priming—Complete
- Wall Painting—Complete
- Storefront Windows—Complete
- Technology Cabling—In Progress
- Drop Ceilings—In Progress

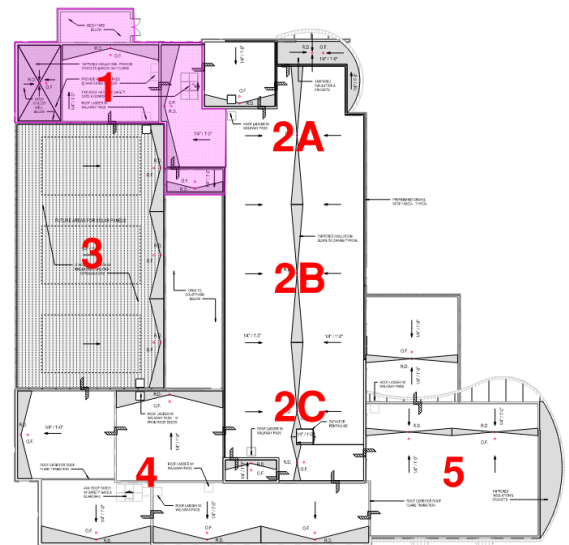

PROJECT SUMMARY

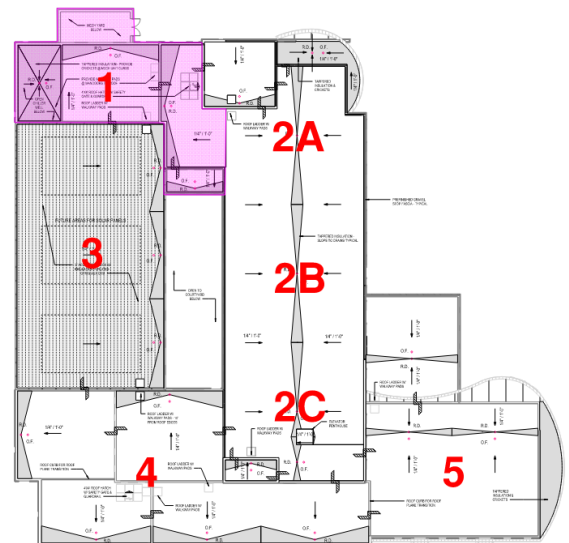

PROJECT SUMMARY

Phase 2


- Educational Classrooms

May 2025 Progress


- Sprinkler Piping on 2nd Floor—Complete
- Sprinkler Piping on 3rd Floor—In Progress
- Duct and Pipe Insulation—Complete
- Wall Priming 1st Floor—In Progress
- Wall Painting 1st Floor—In Progress
- Wall Priming 2nd Floor—In Progress
- Wall Painting 2nd Floor—In Progress
- Drywall Finishing 3rd Floor—In Progress
- Temperature Control Wiring—In Progress
- Drop Ceiling on 1st Floor—In Progress
- Windows—Complete

Upcoming Progress

- Casework
- Drop Ceilings 2nd Floor

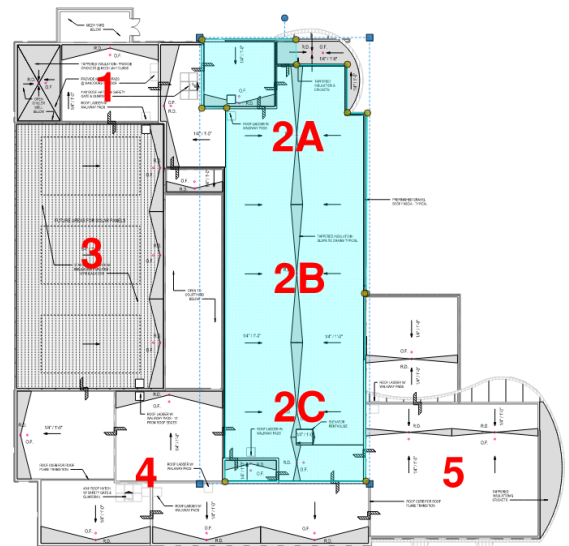

PROJECT SUMMARY

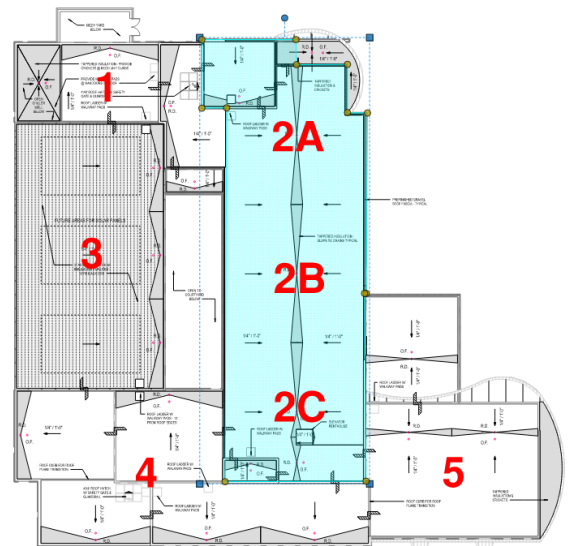

PROJECT SUMMARY

Phase 3


- **Auxiliary GYM**
- **Gymnasium**

May 2025 Progress


- **Wall Painting Aux Gym—Complete**
- **Wall Priming Main gym—In Progress**
- **Main Gym Electrical Rough In—In Progress**
- **Main Gym Technology Rough In—In Progress**
- **Technology Cabling in Aux Gym—In Progress**

Upcoming Progress

- **Wall Painting in Main Gym**

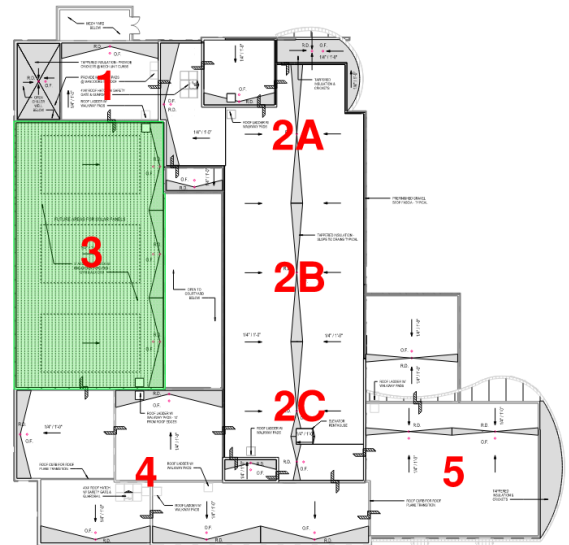

PROJECT SUMMARY

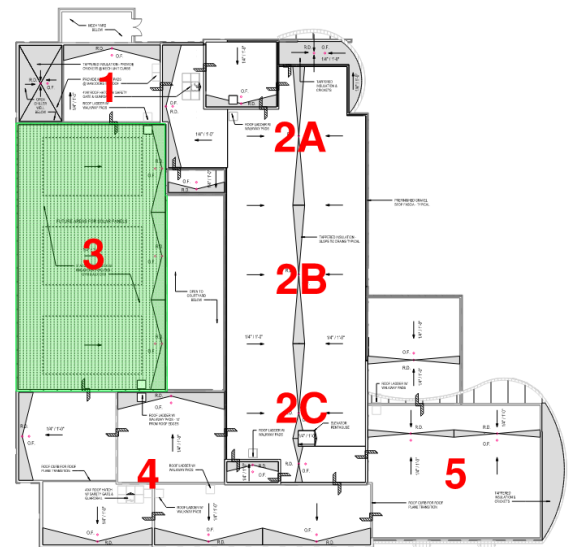

PROJECT SUMMARY

Phase 4


- Kitchen
- Locker Room

May 2025 Progress


- Interior Nonbearing Walls—In Progress
- In Wall Electrical Rough In—In Progress
- In Wall Plumbing Rough In—In Progress
- Bearing Masonry East Half—In Progress

Upcoming Progress

- Slab on Grade prep and Pour Middle Section
- Joist and Deck East Half
- Roof Membrane

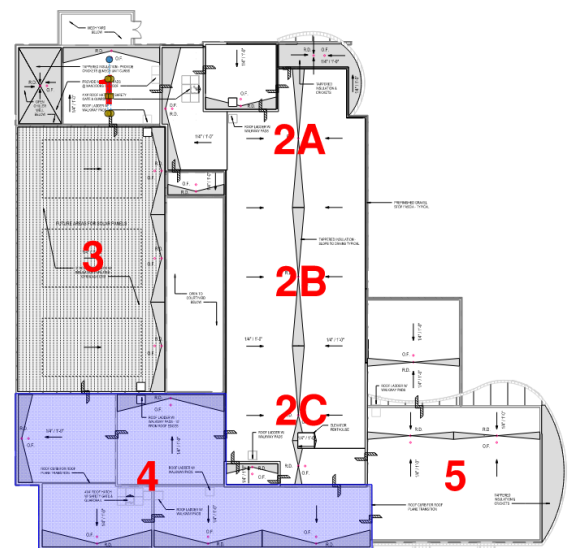

PROJECT SUMMARY

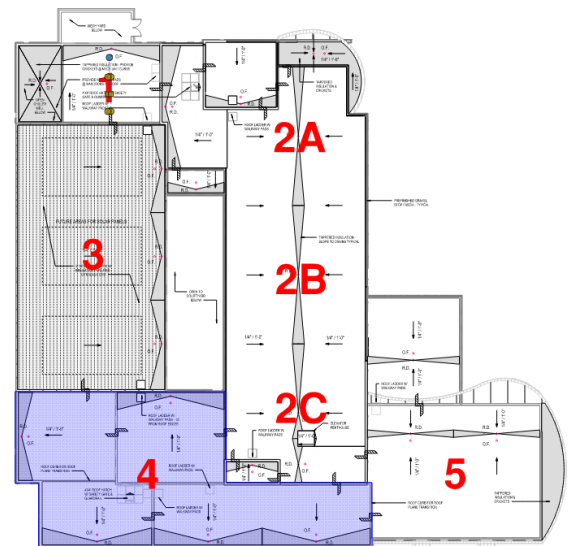

PROJECT SUMMARY

Phase 5


- Administration
- Library

May 2025 Progress

- Underground Plumbing—complete
- Structural Steel—In progress
- Bearing Masonry—In Progress
- Exterior Framing—In Progress
- Exterior Sheathing—In Progress

Upcoming Progress

- Slab on Grade Prep South Half
- Roof Membrane
- Duct Work

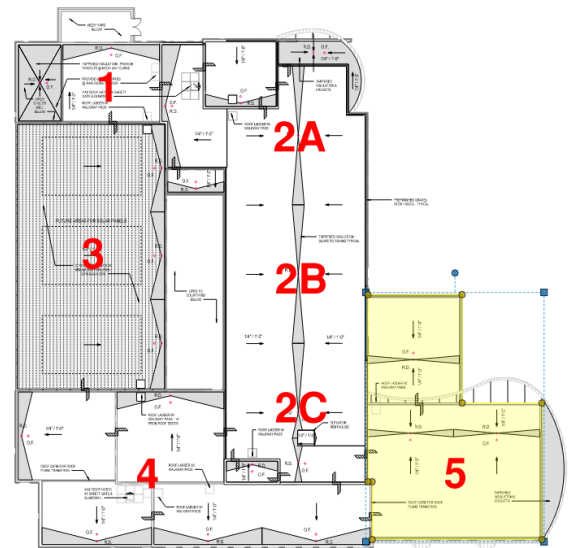

PROJECT SUMMARY

