


SMALLWOOD ELEMENTARY SCHOOL SITE LOGISTIC PLAN

SEQUENCE A: 06/30/25 - 10/31/25

SITE LOGISTICS KEY

	CONSTRUCTION EGRESS / ENTRANCE
	CONSTRUCTION FENCING - POST DRIVEN
	CONTRACTOR PARKING
	DUMPSTERS
	H2M DUMPMSTER
	OWNER EGRESS / ENTRANCE
	TEMPORARY STAGING AREA & ACCESS ROAD - EXISTING TO MAINTAIN
	TEMPORARY STAGING AREA & ACCESS ROAD - EXPANSION
	TEMPORARY TOILET UNIT

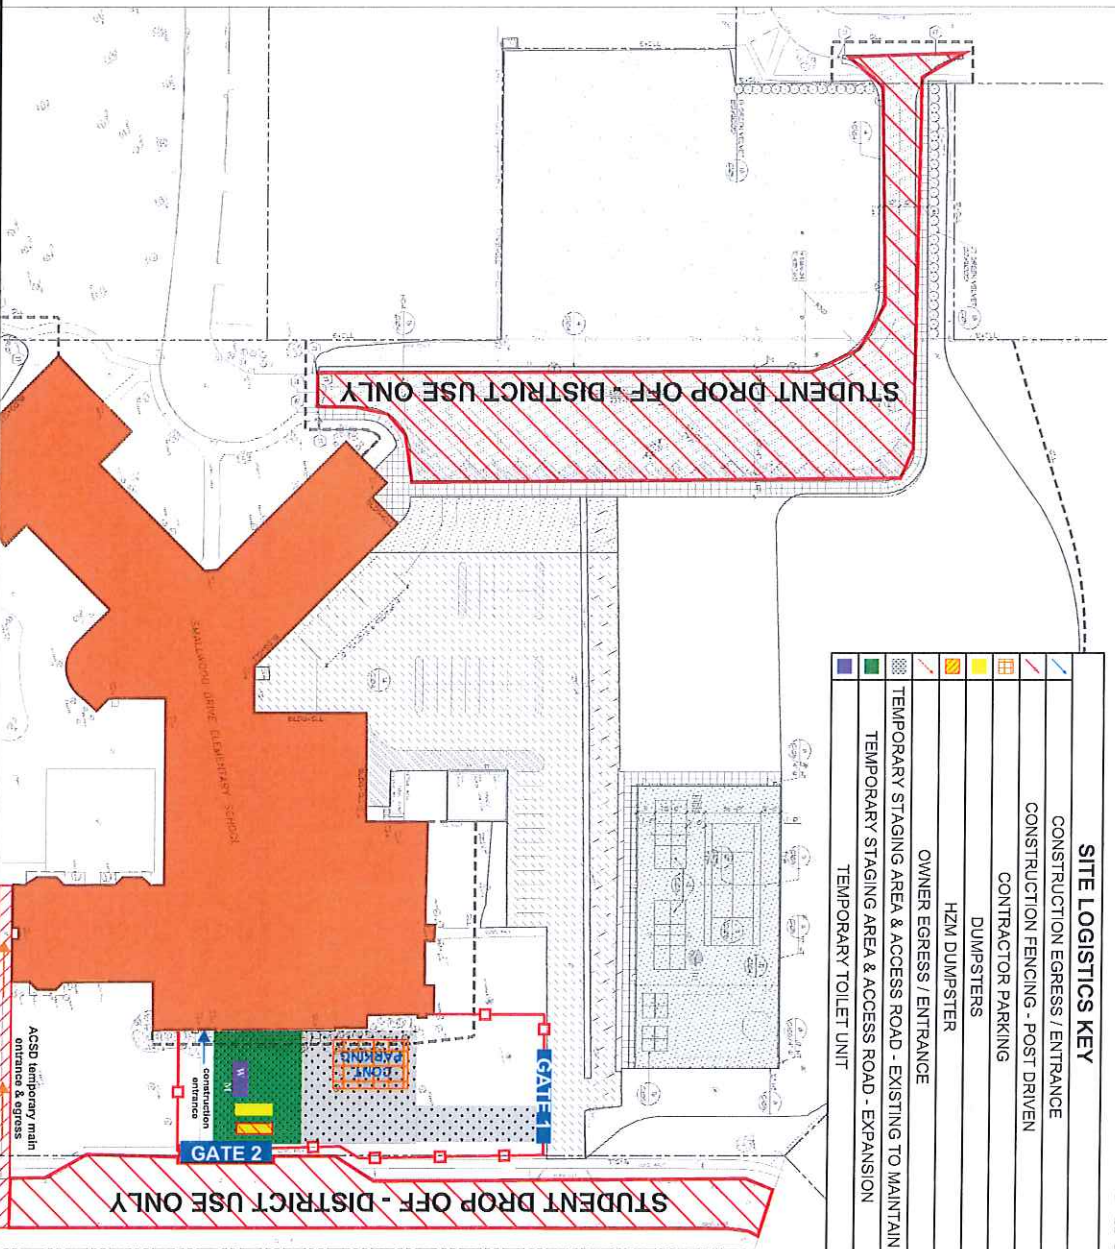

General Notes:

1. Reference Scope of Work and Special Provisions for responsibility of temporary construction / facilities as shown.
2. Site Work Contractor to install and maintain temporary site fencing and entry/exit gates for the duration of the main office / secure entrance renovations.
3. Site Work Contractor to extend temporary roadway (as shown in green). Temporary compacted stone material lay down area to be included and maintained until landscaping work is scheduled to begin. Reference Milestone Schedule for more information. Site Work Contractor to relocate all portable fencing at the direction of the CM. Reference Logistics Plans for sequencing and schedule durations.
4. General Trades Contractor to provide dumpsters and temporary toilet facilities for the duration of the secure entrance / main office renovation. Dumpster locations do not represent quantities. Refer to Special Provisions and Scope of Work for dumpster requirements. General Trades Contractor to relocate dumpster locations as work progresses.
5. All contractors to use Gate 1 for entry / exit to site during school hours. Gate 2 to be used for July - August for the secure main entrance / main office work only.
6. All contractors to maintain clear access for temporary main entrance / egress through Fall 2025. Refer to Special Provisions and Scope of work for relocation / temporary provisions for access control by Electrical Contractor.

SL-1
SITE
LOGISTICS
PLAN

AMHERST CENTRAL SCHOOL DISTRICT - PHASE 2
SMALLWOOD ELEMENTARY SCHOOL
300 Smallwood Dr. Amherst, NY 14226

Exhibit C
2/10/2025
