



Citizen-Led Oversight Committee (CLOC) 2023 Bond Referendum

Fifteenth Meeting
(Hilton Head Island High School Media Center and Via Zoom)
June 11, 2025

Pledge of Allegiance





CLOC's Mission

Independently monitor all building projects, schedules, budgets, and expenditures from the Beaufort County School District's Nov. 2023 Bond Referendum, thereby ensuring proper use of Beaufort County taxpayer funds and superior facilities for Beaufort County students.

PRESENTATION AGENDA



1. Pledge of Alleginace
2. Public Comments
3. Approval of Draft CLOC Meeting Minutes from May 14, 2025
4. Glossary of Acronyms
5. May 2025 Master Schedule (No Update)
6. 2023 Bond Referendum Project Updates
7. 2023 Bond Referendum Financial Reports and Summary
 - A. Financial Summary Report
 - B. Project Level Financial Reports
 - C. Contingency Use Log
 - D. Financial Update

PRESENTATION AGENDA



8. 2023 Bond Referendum Cash Flow Projections vs Actual Expenditures
9. 2023 Bond Referendum Community Outreach (No Activity to Report)
10. 2023 Bond Referendum CLOC Sub-Committee Reports/Updates
11. 2023 Bond Referendum Forward Looking Items and Events
12. 2023 Bond Referendum Next Meeting July 9, 2025 (Location TBD)

4. Glossary of Acronyms



Glossary of Acronyms

A/E – Architect/Engineer

ADA – American with Disabilities Act

AHJ – Authority Having Jurisdiction

ATP – Authorization To Proceed

CATE – Career And Technology Education

CD – Construction Documents

CLOC – Citizen-Led Oversight Committee

CM – Construction Manager

CMU – Concrete Masonry Unit

CMAR – Construction Manager At Risk

CTE – Career and Technical Education

DD – Design Development

DOR – Designer Of Record

GMP – Guaranteed Maximum Price

IT – Information Technology

JCS – Jumper Carter Sease Architects

HCM – Hord Coplan Macht

HVAC – Heating, Ventilation and Air Conditioning

LDAC – Little Diversified Architectural Consulting

LGIP – Local Government Investment Pool

LULL – Mfg. of Const. Equipment (combo forklift & tractor)

MBK – M.B. Kahn Construction Co., Inc.

MCT – Marmoleum Composition Tile

MEP – Mechanical Electrical Plumbing

MOA – Memorandum Of Agreement

MOU – Memorandum Of Understanding

Glossary of Acronyms

MWBE – Minority Women-owned Business Enterprises
NTP – Notice To Proceed
OSF – Office of School Facilities, SC Dept. of Education
QAP – Quackenbush Architects and Planners
RFI – Request For Information
RFP – Request For Proposals
RFQ – Request For Qualifications
SD – Schematic Design
TTC – Thompson Turner Construction
VCT – Vinyl Composition Tile



School Acronyms

BCHS – Battery Creek High School

BES – Beaufort Elementary School

BHS – Beaufort High School

BLECC – Bluffton Early Childhood Center

BLES – Bluffton Elementary School

BLHS – Bluffton High School

BLMS – Bluffton Middle School

BMS – Beaufort Middle School

BRES – Broad River Elementary School

CES – Coosa Elementary School

DESC – District Educational Support Center

DIES – Daufuskie Island Elementary School

HEMMS – H.E. McCracken Middle School

HHIECC – Hilton Head Island Early Childhood Center

HHIES – Hilton Head Island Elementary School

HHIHS – Hilton Head Island High School

HHIMS – Hilton Head Island Middle School

HHISCA – Hilton Head Island School for The Creative Arts

JJDELC – James J. Davis Early Learning Center

JSES – Joseph S. Shanklin Elementary School

LIES – Lady's Island Elementary School

LIMS – Lady's Island Middle School

MCRECC – M.C. Riley Early Childhood Center

MCRES – M.C. Riley Elementary School

MOES – Mossy Oaks Elementary School

MRES – May River Elementary School

School Acronyms

MRHS – May River High School
OES – Okatie Elementary School
PRES – Port Royal Elementary School
PVES – Pritchardville Elementary School
RCES – Red Cedar Elementary School
RRA – River Ridge Academy
RSLA – Robert Smalls Leadership Academy
RVCS – Riverview Charter School
SHELC – St. Helena Early Learning Center
SHES – St. Helena Elementary School
WBECHS – Whale Branch Early College High School
WBES – Whale Branch Elementary School
WBMS – Whale Branch Middle School



5. March 2025 Master Schedule (No Update)



6. 2023 Bond Referendum Project Updates



May River Elementary School

(Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
77 – May River Elementary School (AM)	New PreK-5 Elementary School	● 1	●

Status Flag Comments:

1 ● See 2023 Referendum Project Contingency Log for details



May River Elementary School **(Quackenbush Architects and Planners/TTC)**



- Town of Bluffton Land Disturbance Development Permit is scheduled to be received in June 2025
- Work is scheduled to begin shortly after
- Other Item(s) To Note: None at this time


May River High School

(Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
97 – May River High School (AM)	CTE/JROTC Addition and CTE Partial Renovations	●	●

- JROTC Roof Top Units have been installed; Building is dried in, Rough in is progressing
- CTE mezzanine slab is poured; Masonry is 90% complete
- Masonry brick has arrived
- Other Item(s) To Note: None at this time

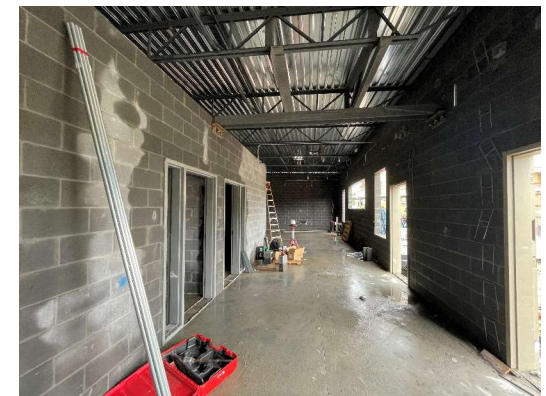

New Early Learning Center (Hord Coplan Macht/McKnight Construction Co., Inc.)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
79 – New Early Learning Center (AM)	New Early Learning Center Construction (RRA Campus)	●	●

- Second public reading for the annexation and rezoning is scheduled to occur on June 10, 2025
- SD's are scheduled to be received in June 2025
- Other Item(s) To Note: None at this time

Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
96 – Hilton Head Island High School (TS)	New Construction, Renovations and Demolition	●	●



Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



Phase 1: Contractual Substantial Completion date is June 19, 2026

- Site Work: Scope is proceeding on schedule
- Phase 1A: Scope includes construction of a 3-story classroom addition (approximately 144,000 SF) and a mechanical support building; Section "A" sheetrock, Glazing is complete; Section "B" framing is complete; Ceiling grid is scheduled to begin in June; Section "C" framing is complete; Ceiling grid is scheduled to begin in June
- Phase 1B: Scope includes selective demolition and initial renovations of the "D" wing (Music & Art), group restroom improvements, and modifications of corridor walls and finishes; Phase 1B construction has begun

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 1 May 2025 Progress Photos



Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 1 May 2025 Progress Photos



Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



Phase 2: Substantial Completion date to be established in Q1 2025 when GMP Proposal is approved

- Phase 2 scope includes the demolition of the "B" and "C" wings (Academic Spaces); Construction of a new cafeteria and CTE addition; Remaining renovations/improvements for the "D" wing (Music and Fine Arts); New parking lot and courtyard
- 100% Construction Documents (CD's) have been received and issued to MBK for GMP pricing
- GMP Proposal is scheduled to be received in June 2025

Hilton Head Island High School

(Little Diversified Architectural Consulting, Inc./MBK)



Phase 3: Substantial Completion date to be established in Q1 2025 when GMP Proposal is approved

- Phase 3 scope includes renovation of both existing gymnasiums, existing JROTC and existing cafeteria
- 100% Construction Documents (CD's) have been received and issued to MBK for GMP pricing
- GMP Proposal is scheduled to be received in June 2025

Hilton Head Island High School (Little Diversified Architectural Consulting, Inc./MBK)



Phase 4: Substantial Completion date to be established in Q1 2025 when GMP Proposal is approved

- Phase 4 scope includes renovation of the existing Performing Arts Center (PAC)
- 100% Construction Documents (CD's) have been received and issued to MBK for GMP pricing
- GMP Proposal is scheduled to be received in June 2025

Beaufort High School

(Jumper Carter Sease Architects/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
90 – Beaufort High School (MK)	CTE Addition and Renovations	●	●



Beaufort High School

(Jumper Carter Sease Architects/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
90 – Beaufort High School (MK)	CTE Addition and Renovations	●	●

- DD's Pricing has been received; Meeting is being coordinated to review pricing
- Other Item(s) To Note: None at this time

Lady's Island Middle School

(Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
81 – Lady's Island Middle School Replacement (MK)	Phase 1 – New School Construction	●	●
	Phase 2 – Demo Existing School	●	●
	Phase 3 – New Athletics (Football, Softball and Baseball Fields, Lighting, Track, Restrooms, Concessions and Storage Facilities	●	●



Lady's Island Middle School

(Quackenbush Architects and Planners/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
81 – Lady's Island Middle School Replacement (MK)	Phase 1 – New School Construction	●	●
	Phase 2 – Demo Existing School	●	●
	Phase 3 – New Athletics (Football, Softball and Baseball Fields, Lighting, Track, Restrooms, Concessions and Storage Facilities	●	●

- SD's have been received; TTC is pricing the SD's; Estimate is scheduled to be received in June 2025
- Second reading at city council is scheduled to occur on June 10, 2025
- Other Item(s) To Note: None at this time

Port Royal Elementary School

(Jumper Carter Sease Architects/TTC)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
38 – Port Royal Elementary School (MK)	HVAC Replacements	●	●

- Units are scheduled to arrive in June 2025; Completion is scheduled to occur in June 2025
- Other Item(s) To Note: None at this time

Technology Warehouse & Imaging Center (Jumper Carter Sease Architects/Shoreline Construction)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
01 – District Educational Services Center (MK)	Technology Warehouse & Imaging Center	●	●

Status Flag Comments:

1 ● See 2023 Referendum Project Contingency Log for details

- Sitework and utilities continue to progress; Site work completion is scheduled to occur in August 2025
- Structure is in queue for production
- Other Item(s) To Note: None at this time

Whale Branch Elementary School

(Jumper Carter Sease Architects/Ajax Building Co.)



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
54 – Whale Branch Elementary School (MK)	HVAC Replacements	●	●

- HVAC installation is scheduled to occur during Summer 2025
- Other Item(s) To Note: None at this time

Safety/Security Improvements



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
44 – Joseph S. Shanklin Elementary School (BF)	Cameras at Parking Lots & Playgrounds, Access Controls, Intrusion Alarm	●	●
83 – Robert Smalls Leadership Academy (AM)	Cameras at Parking Lots, Playgrounds & Athletic Fields, Access Controls, Intrusion Alarm	●	●
87 – Hilton Head Island Middle School (TS)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm – COMPLETED	●	●
90 – Beaufort High School (MK)	Cameras at Parking Lots & Athletic Fields, Access Controls, Intrusion Alarm	●	●

- JSES: Precast bases and camera poles are being installed
- RSLA: Precast bases and camera poles are being installed
- BHS: Precast bases and camera poles are being installed

School Furniture Replacements



School Code - Project (Project Manager)	2023 Bond Referendum Scope	Budget	Schedule
37 – Mossy Oaks Elementary School (FL)	Furniture Replacements: Phase 1 – COMPLETED Phase 2 (Summer Break 2025)	●	●
38 – Port Royal Elementary School (FL)	Furniture Replacements: Phase 1 – COMPLETED Phase 2 (Summer Break 2025)	●	●
44 – Joseph S. Shanklin Elementary School (FL)	Furniture Replacements: Phase 1 – COMPLETED Phase 2 (Summer Break 2025)	●	●

- Phase 2 Classroom furniture for MOES, PRES and JSES Related Arts classes, Special Education Classes and Resource Rooms is being postponed for replacement to occur during Summer Break 2025
- Other Item(s) To Note: Phase 2 Furniture replacements are scheduled to take place during Summer Break 2025 to accommodate for the Principal requests to avoid disruptions during the school year

7. 2023 Bond Referendum Financial Reports and Summary





2023 Bond Referendum Financial Reports and Summary

A. Financial Summary Report

- See handout/attachment for details

B. Project Level Financial Reports

- See handout/attachment for details

C. Contingency Use Log

- See handout/attachment for details

2023 Bond Referendum Financial Reports and Summary

FINANCIAL SUMMARY ●



Budget Summary 05/31/25

Beginning Original Budget
Current Budget

\$439,035,000
\$439,035,000

Paid and Committed Through 05/31/25

\$183,874,787 (41.88%)

Total Remaining Funds to Commit (Including Program Contingency)

\$255,160,213 (58.12%)

Program Contingency Activity in May 2025

Savings Returned
Contingency Used

\$22,098
\$0

Program Contingency Remaining

\$11,746,970

Original Project Level Contingencies
Current Project Level Contingencies

\$17,060,756
\$13,652,014

8. 2023 Bond Referendum Cash Flow Projections vs Actual Expenditures





2023 Bond Referendum Cashflow Projections vs Actual

CASH FLOW: DATA thru May 2025																
2023 BOND REFERENDUM ONLY																
Projects	Project Total (Millions)	Previously Spent	January	February	March	April	May	June	July	August	Sept	October	Nov	Dec	Total	% Project Budget
Safety/Security & Tech. Enhancement Projects	\$17.95	\$0.23	\$0.00	\$0.00	\$0.46	\$0.89	\$1.40	\$0.71	\$0.48	\$0.29	\$0.09	\$0.07	\$0.09	\$0.21	\$4.91	27.38%
Technology Warehouse & Imaging Center	\$3.33	\$0.06	\$0.00	\$0.00	\$0.00	\$0.00	\$0.10	\$0.03	\$0.03	\$0.30	\$0.52	\$0.40	\$0.72	\$0.36	\$2.51	75.47%
Right Choices Kitchen Addition	\$2.32	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.02	\$0.00	\$0.00	\$0.00	\$0.00	\$0.03	\$0.00	\$0.00	\$0.05	2.12%
Riverview Charter School Gym Addition & Reno	\$17.92	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.17	\$0.00	\$0.23	\$0.00	\$0.00	\$0.00	\$0.00	\$0.41	2.26%
New - May River Elementary	\$58.74	\$1.67	\$0.00	\$0.00	\$0.53	\$1.86	\$1.61	\$2.83	\$3.19	\$3.89	\$4.45	\$3.68	\$4.87	\$3.17	\$31.75	54.04%
New Early Learning Center (RRA Campus)	\$27.77	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.26	\$0.00	\$0.00	\$0.00	\$0.34	\$0.00	\$0.00	\$0.00	\$0.60	2.16%
New Lady's Island Middle & Demo Old School	\$61.51	\$0.23	\$0.00	\$0.23	\$0.00	\$0.00	\$0.34	\$0.00	\$0.00	\$0.00	\$0.00	\$0.57	\$0.00	\$0.00	\$1.38	2.24%
Hilton Head Island High New Const., Reno & Demo	\$157.52	\$8.75	\$1.31	\$4.83	\$0.96	\$0.96	\$1.91	\$2.15	\$2.41	\$3.02	\$3.01	\$3.37	\$3.78	\$5.40	\$41.85	26.57%
School Furniture Replacement	\$1.81	\$0.63	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1.17	\$0.00	\$0.00	\$0.00	\$1.81	100.00%
HVAC Replacements	\$16.36	\$0.38	\$0.00	\$0.00	\$0.15	\$0.16	\$0.07	\$0.16	\$0.68	\$0.83	\$0.79	\$0.31	\$0.14	\$0.11	\$3.78	23.09%
Beaufort High CTE New Const. & Reno	\$7.66	\$0.07	\$0.07	\$0.00	\$0.09	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.20	\$0.00	\$0.43	5.61%
May River High CTE New Const. & Reno	\$16.21	\$0.10	\$0.00	\$0.00	\$0.02	\$0.64	\$0.57	\$0.53	\$1.02	\$0.88	\$0.96	\$1.20	\$1.17	\$2.05	\$9.13	56.35%
Bluffton High CTE New Const.	\$11.90	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.11	\$0.00	\$0.00	\$0.15	\$0.00	\$0.00	\$0.26	2.19%
Parking Lot Reconfiguration & Paving Projects	\$13.37	\$0.88	\$0.00	\$0.00	\$0.00	\$0.00	\$0.04	\$0.04	\$0.03	\$0.00	\$0.00	\$0.00	\$0.00	\$0.26	\$1.24	9.31%
Sub-Total (Including District Level Costs)	\$439.04	\$13.87	\$1.39	\$5.71	\$2.80	\$4.95	\$6.78	\$7.08	\$8.43	\$9.89	\$11.89	\$10.24	\$11.44	\$12.04		
Forecasted Total			\$15.26	\$20.98	\$23.77	\$28.72	\$35.50	\$42.58	\$51.01	\$60.90	\$72.79	\$83.03	\$94.48	\$106.51		
Actual Spent			\$17.41	\$19.18	\$25.05	\$31.07	\$42.45									

Total Funding	\$439,035,000	(BAN sale closed on 8/29/24)
Total of Bond Sales to Date	\$50,000,000	(1st Bond Sale closed on 2/13/25 - Total Amount \$50.3M)

9. 2023 Bond Referendum Community Outreach (No Activity to Report)



10. 2023 Bond Referendum CLOC Sub- Committee Reports/ Updates



11. 2023 Bond Referendum Forward Looking Items and Events



12. 2023 Bond
Referendum
Next Meeting
July 9, 2025
(Location TBD)





Citizen-Led Oversight Committee (CLOC) 2023 Bond Referendum

Fifteenth Meeting
(Hilton Head Island High School Media Center and Via Zoom)
June 11, 2025
