



**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

31

Week of: 6/2/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- Band Addition/Remodel
 - Monarch finished paving parking lots at area B & E.
 - Monarch completed line painting in parking lots at area B & E.
 - Rhom completed TB, MB/Hardware & casework reinstall.
 - Subs completed pre-punch list items in band addition & remodel.
 - Architect & Owner Punch List walk was completed 6/4.
- Auditorium Remodel
 - Subs continued MEP rough in in auditorium.
 - ICS started installing ceiling cloud structure steel & framing in auditorium.
- Memorial High Schools last day was 6/6.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- Band Addition/Remodel
 - Occupancy inspection to happen on 6/9.
- Auditorium Remodel
 - Subs to continue MEP rough-ins.
 - RJP to begin dryfall painting structure.
 - ICS to continue to complete ceiling cloud framing.
 - Tweet Garot to start chiller replacement.
 - ICS to begin side catwalk structure installation.
- Commons Addition/Remodel
 - Rhom to start demolition of fixtures/ACT/walls & frames

Project Manager: Jordan Lieftring

(715) 579-0176


jlieftring@market-johnson.com


Superintendent: Josh Snyder

(715) 450-4508

jsnyder@market-johnson.com

Weekly Photos

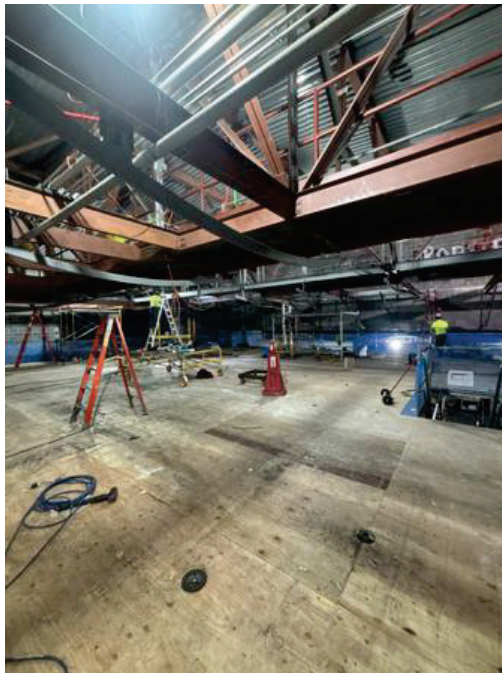

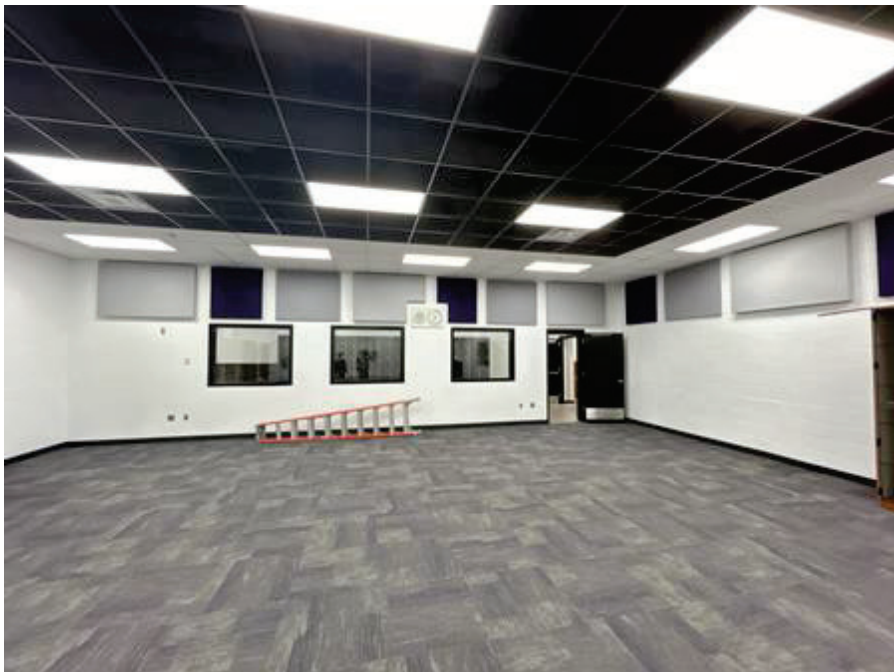



**Market &
Johnson**

Adding Value to Everything We Do

ECASD Memorial HS Additions & Alterations

31

Week of: 6/2/2025

