

# HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



## School Site Improvement Projects

Regular Board Meeting  
June 24, 2025

### Business Services



# PROJECT COMPLETE LIST

## 2024/2025



Site	Item Description	Funding Source	Completed Date
Wedgeworth Elementary	K-5 Permanent School	COPS	06/2025
Amar Center	Phase II of Re-Roofing	Child Development	4/2025
Baldwin Academy	Administration Floor	Facilities	4/2025
Fairgrove Academy	Multipurpose Room Floor	Facilities	4/2025
Orange Grove Middle School	Classroom Floor	Facilities	4/2025
Orange Grove Middle School	Driveway Repair	Facilities	4/2025
Sparks Middle School	Irrigation Project/ Tree Planting	Facilities	4/2025
Wilson High School	Locker Room	Facilities	4/2025
Los Altos High School	Countertops	Facilities	2/2025
Workman Elementary School	Student Restroom Floor	Facilities	2/2025
Baldwin Academy	Restripping	Facilities	2/2025
Newton Middle School	Fence Installation	Facilities	2/2025
Los Altos High School	Paint Refresh	Facilities	2/2025
Valley High School	Paint Refresh	Facilities	2/2025
Wilson High School	Classroom Sound Abatement	Facilities	2/2025

# Projects Completed as of June 24, 2025


## Baldwin Academy – Administration Floor

**NEW!**

**BEFORE**



**AFTER**

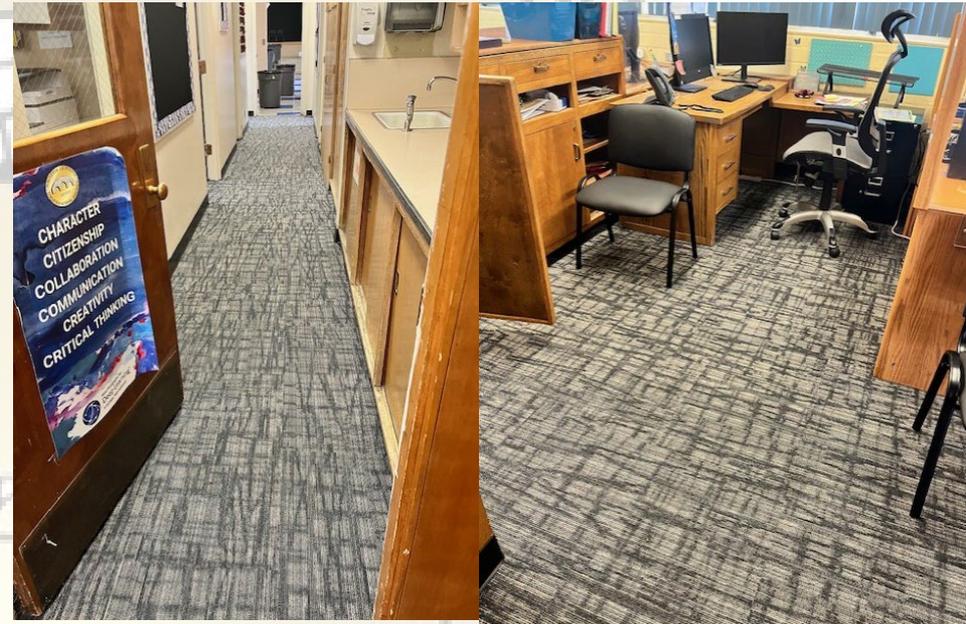

ED SCHOOL DIS

# Projects Completed as of June 24, 2025


## Fairgrove Academy – MPR Floor

**NEW!**

**BEFORE**



**AFTER**

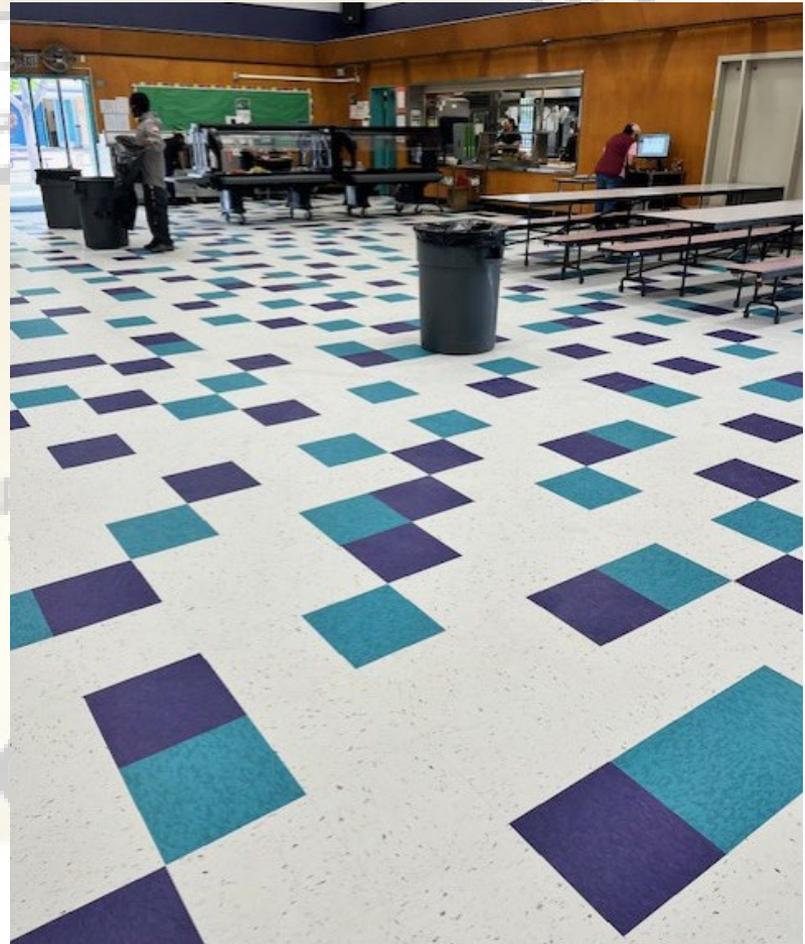

# Projects Completed as of June 24, 2025

## Orange Grove Middle School – Classroom Floor

**NEW!**

**BEFORE**



**AFTER**



# Projects Completed as of June 24, 2025


## Orange Grove Middle School – Driveway Repair

**NEW!**

**BEFORE**



**AFTER**

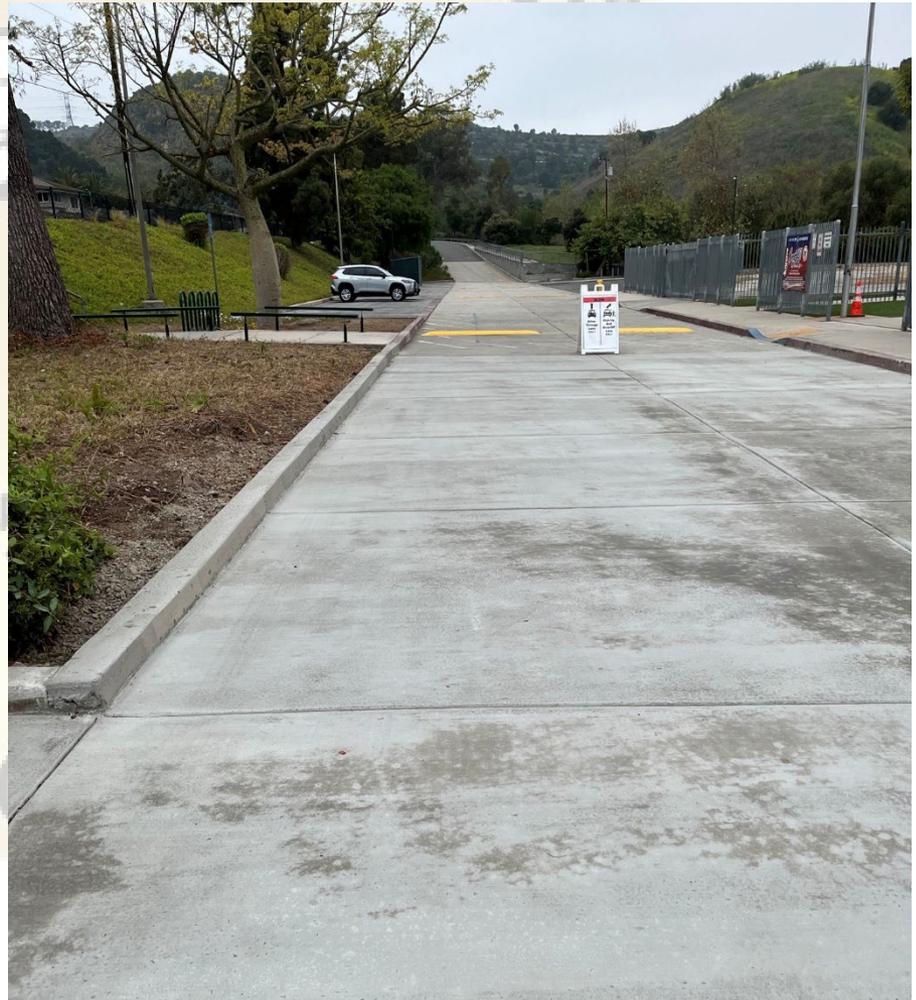

# Projects In Progress

2024-2025



# Projects in Progress as of June 24, 2025

## Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	TBD
District Office	Restroom Renovations	Pending	N/A	TBD	TBD	Facilities	TBD
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	Complete	In Progress	ESSR	12/2026
<b>Fairgrove Academy</b>	<b>Phase III of Re-Roofing</b>	<b>N/A</b>	<b>N/A</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>
La Puente High School	Custom Shade Structure	Complete	Approved	Complete	In Progress	Surplus Property Sales	12/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD
<b>Los Molinos Elementary School</b>	<b>Phase III of Re-Roofing</b>	<b>N/A</b>	<b>N/A</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>
<b>Palm Elementary School</b>	<b>Phase III of Re-Roofing</b>	<b>N/A</b>	<b>N/A</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>
<b>Palm Elementary School</b>	<b>Fire Alarms</b>	<b>Complete</b>	<b>Complete</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>
<b>Sparks Middle School</b>	<b>Phase III of Re-Roofing</b>	<b>N/A</b>	<b>N/A</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>
<b>Wing Lane Elementary School</b>	<b>Fire Alarms</b>	<b>Complete</b>	<b>Complete</b>	<b>Complete</b>	<b>In Progress</b>	<b>Facilities</b>	<b>11/2025</b>

Changes And Progress Since Last Report - Blue

# Projects in Progress as of June 24, 2025

## Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wilson High School	Media Center	Pending	N/A	Complete	TBD	Grant	10/2026
Wilson High School	Stadium Press Box & Bleachers	Complete	Complete	Complete	Pending	General Fund	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	General Fund/ Surplus Property Sales	12/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD

# Projects in Progress as of June 24, 2025

## Wilson High School – Media Center

**NEW!**



# Projects in Progress as of June 24, 2025

## Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Complete	In Progress	Child Development	07/2025
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Complete	Pending	TBD	TBD	Child Development	TBD

# Projects in Progress as of June 24, 2025

## Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Front Entry Alterations & Conference Hall	Complete	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	Complete	In Progress	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	Complete	In Progress	Adult Ed	TBD

# Projects in Progress as of June 24, 2025


## Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Complete	07/2025	Food Services	08/2025
District Office	Warehouse Freezer	Complete	NA	Complete	In Progress	Food Services	10/2025
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Complete	In Progress	Food Services	09/2025
Wilson High School	Kitchen Modernization	Pending	TBD	TBD	TBD	Surplus Property Sales	TBD

# Projects in Progress as of June 24, 2025

## District Office – Warehouse Freezer


**NEW!**

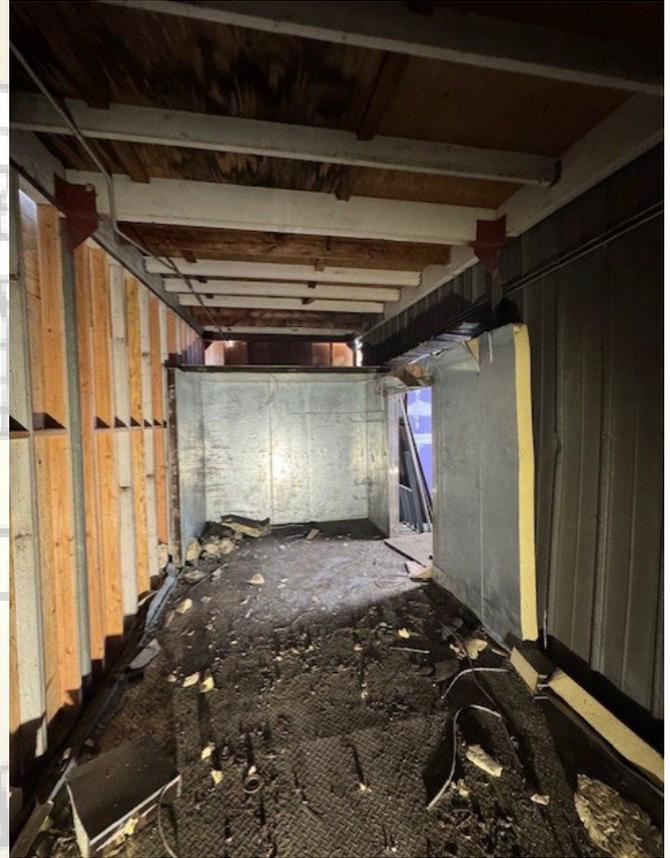

# Projects in Progress as of June 24, 2025

## Mesa Robles – Kitchen Renovation

**NEW!**

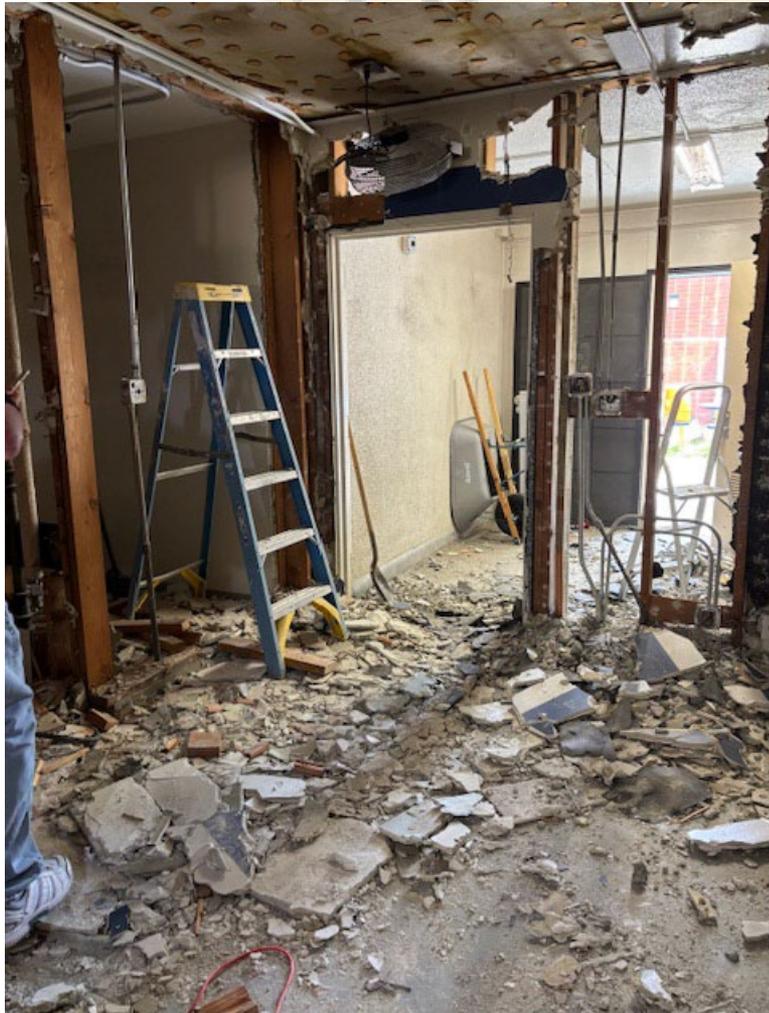



**Next Report – July 17, 2025**
