

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
June 24, 2025

Business Services



PROJECT COMPLETE LIST

2024/2025



Site	Item Description	Funding Source	Completed Date
Wedgeworth Elementary	K-5 Permanent School	COPS	06/2025
Amar Center	Phase II of Re-Roofing	Child Development	4/2025
Baldwin Academy	Administration Floor	Facilities	4/2025
Fairgrove Academy	Multipurpose Room Floor	Facilities	4/2025
Orange Grove Middle School	Classroom Floor	Facilities	4/2025
Orange Grove Middle School	Driveway Repair	Facilities	4/2025
Sparks Middle School	Irrigation Project/ Tree Planting	Facilities	4/2025
Wilson High School	Locker Room	Facilities	4/2025
Los Altos High School	Countertops	Facilities	2/2025
Workman Elementary School	Student Restroom Floor	Facilities	2/2025
Baldwin Academy	Restripping	Facilities	2/2025
Newton Middle School	Fence Installation	Facilities	2/2025
Los Altos High School	Paint Refresh	Facilities	2/2025
Valley High School	Paint Refresh	Facilities	2/2025
Wilson High School	Classroom Sound Abatement	Facilities	2/2025

Projects Completed as of June 24, 2025


Baldwin Academy – Administration Floor



BEFORE



AFTER

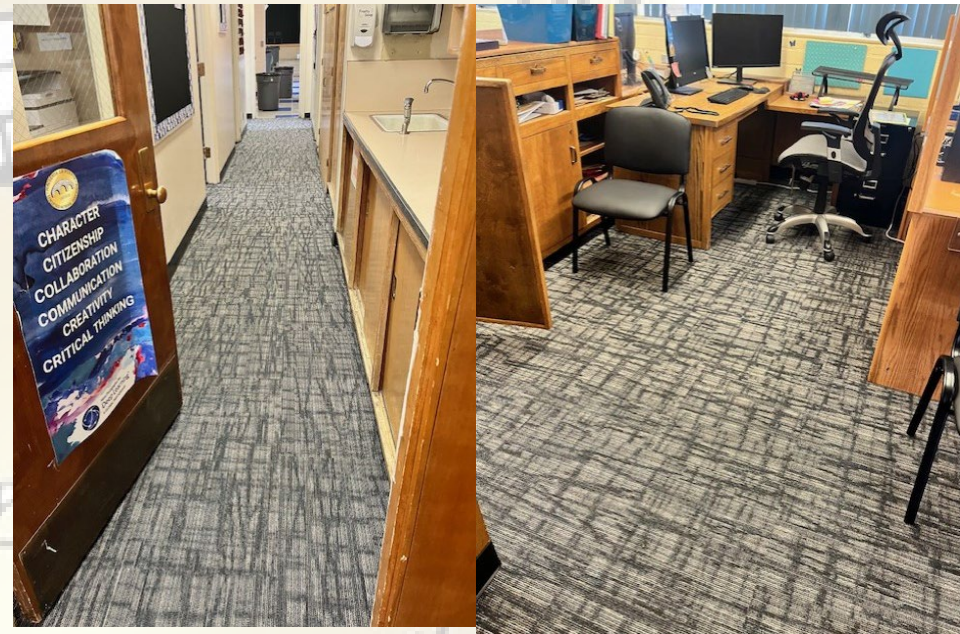

Projects Completed as of June 24, 2025


Fairgrove Academy – MPR Floor



BEFORE



AFTER

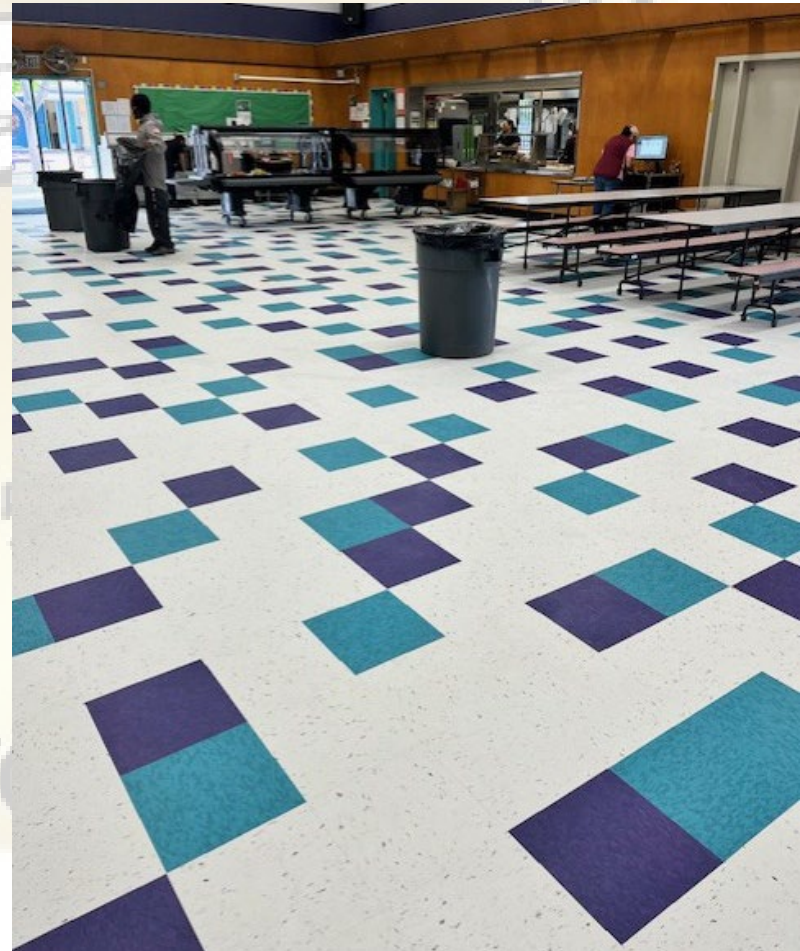

Projects Completed as of June 24, 2025

Orange Grove Middle School – Classroom Floor



BEFORE



AFTER





Projects Completed as of June 24, 2025

Orange Grove Middle School – Driveway Repair

BEFORE



AFTER



Projects In Progress

2024-2025



Projects in Progress as of June 24, 2025

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	TBD
District Office	Restroom Renovations	Pending	N/A	TBD	TBD	Facilities	TBD
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	Complete	In Progress	ESSR	12/2026
Fairgrove Academy	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
La Puente High School	Custom Shade Structure	Complete	Approved	Complete	In Progress	Surplus Property Sales	12/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD
Los Molinos Elementary School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Palm Elementary School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Palm Elementary School	Fire Alarms	Complete	Complete	Complete	In Progress	Facilities	11/2025
Sparks Middle School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Wing Lane Elementary School	Fire Alarms	Complete	Complete	Complete	In Progress	Facilities	11/2025

Changes And Progress Since Last Report - Blue

Projects in Progress as of June 24, 2025

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wilson High School	Media Center	Pending	N/A	Complete	TBD	Grant	10/2026
Wilson High School	Stadium Press Box & Bleachers	Complete	Complete	Complete	Pending	General Fund	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	General Fund/ Surplus Property Sales	12/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD

Projects in Progress as of June 24, 2025

Wilson High School – Media Center



Projects in Progress as of June 24, 2025

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Complete	In Progress	Child Development	07/2025
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Complete	Pending	TBD	TBD	Child Development	TBD

Projects in Progress as of June 24, 2025

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Front Entry Alterations & Conference Hall	Complete	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	Complete	In Progress	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	Complete	In Progress	Adult Ed	TBD

Projects in Progress as of June 24, 2025


Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Complete	07/2025	Food Services	08/2025
District Office	Warehouse Freezer	Complete	NA	Complete	In Progress	Food Services	10/2025
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Complete	In Progress	Food Services	09/2025
Wilson High School	Kitchen Modernization	Pending	TBD	TBD	TBD	Surplus Property Sales	TBD

Projects in Progress as of June 24, 2025

District Office – Warehouse Freezer

NEW!

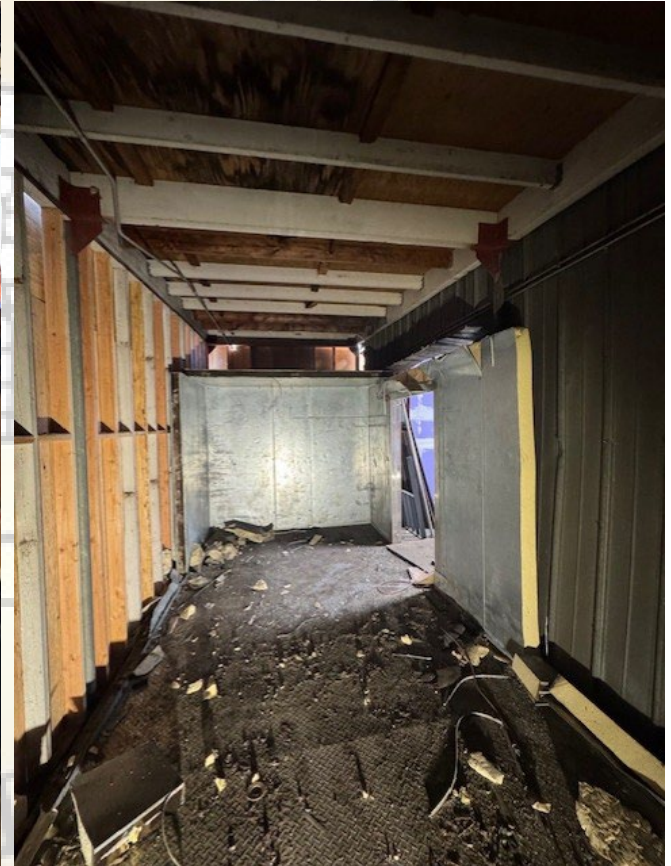



Projects in Progress as of June 24, 2025

Mesa Robles – Kitchen Renovation





Next Report – July 17, 2025
