



WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- Auditorium Remodel
 - Rhom completed ceiling cloud framing.
 - Rhom continued ceiling cloud drywall.
 - Norcostco completed projection screen rough ins.
 - RJP continued taping & applying VWC to ceiling clouds.
 - Subs continued MEP/AV-low voltage rough ins.
- Commons Addition/Remodel
 - Rhom continued floor demo.
 - Rhom continued reworking new wall openings.
 - Subs continued MEP rough ins.
- Little Theater
 - RJP continued wall painting/patching.
 - Norcostco demoed stage curtains.
- Choir Room
 - Tweet Garot demoed unit ventilators.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- Auditorium Remodel
 - Rhom to continue ceiling cloud drywall.
 - RJP to continue taping & applying VWC to ceiling clouds.
 - Subs to continue MEP/AV-low voltage rough ins.
 - Rhom to start side wall cloud framing & drywall.
 - Subs to start MEP fixtures & punch list.
 - Tweet Garot to complete chiller factory start-up.
- Commons Addition/Remodel
 - Rhom to continue floor demo.
 - Rhom to continue reworking new wall openings.
 - Rhom to start OH door rough in & ACT grid install.



Market & Johnson

ECASD Memorial HS Additions & Alterations

Adding Value to Everything We Do

35

Week of: 6/30/2025

- Subs to continue MEP rough ins.
- Little Theater
 - RJP to continue wall painting/patching.
- Choir Room
 - Cutting Edge to start & complete demo concrete risers.

Project Manager: Jordan Lieffring

(715) 579-0176

jlieffring@market-johnson.com

Superintendent: Josh Snyder

(715) 450-4508

jsnyder@market-johnson.com

Weekly Photos





**Market &
Johnson**

Adding Value to Everything We Do


ECASD Memorial HS Additions & Alterations

35

Week of: 6/30/2025





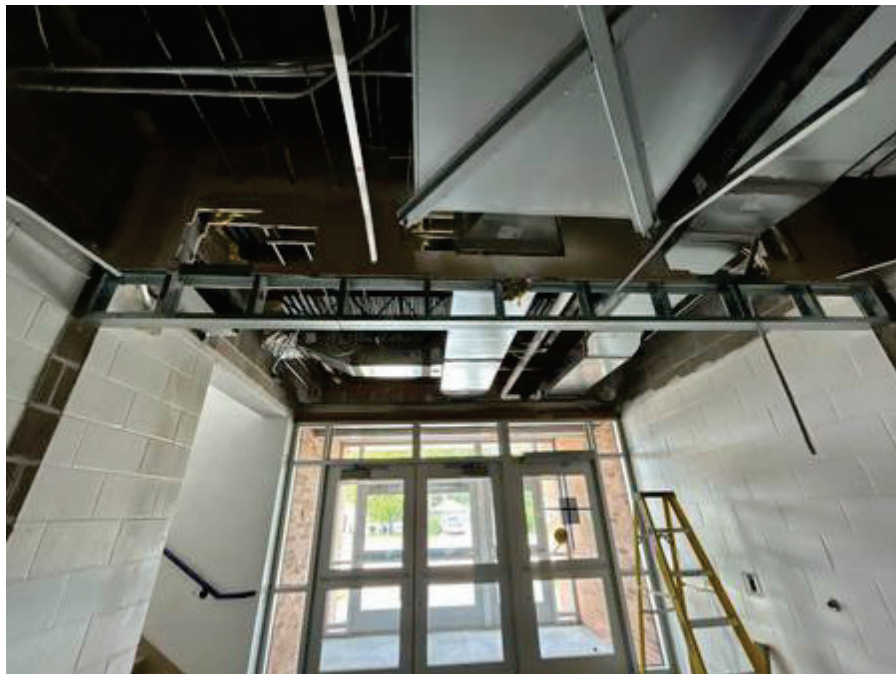

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- M&J carpenters completed soffit & wall framing.
- M&J carpenters started installing drywall.
- Subs continued MEP wall & overhead rough ins.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- M&J carpenters to continue installing drywall.
- Subs to finish MEP wall & overhead rough ins.
- RJP to start tape & paint on walls & soffits.

Weekly Photos



