
WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- Forum/Old Weight room
 - M&J completed soffit & wall framing.
 - M&J started hanging drywall.
 - Subs completed wall & overhead rough ins.
- Art Rooms
 - Subs completed MEP rough ins.
 - Subs installed structural steel for skylights.
- Gym Corridor
 - M&J carpenters began framing & setting HM frames.

Upcoming Week


Market & Johnson to supervise and coordinate with trades.

- Forum/Old Weight room
 - M&J to continue hanging drywall.
 - Kumplete Dec. to start tape, finish, & paint.
- Art Rooms
 - M&J to frame & drywall chases.
 - Kumplete Dec. to start tape, finish, & paint.
 - C&A to complete skylight roof tie ins.

Weekly Photos





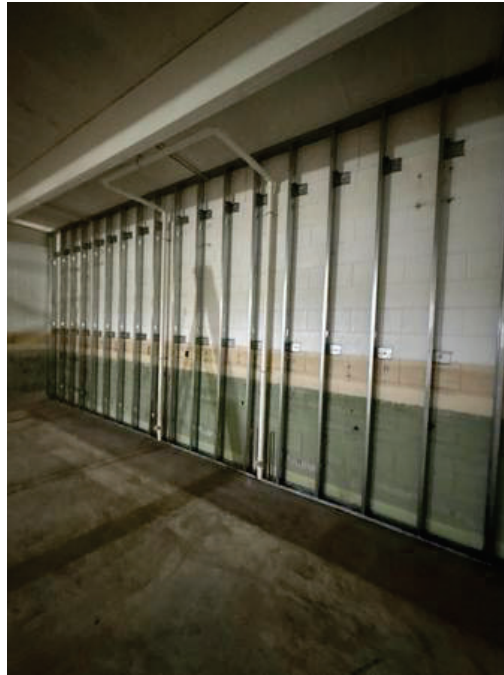



**Market &
Johnson**

Adding Value to Everything We Do

ECASD North HS Media Center Alterations

5

Week of: 6/30/2025

WEEKLY PROJECT UPDATE

Current Week

Market & Johnson supervised and coordinated with trades.

- M&J completed drywall install on ceiling/soffit.
- M&J continued drywall install on stud walls.
- M&J completed installation of backing.
- Subs continued MEP rough ins.

Upcoming Week

Market & Johnson to supervise and coordinate with trades.

- M&J to complete drywall install on stud walls.
- RJP to start tape, finish, & paint.
- Subs to complete MEP rough ins.

Priority Submittals

- #26 28 16-1 Revision 0: Enclosed Switches & Circuit Breakers

Project Manager: Jordan Lieftring

(715) 579-0176

jlieffring@market-johnson.com

Superintendent:



**Market &
Johnson**

Adding Value to Everything We Do

ECASD North HS Media Center Alterations

5

Week of: 6/30/2025



Weekly Photos

