

# HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



## School Site Improvement Projects

Regular Board Meeting  
July 17, 2025

## Business Services



# PROJECT COMPLETE LIST

## 2024/2025



Site	Item Description	Funding Source	Completed Date
Workman Elementary	K1 & K2 Classroom Floor	Facilities	06/2025
Amar Center	Phase II of Re-Roofing	Child Development	4/2025
Baldwin Academy	Administration Floor	Facilities	4/2025
Fairgrove Academy	Multipurpose Room Floor	Facilities	4/2025
Orange Grove Middle School	Classroom Floor	Facilities	4/2025
Orange Grove Middle School	Driveway Repair	Facilities	4/2025
Sparks Middle School	Irrigation Project/ Tree Planting	Facilities	4/2025
Wilson High School	Locker Room	Facilities	4/2025
Los Altos High School	Countertops	Facilities	2/2025
Workman Elementary School	Student Restroom Floor	Facilities	2/2025
Baldwin Academy	Restriping	Facilities	2/2025
Newton Middle School	Fence Installation	Facilities	2/2025
Los Altos High School	Paint Refresh	Facilities	2/2025
Valley High School	Paint Refresh	Facilities	2/2025

# Projects Completed as of July 17, 2025


## Workman Elementary- Classroom Floor



**BEFORE**



**AFTER**

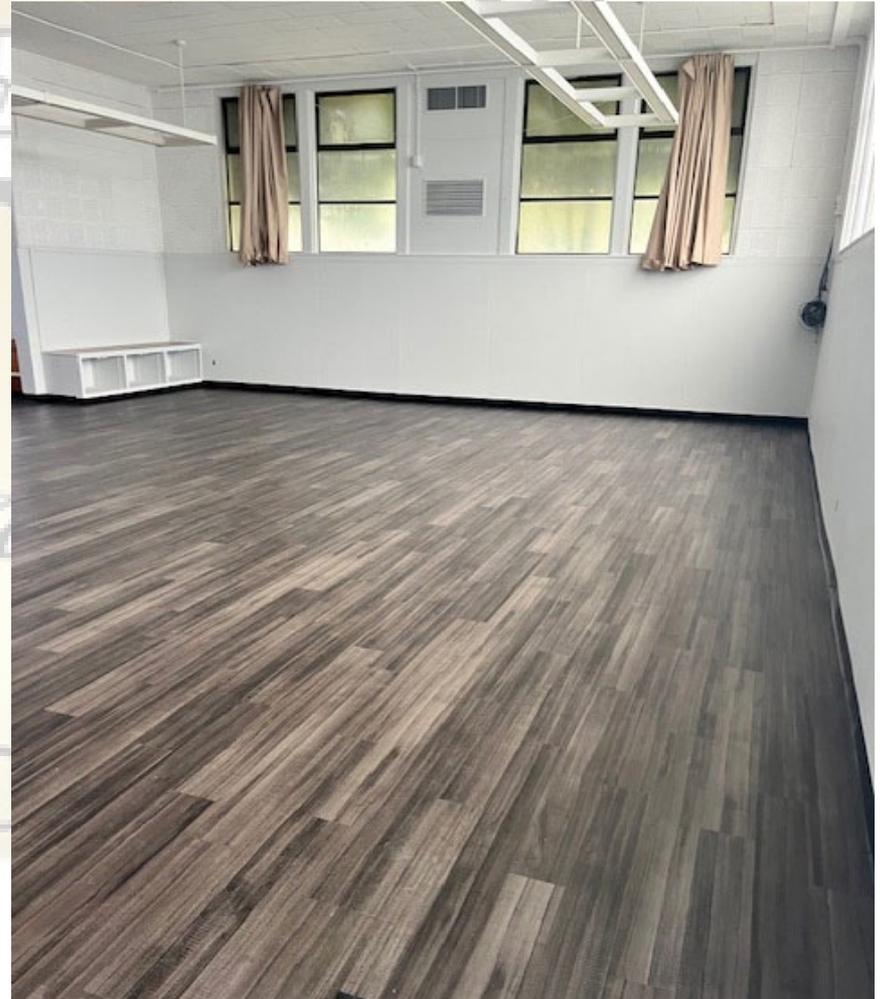

# Projects In Progress

2025-2026



# Projects in Progress as of July 17, 2025

## Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	08/2025
District Office	Restroom Renovations	Pending	N/A	TBD	TBD	Facilities	TBD
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	Complete	In Progress	ESSR	12/2026
Fairgrove Academy	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
La Puente High School	Custom Shade Structure	Complete	Approved	Complete	In Progress	Surplus Property Sales	08/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD
Los Molinos Elementary School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Palm Elementary School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Palm Elementary School	Fire Alarms	Complete	Complete	Complete	In Progress	Facilities	11/2025
Sparks Middle School	Phase III of Re-Roofing	N/A	N/A	Complete	In Progress	Facilities	11/2025
Wing Lane Elementary School	Fire Alarms	Complete	Complete	Complete	In Progress	Facilities	11/2025

Changes And Progress Since Last Report - Blue

# Projects in Progress as of July 17, 2025

## Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Wilson High School	ADA Restrooms	Complete	Complete	Complete	In Progress	Facilities	08/2025
Wilson High School	Media Center	Pending	N/A	Complete	TBD	Grant	10/2025
Wilson High School	Stadium Press Box & Bleachers	Complete	Complete	Complete	Pending	General Fund	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	General Fund/ Surplus Property Sales	11/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD

# Projects in Progress as of July 17, 2025

## La Puente High School – Shade Structure

**NEW!**



# Projects in Progress as of July 17, 2025

## Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Complete	In Progress	Child Development	07/2025



# Projects in Progress as of July 17, 2025

## Amar Center – Entry Security Project



# Projects in Progress as of July 17, 2025


## Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Front Entry Alterations & Conference Hall	Complete	NA	In Progress	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	Complete	In Progress	Adult Ed	08/2025
Willow Adult Ed	Marquee	Complete	NA	Complete	In Progress	Adult Ed	08/2025

# Projects in Progress as of July 17, 2025

## Willow Adult Education – Dental Office

**NEW!**

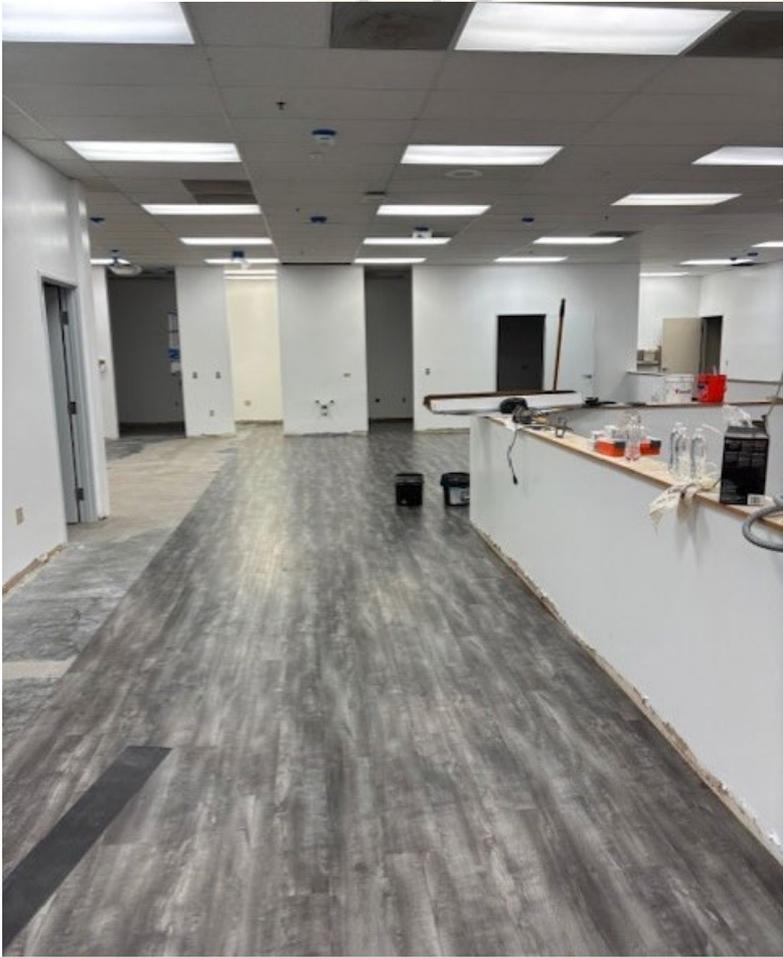

# Projects in Progress as of July 17, 2025

## Willow Adult Education – Marquee

**NEW!**



# Projects in Progress as of July 17, 2025

## Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Complete	In Progress	Food Services	08/2025
District Office	Warehouse Freezer	Complete	NA	Complete	In Progress	Food Services	10/2025
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Complete	In Progress	Food Services	11/2025
Wilson High School	Kitchen Modernization	Pending	TBD	TBD	TBD	Surplus Property Sales	TBD

# Projects in Progress as of July 17, 2025

## District Office – Warehouse Freezer

**NEW!**




# Projects in Progress as of July 17, 2025

## Mesa Robles – Kitchen Renovation

**NEW!**



The background features a large, faded circular logo for Unifield School District. The logo contains a central illustration of a building with three arches, the year '1970' below it, and the text 'UNIFIELD SCHOOL DISTRICT' around the perimeter. A horizontal bar with a green-to-yellow gradient is positioned at the top of the page.

**Next Report – August 28, 2025**
