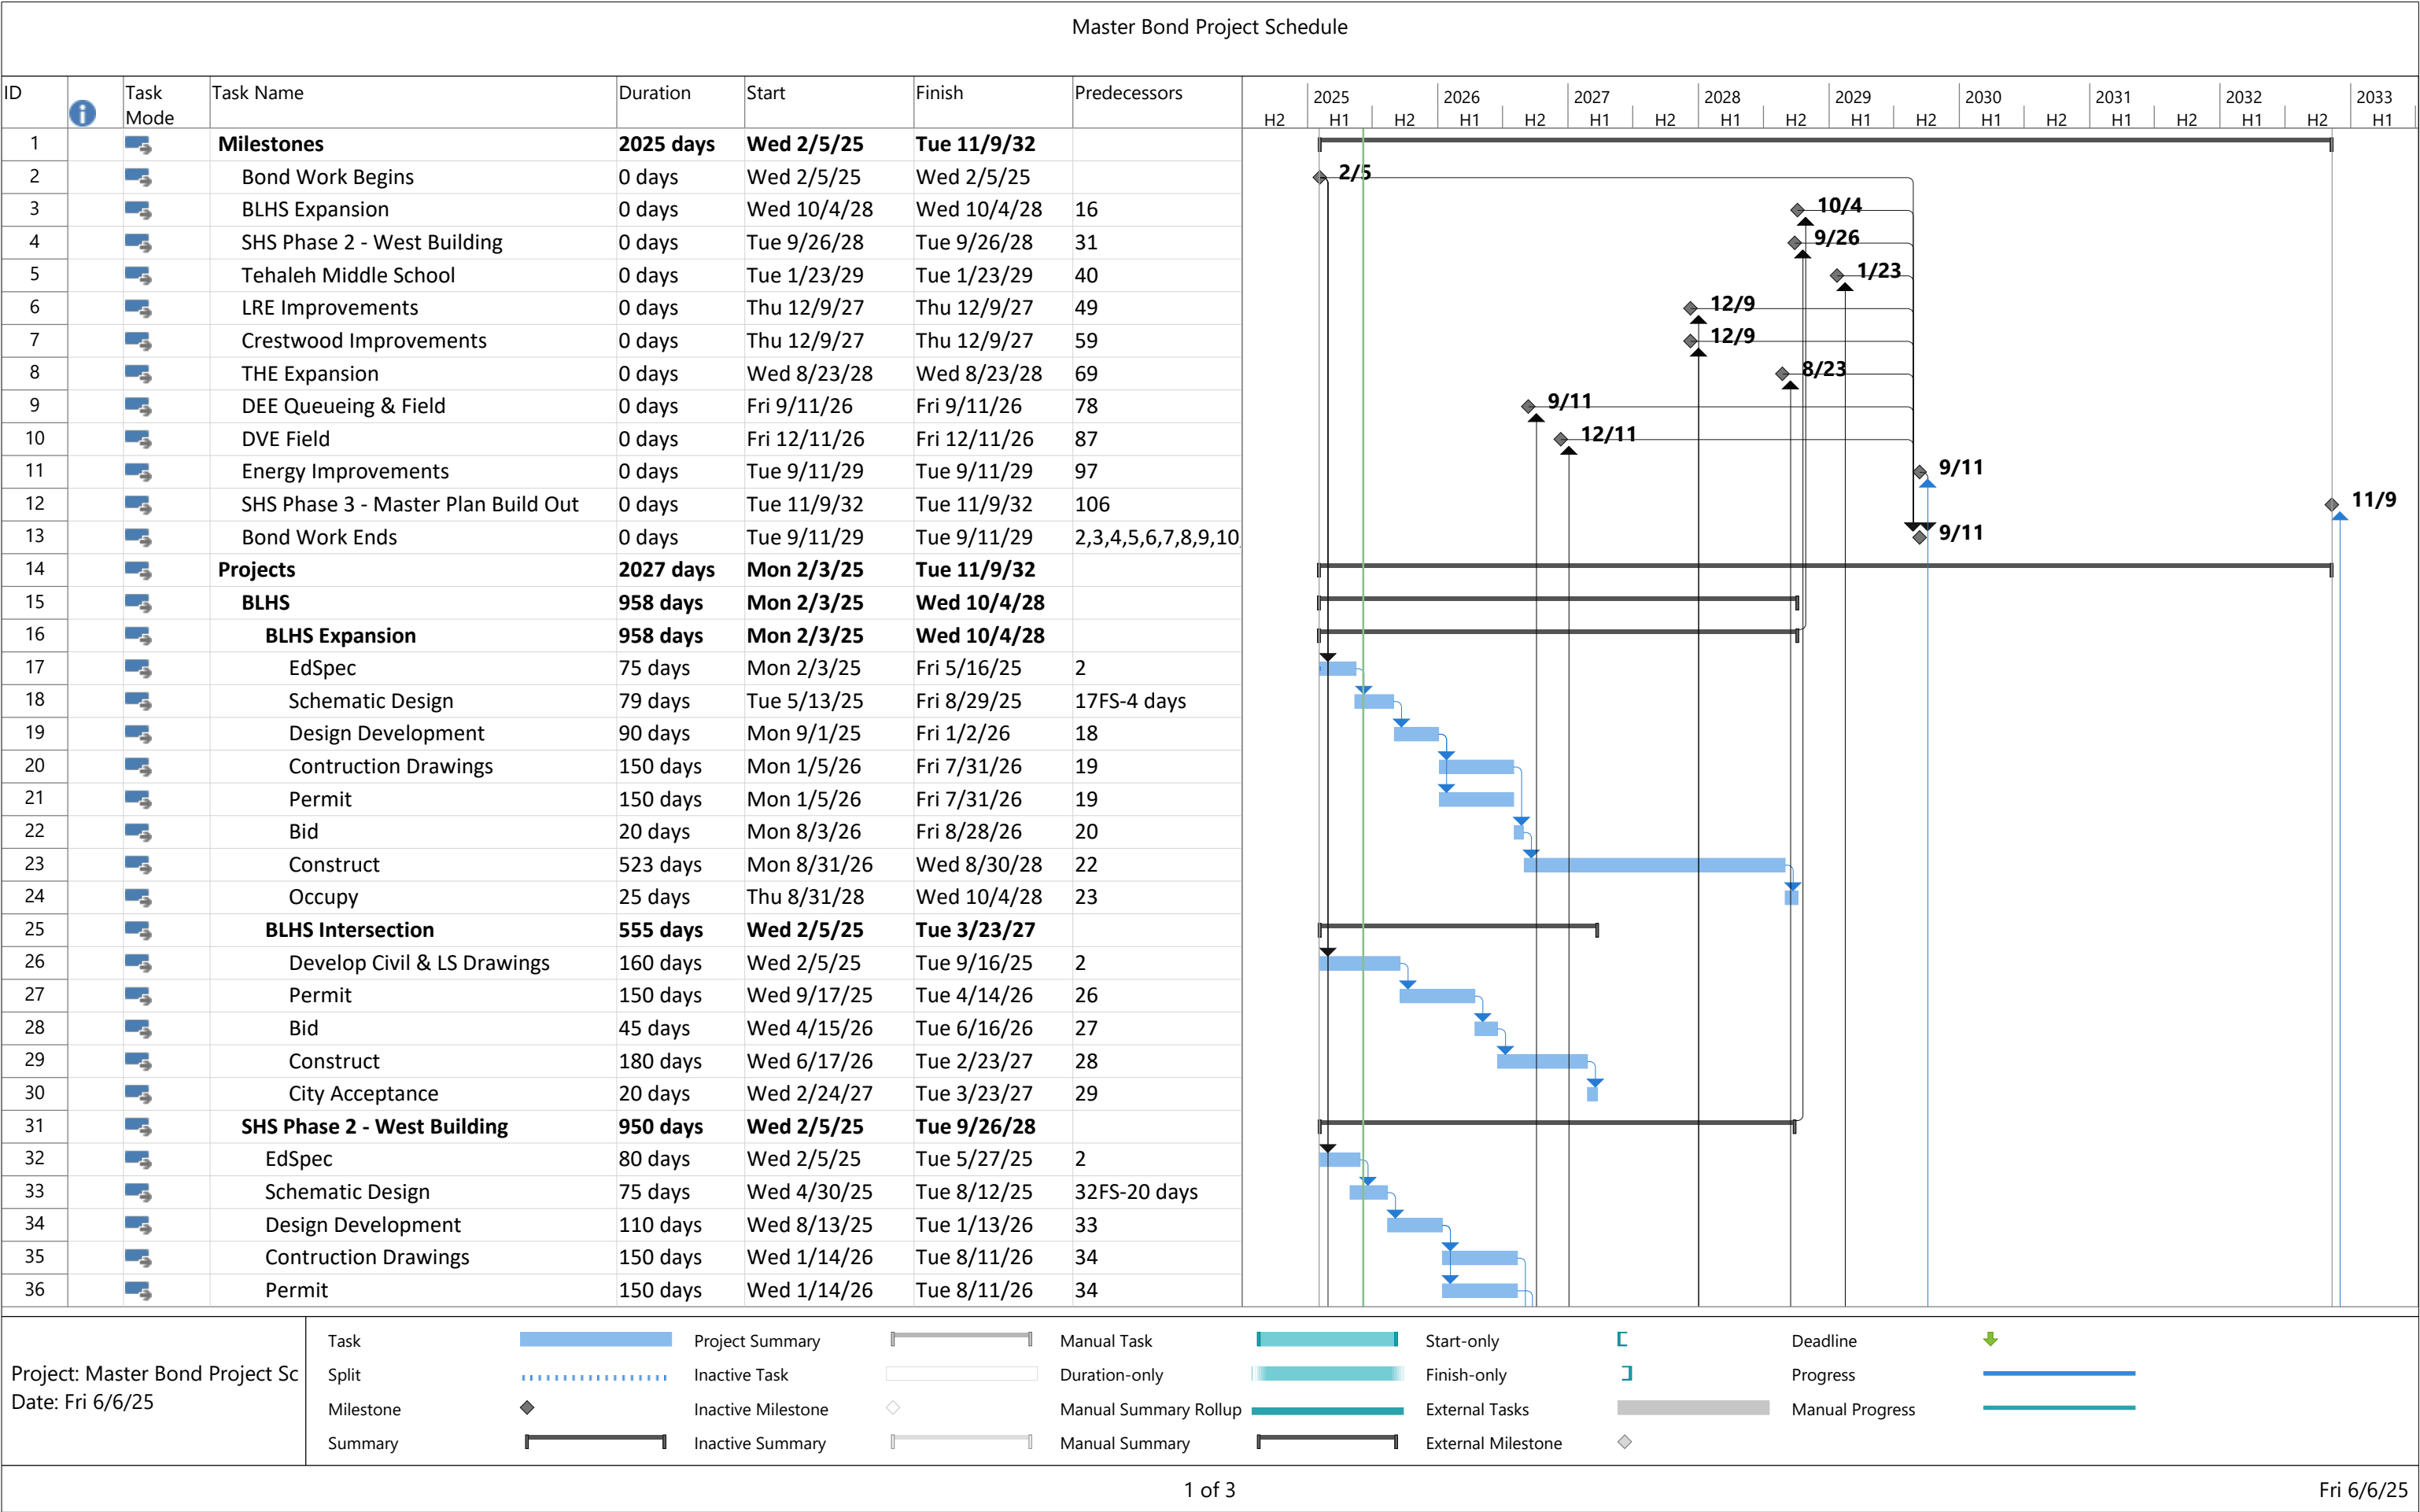


DeadlineProgressManual Progress

1 of 3

Fri 6/6/25

Master Bond Project Schedule

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors																								
							H2	2025 H1	H2	2026 H1	H2	2027 H1	H2	2028 H1	H2	2029 H1	H2	2030 H1	H2	2031 H1	H2	2032 H1	H2	2033 H1						
37		Bid	30 days	Wed 8/12/26	Tue 9/22/26	35																								
38		Construct	500 days	Wed 9/23/26	Tue 8/22/28	37,36																								
39		Occupy	25 days	Wed 8/23/28	Tue 9/26/28	38																								
40		Tehaleh Middle School	1035 days	Wed 2/5/25	Tue 1/23/29																									
41		EdSpec	100 days	Wed 2/5/25	Tue 6/24/25	2																								
42		Schematic Design	100 days	Wed 6/25/25	Tue 11/11/25	41																								
43		Design Development	120 days	Wed 11/12/25	Tue 4/28/26	42																								
44		Contruction Drawings	160 days	Wed 4/29/26	Tue 12/8/26	43																								
45		Permit	180 days	Wed 4/29/26	Tue 1/5/27	43																								
46		Bid	30 days	Wed 12/9/26	Tue 1/19/27	44																								
47		Construct	500 days	Wed 1/20/27	Tue 12/19/28	45,46																								
48		Occupy	25 days	Wed 12/20/28	Tue 1/23/29	47																								
49		LRE Improvements	640 days	Fri 6/27/25	Thu 12/9/27																									
50		Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25																									
51		EdSpec	30 days	Fri 9/19/25	Thu 10/30/25	50																								
52		Schematic Design	40 days	Fri 10/31/25	Thu 12/25/25	51																								
53		Design Development	60 days	Fri 12/26/25	Thu 3/19/26	52																								
54		Contruction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	53																								
55		Permit	120 days	Fri 3/20/26	Thu 9/3/26	53																								
56		Bid	30 days	Fri 7/24/26	Thu 9/3/26	54																								
57		Construct	320 days	Fri 9/4/26	Thu 11/25/27	56																								
58		Occupy	10 days	Fri 11/26/27	Thu 12/9/27	57																								
59		Crestwood Improvements	640 days	Fri 6/27/25	Thu 12/9/27																									
60		Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25																									
61		EdSpec	30 days	Fri 9/19/25	Thu 10/30/25	60																								
62		Schematic Design	40 days	Fri 10/31/25	Thu 12/25/25	61																								
63		Design Development	60 days	Fri 12/26/25	Thu 3/19/26	62																								
64		Contruction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	63																								
65		Permit	120 days	Fri 3/20/26	Thu 9/3/26	63																								
66		Bid	30 days	Fri 7/24/26	Thu 9/3/26	64																								
67		Construct	320 days	Fri 9/4/26	Thu 11/25/27	66																								
68		Occupy	10 days	Fri 11/26/27	Thu 12/9/27	67																								
69		Tehaleh Heights Elementary	763 days	Mon 9/22/25	Wed 8/23/28																									
70		EdSpec	53 days	Mon 9/22/25	Wed 12/3/25																									
71		Schematic Design	60 days	Thu 12/4/25	Wed 2/25/26	70																								
72		Design Development	110 days	Thu 2/26/26	Wed 7/29/26	71																								

Project: Master Bond Project Sc
Date: Fri 6/6/25

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Master Bond Project Schedule																										
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors		2025		2026		2027		2028		2029		2030		2031		2032		2033	
								H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	
73			Construction Drawings	150 days	Thu 7/30/26	Wed 2/24/27	72																			
74			Permit	120 days	Thu 7/30/26	Wed 1/13/27	72																			
75			Bid	50 days	Thu 1/14/27	Wed 3/24/27	74																			
76			Construct	350 days	Thu 3/25/27	Wed 7/26/28	75																			
77			Occupy	20 days	Thu 7/27/28	Wed 8/23/28	76																			
78			Donald Eisman Queueing & Field	335 days	Mon 6/2/25	Fri 9/11/26																				
79			EdSpec	20 days	Mon 6/2/25	Fri 6/27/25																				
80			Schematic Design	30 days	Mon 6/30/25	Fri 8/8/25	79																			
81			Design Development	40 days	Mon 8/11/25	Fri 10/3/25	80																			
82			Construction Drawings	60 days	Mon 10/6/25	Fri 12/26/25	81																			
83			Permit	120 days	Mon 10/6/25	Fri 3/20/26	81																			
84			Bid	30 days	Mon 3/23/26	Fri 5/1/26	83																			
85			Construct	90 days	Mon 5/4/26	Fri 9/4/26	84																			
86			Occupy	5 days	Mon 9/7/26	Fri 9/11/26	85																			
87			Daffodil Valley Field	400 days	Mon 6/2/25	Fri 12/11/26																				
88			EdSpec	20 days	Mon 6/2/25	Fri 6/27/25																				
89			Geotech Exploration (After Bill Heath Decision)	10 days	Mon 9/15/25	Fri 9/26/25																				
90			Schematic Design	30 days	Mon 9/29/25	Fri 11/7/25	89																			
91			Design Development	40 days	Mon 11/10/25	Fri 1/2/26	90																			
92			Construction Drawings	60 days	Mon 1/5/26	Fri 3/27/26	91																			
93			Permit	120 days	Mon 1/5/26	Fri 6/19/26	91																			
94			Bid	30 days	Mon 6/22/26	Fri 7/31/26	93																			
95			Construct	90 days	Mon 8/3/26	Fri 12/4/26	94																			
96			Occupy	5 days	Mon 12/7/26	Fri 12/11/26	95																			
97			Energy Improvements	1200 days	Wed 2/5/25	Tue 9/11/29																				
98			SHS Phase 3	1100 days	Wed 8/23/28	Tue 11/9/32																				
99			EdSpec	80 days	Wed 8/23/28	Tue 12/12/28	38																			
100			Schematic Design	75 days	Wed 11/15/28	Tue 2/27/29	99FS-20 days																			
101			Design Development	110 days	Wed 2/28/29	Tue 7/31/29	100																			
102			Construction Drawings	150 days	Wed 8/1/29	Tue 2/26/30	101																			
103			Permit	150 days	Wed 8/1/29	Tue 2/26/30	101																			
104			Bid	30 days	Wed 2/27/30	Tue 4/9/30	102																			
105			Construct	650 days	Wed 4/10/30	Tue 10/5/32	103,104																			
106			Occupy	25 days	Wed 10/6/32	Tue 11/9/32	105																			
Project: Master Bond Project Sc Date: Fri 6/6/25			Task		Project Summary		Manual Task		Start-only		Deadline															
			Split		Inactive Task		Duration-only		Finish-only		Progress															
			Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress															
			Summary		Inactive Summary		Manual Summary		External Milestone																	
3 of 3																								Fri 6/6/25		
