



Construction Update Measure X&T June 2025

Measure X 2015 - \$148M



Measure T 2020 - \$409M



Status Update

- All Solar Shade structures are now generating electricity
- Fiesta Gardens North project started construction early April, campus move this summer with College Park
- Measure T Issuance "C" sale mid-summer 2025
- Bowditch New Academic Core scheduled move-in for early October, gym completion Q1 2026
- Phase III Paving and Turf project awarded



Funded By:
Measure T

BOWDITCH ACADEMIC CORE & GYM



Funded By:
Measure T

BOWDITCH ACADEMIC CORE & GYM



Funded By:
Measure X

FIESTA GARDENS NORTH



Funded By:
Measure X

FIESTA GARDENS NORTH



Funded By:
Measure T

HIGHLANDS MULTI-PURPOSE ROOM



Funded By:
Measure T

HIGHLANDS MULTI-PURPOSE ROOM



Funded By:
Measure T

PARKSIDE MULTI-PURPOSE ROOM



Funded By:
Measure T

PARKSIDE MULTI-PURPOSE ROOM



Funded By:
Measure T

MEADOW HEIGHTS MULTI-PURPOSE ROOM



Borel MS

Funded By:
Measure T

TURF AND PAVING



Consolidated Budget Status Report

Budgets versus Commitments and Expenditures for multiple Projects

Budget vs. Commitments and Expenditures Measure X & Additional Funding Sources	Budget	Commitments		Expenditures		Status	Construction Start Date Anticipated	Completed Date Anticipated
	Total Budget	Total Commitments	% Budget Committed	Total Expenditures	% Budget Spent			
Active Projects								
Bowditch Middle School - Ph 1 Drama Science	19,800,000	19,465,842	98.3%	19,202,812	97.0%	Close Out	Oct-23	Fall 2024
Fiesta Garden North	36,000,000	30,464,274	84.6%	3,010,085	8.4%	Construction	2025	Aug-26
Sunnybrae Elementary - MPR	16,000,000	14,636,860	91.5%	14,524,091	90.8%	Close Out	Jan-23	Summer 2024
Program - MX Non Project Specific Expenses	4,000,000	3,892,071	97.3%	3,892,071	97.3%	Ongoing		Duration of Bond
Totals	75,800,000	68,459,047	90.3%	40,629,059	53.6%			
Completed Projects								
EV Bus Charging	486,831	486,831	100.0%	486,831	100.0%	Complete		
Abbott Middle School - Gym & Classrooms	21,016,488	21,016,488	100.0%	21,016,488	100.0%	Complete		
Abbott Middle School - Shade Structure	54,679	54,678	100.0%	54,678	100.0%	Complete		
Bayside S.T.E.M. - New Gym	12,131,841	12,131,841	100.0%	12,131,841	100.0%	Complete		
Beach Park Elementary - Charter Square	24,257,031	24,257,031	100.0%	24,257,031	100.0%	Complete		
Borel Middle School - Shade Structure	1,678,021	1,678,021	100.0%	1,678,021	100.0%	Complete		
Borel Middle School - Gym & Classrooms	22,724,137	22,724,137	100.0%	22,724,137	100.0%	Complete		
George Hall Elementary - MPR	11,824,233	11,799,694	99.8%	11,762,822	99.5%	Complete		
Totals	94,173,262	94,148,722	100.0%	94,111,850	99.9%			
Grand Totals	169,973,262	162,607,769		134,740,909				
FUNDING SOURCES								
Measure X Series A	73,755,000.00	Funds Not Received						
Measure X Series B	44,865,000.00							
Measure X Series C	28,800,000.00							
Interest FY 20-21; 21-22; 22-23; 23-24; 24-25	2,335,900.60							
Developer Fees	6,174,505.00							
Fund 40	16,000,000.00							
Transportation Funds AB181	486,831.05							
State Funding Mod Eligibility				22,000,000.00				
Totals	172,417,236.65			22,000,000.00				
Funds not Allocated	\$ 2,443,975.14							

Measure X



Consolidated Budget Status Report

Budgets versus Commitments and Expenditures for multiple Projects

Budget vs. Commitments and Expenditures Measure T & Additional Funding Sources

	Budget	Commitments		Expenditures		Status	Construction Start Date Anticipated	Completion Date Anticipated
	Total Budget	Total Commitments	% Budget Committed	Total Expenditures	% Budget Spent			
Active Projects								
Bowditch - Ph II-IV: Academic Core, Gym	67,200,000	51,308,134	76.4%	32,939,903	49.0%	Construction	Winter 23	Summer 27
District Wide - Solar	19,141,863	18,956,018	99.0%	15,283,901	79.8%	Construction	Late 23	Spring 25
District Wide - Flooring Ph 5	3,000,000	-	0.0%	-	0.0%	Construction	Summer 25	Fall 25
District Wide - HVAC II	47,000,000	46,631,334	99.2%	46,434,356	98.8%	Close Out	Spring 23	Fall 24
District Wide - HVAC III	10,500,000	8,081,353	77.0%	2,545,171	24.2%	Construction	Spring 25	Fall 26
District Wide - AV Upgrades	1,500,000	1,087,857	72.5%	657,715	43.8%	Construction	Fall 24	Fall 25
District Wide - Restroom Modernization	61,993,000	9,068,846	14.6%	6,963,156	11.2%	Design Cons	Summer 23	Late 27
District Wide - Technology Upgrades	9,000,000	-	0.0%	-	0.0%	Scoping	Fall 25	Fall 27
District Wide - Turf & Paving Phase 2	25,500,000	23,149,712	90.8%	21,136,539	82.9%	Construction	Summer 23	Summer 25
District Wide - Turf & Paving Phase 3	19,100,000	17,667,811	92.5%	204,627	1.1%	Design	Summer 25	Fall 26
Program - Non Project Specific Expenses	10,000,000	5,972,940	59.7%	4,663,486	46.6%	Ongoing		Duration of Bond
MPR Projects								
Highlands Elementary - MPR	17,500,000	17,121,648	97.8%	16,311,710	93.2%	Close Out	Spring 23	Winter 25
Lead Elementary - MPR	15,000,000	14,624,731	97.5%	14,374,384	95.8%	Close Out	Spring 23	Fall 24
Meadow Heights Elem - MPR	14,940,000	14,279,072	95.6%	12,639,962	84.6%	Construction	Winter 24	Summer 25
Parkside Elementary - MPR	17,000,000	16,055,672	94.4%	12,109,018	71.2%	Construction	Winter 23	Summer 25
Totals	338,374,862	244,005,128	72.1%	186,263,928	55.0%			
Completed Projects								
Completed Project Totals	56,329,818	56,176,035	99.7%	56,171,546	99.7%			
Grand Totals	394,704,680	300,181,163		242,435,474				
Funding Sources								
		Funds Not Received						
MT Series A	100,000,000.00							
MT Series B	150,000,000.00							
MT Series C - Summer 2025	100,000,000.00							
MT Series D - Future Bond Sale	59,000,000.00							
Interest FY 21-22; 22-23; 23-24; 24-25	10,255,541.52							
Developer Fee	180,000.00							
Erate		1,670,000.00						
State Funding Mod Eligibility (2025-2027)		31,000,000.00						
Solar - IRS & Grants	200,000.00	4,907,344.00						
Totals	419,645,541.52	37,577,344.00						

Funds Not Allocated


\$ 24,940,861.50

Measure T

Facilities Master Plan Update

- Previous Plan, “Facilities Master Plan for the Next Decade,” was adopted in 2020 before deciding to go for Measure T
- Aedis Architects and District Staff are updating the previous plan, verifying completed scopes, and updating needs
- Draft of FMP scheduled for August 2025
- Meetings at school sites to review scopes and rank priorities Fall 2025
- Plan to be completed by end of 2025. An updated FMP required every 5 years to participate in the CA State Bond Program, SMFCSD’s eligibility is \$55M

Update to District's Facilities Master Plan (FMP)

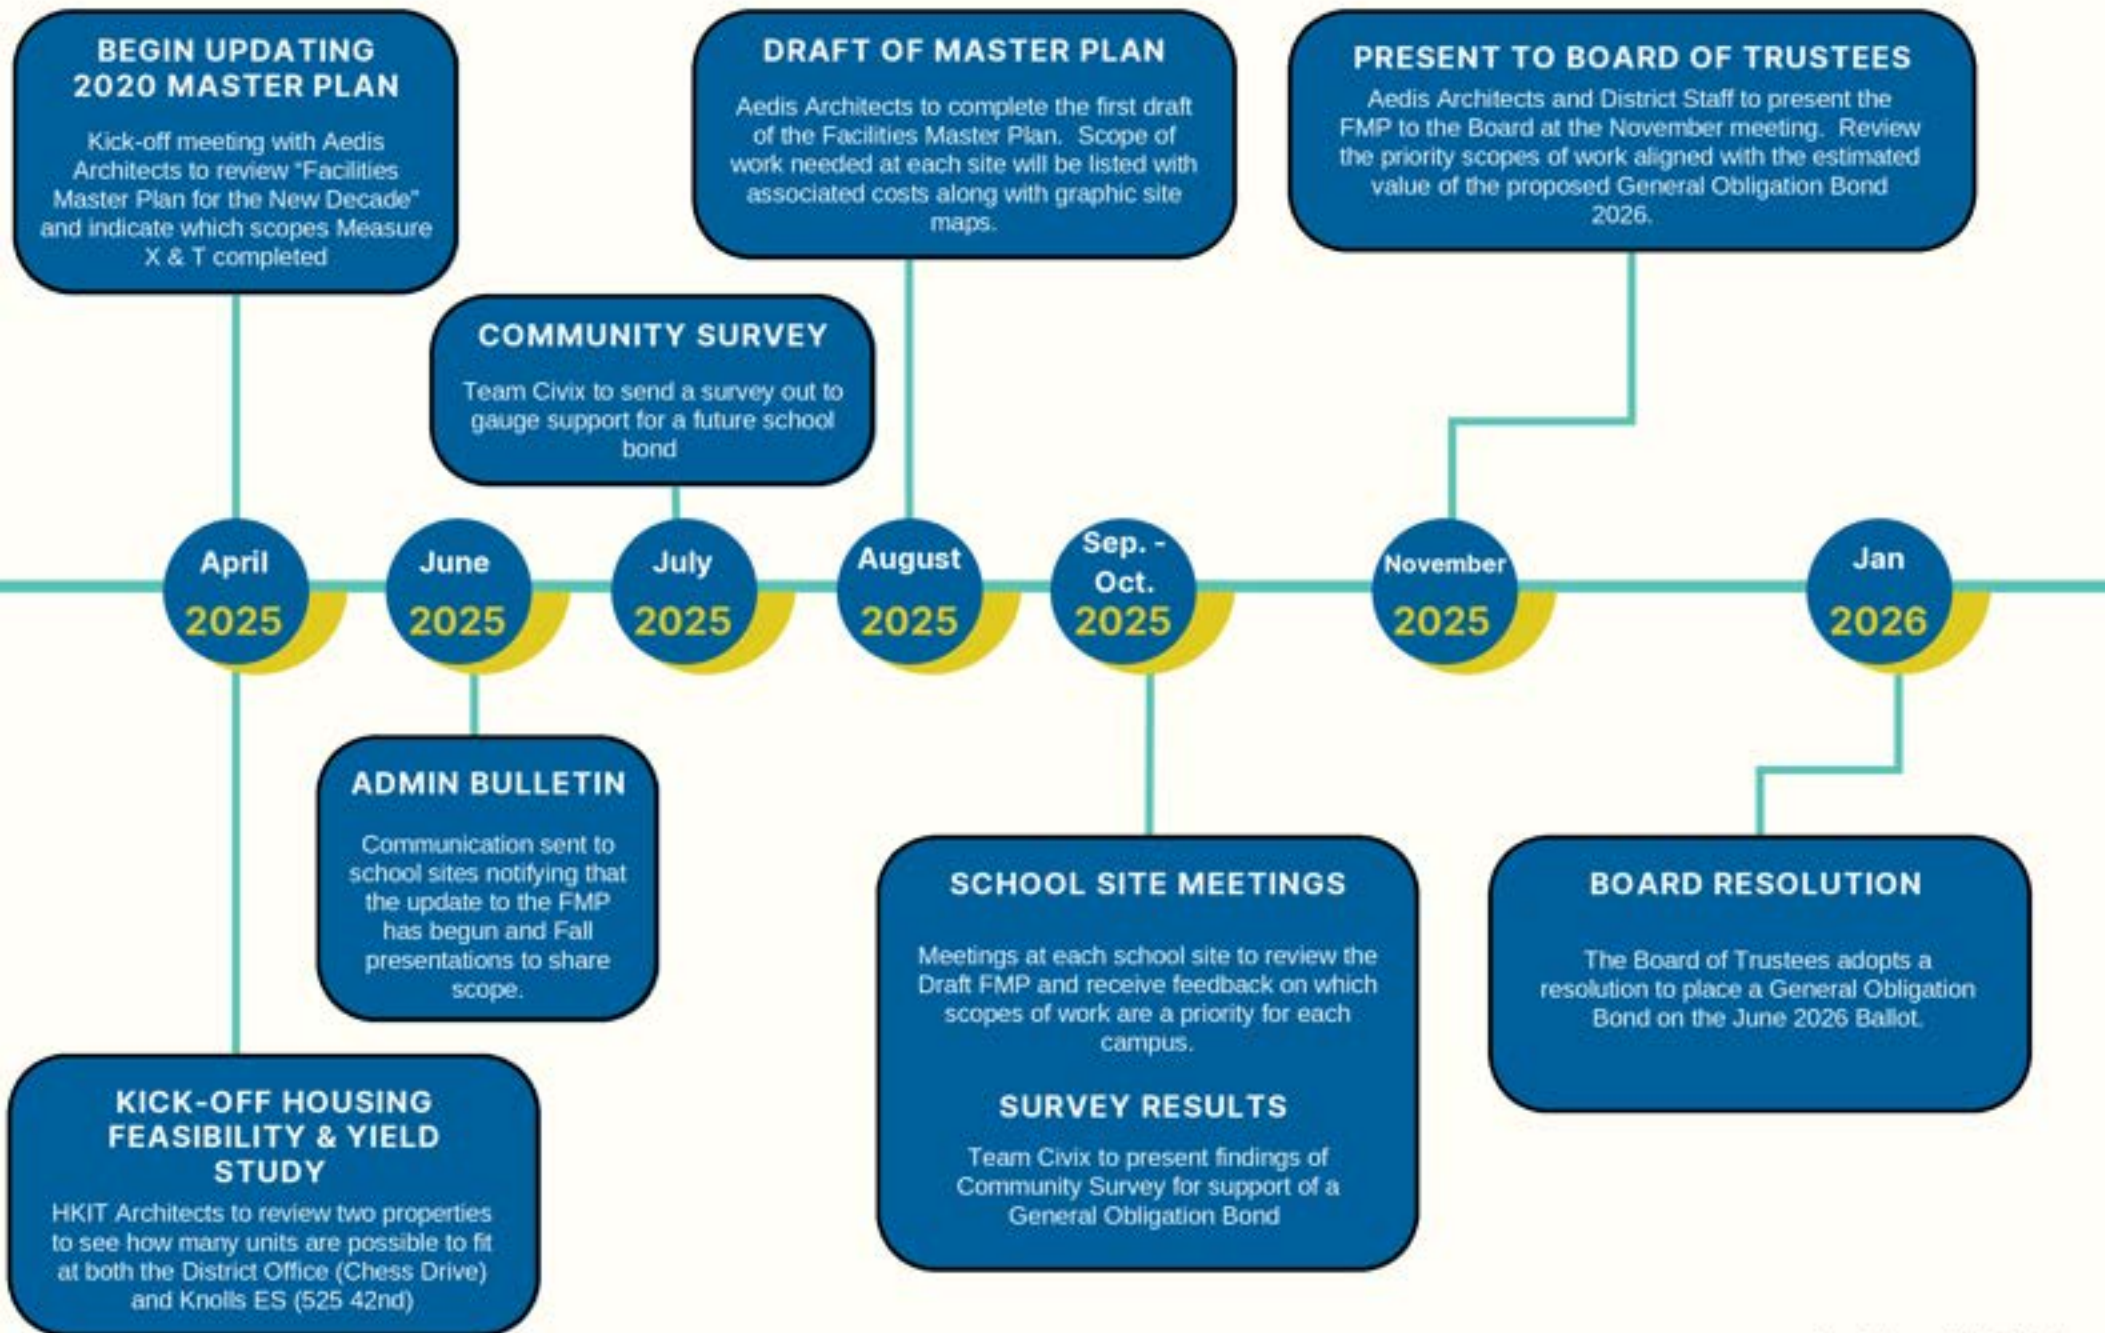



Construction Update Measure X&T June 2025
