




# Monthly Progress Report

July 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress July 2025

**Section III** – Work Projected for August 2025

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary July 2025

### Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
  - Staircase railings upgrades.
  - Classroom wall upgrades per code.
  - Install eye wash stations.
  - Install new exhaust fans.
  - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
  - Remove old asphalt tennis grounds.
  - Install new tennis courts with bleachers.
  - Install a bridge for students to access the tennis courts.



## Section II - Work Progress July 2025

### Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
  - Completed demo of existing non-fire rated walls.
  - Completed framing all walls in room 105 and 106.
  - Completed CMU block build for double door installation in hallway.
  - Completed removal of wall and lockers for double door installation in science room.
  - Completed taping and spackling of new walls.
  - Removed the existing staircase and excavated for a new ramp in A building.
  - Installed foundation walls and brick for ramp.
  - Poured concrete for interior ramp.
- Locust Valley:
  - Completed all in wall roughing in rooms 105 and 106.
  - Completed roughing for double
- IMC:
  - BMS controls punch list completed.
  - HVAC balancing started.

### Hempstead UFSD – HS Tennis Courts

- United Paving
  - Installed trench drains and poured concrete for trench drains.
  - Installed asphalt topcoat for courts
  - Installed bleacher pads and bleachers.
  - Saw cut as needed in asphalt.
  - Installed fencing around perimeter of courts.
  - Installed asphalt walkway.



## Section III - Work Planned August 2025

### **Hempstead UFSD – HS Priority Infrastructure Upgrades**

- Total:
  - Complete C building classrooms, and A building interior ramp.
- Locust Valley:
  - Complete all electrical work in C building classrooms.
- IMC
  - Complete balancing for HVAC system.

### **Hempstead UFSD – HS Tennis Courts**

- United Paving
  - Install paint lines for courts.
  - Install court netting.
  - Fully complete tennis courts.
  - Submit new design of bridge.




## Section IV – Progress Photos



Hempstead HS – Interior Ramp



## Section IV – Progress Photos

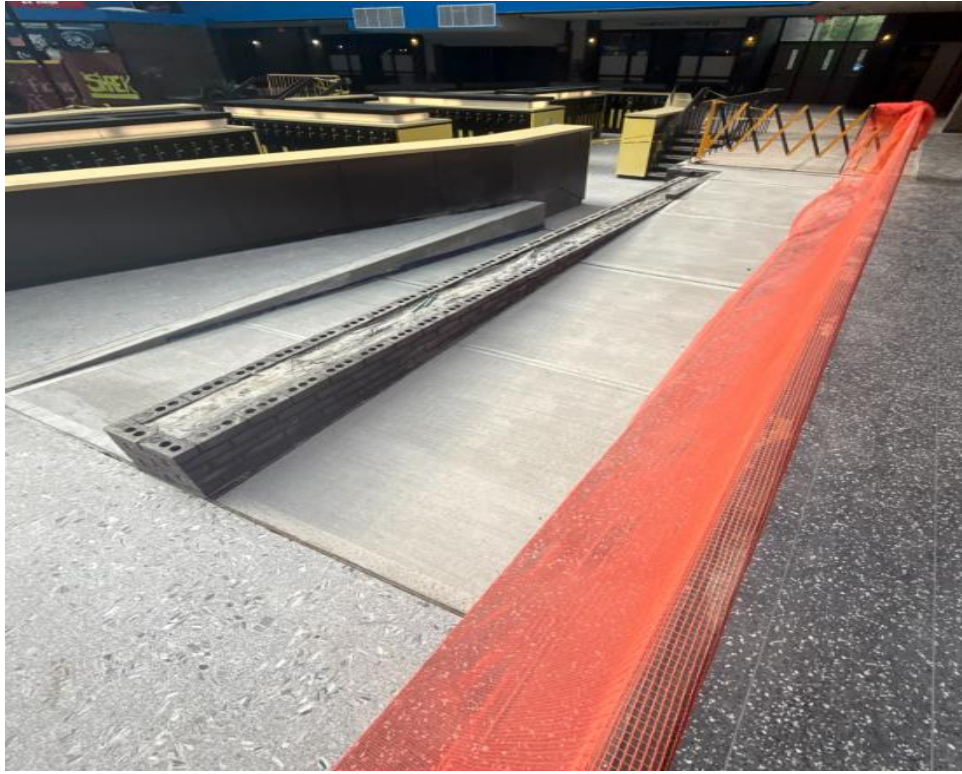

Hempstead HS – Interior Ramp



## Section IV – Progress Photos



### Hempstead HS – C Building Classrooms




## Section IV – Progress Photos



Hempstead HS – C Building Classrooms



## Section IV – Progress Photos

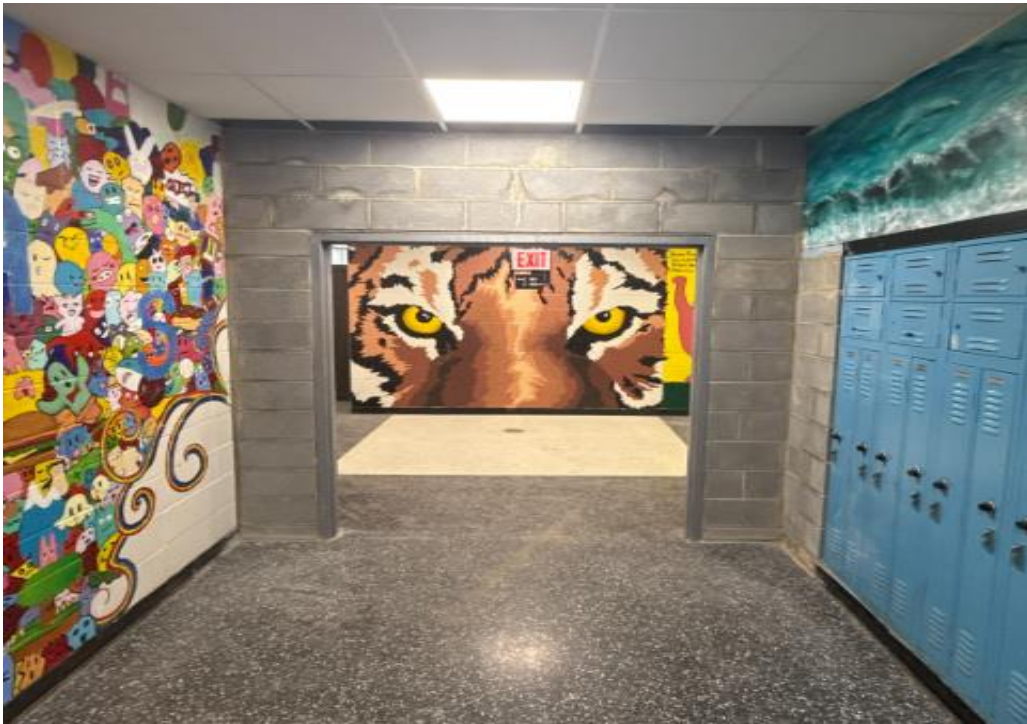

Hempstead HS – Double Doors



## Section IV – Progress Photos



## Hempstead HS – Tennis Courts



## Section IV – Progress Photos



## Hempstead HS – Tennis Courts




# Section V – Workforce Summary – Company/Hours

## July 2025

### Manpower Chart

#### MANPOWER GRAPH

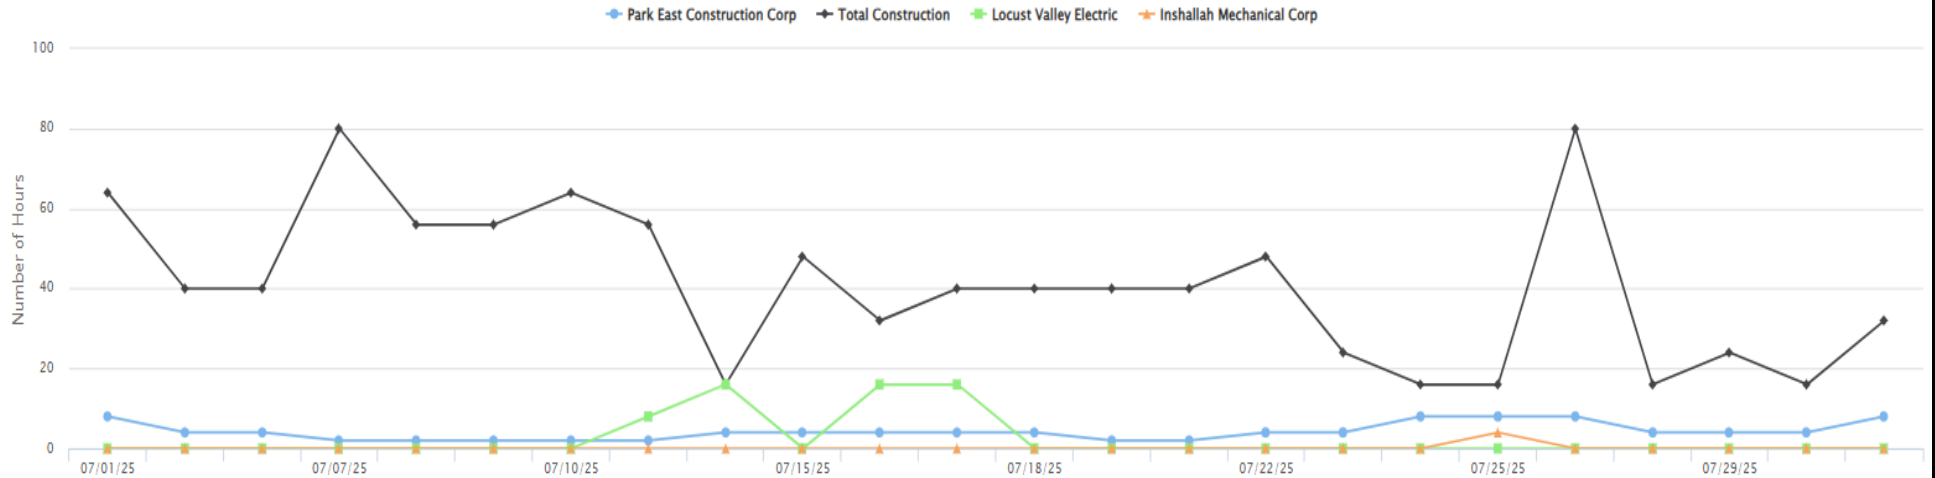


Hempstead HS – Infrastructure



## Section V – Workforce Summary – Company/Hours

### July 2025

#### MANPOWER GRAPH

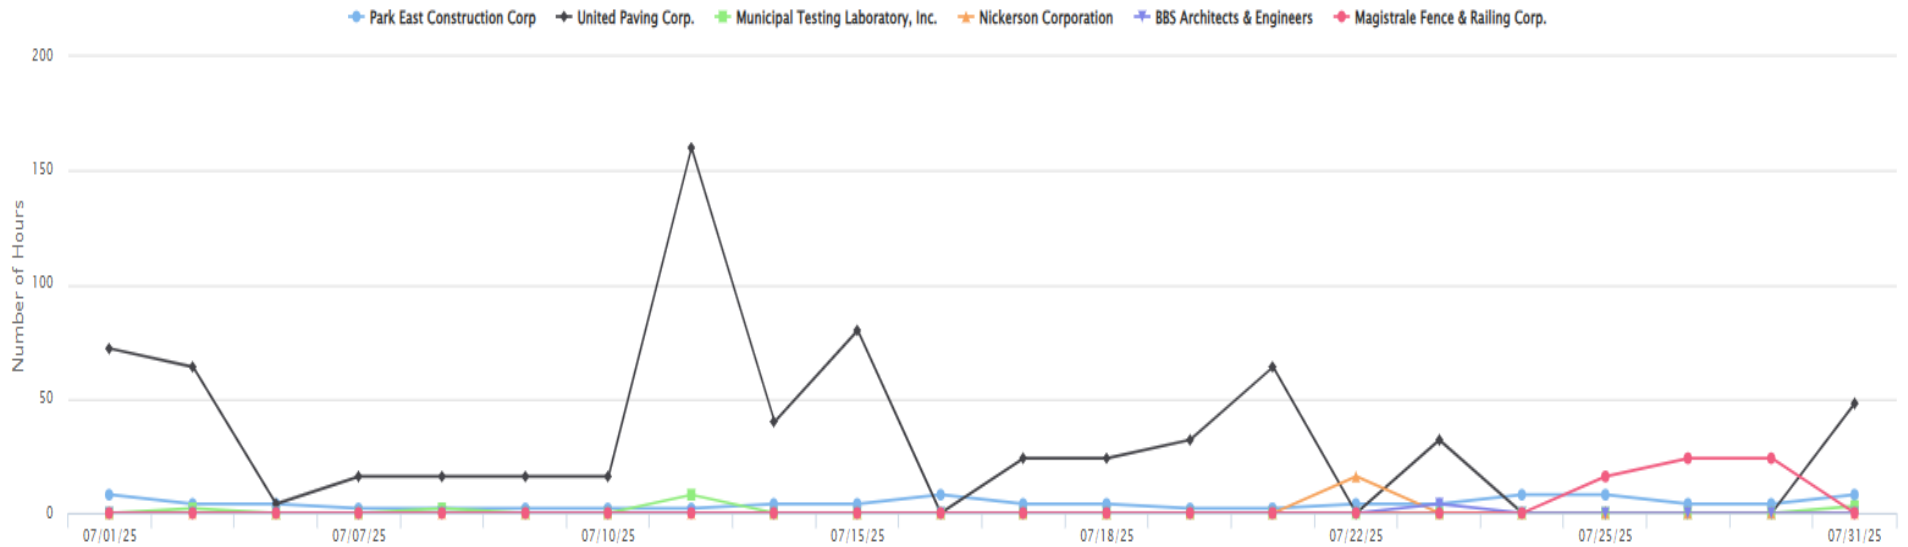

Hempstead HS – Tennis Courts



Hempstead Union Free School District

July 2025

## End of Progress Report
