


New Henry Clay High School

➤ Completed/Work in Progress:

- Site grading work is underway.
- Grading for the roadway to the west of the new building is underway.
- New water line tap is complete.
- Geothermal well drilling is in progress.
- Structural caissons drilling is underway.
- Foundations are in progress.
- Temporary sanitary sewer line complete.
- Temporary car drop-off loop is complete and ready for striping.
- Temporary sidewalks are complete.
- ICF and CIP formwork placing and pouring is in progress.
- Underground / Under-slab plumbing is in progress.
- Laying CMU walls is in progress.

➤ Upcoming Look Ahead:

- Site demolition work will continue.
- Continue hauling in fill materials.
- Continue site grading.
- Continue sanitary piping and manholes.
- Continue pouring ICF and CIP concrete walls.
- Continue underground plumbing.
- Continue laying CMU walls.
- Begin pouring concrete slabs on grade.
- Begin placing ICF frames for framed openings.

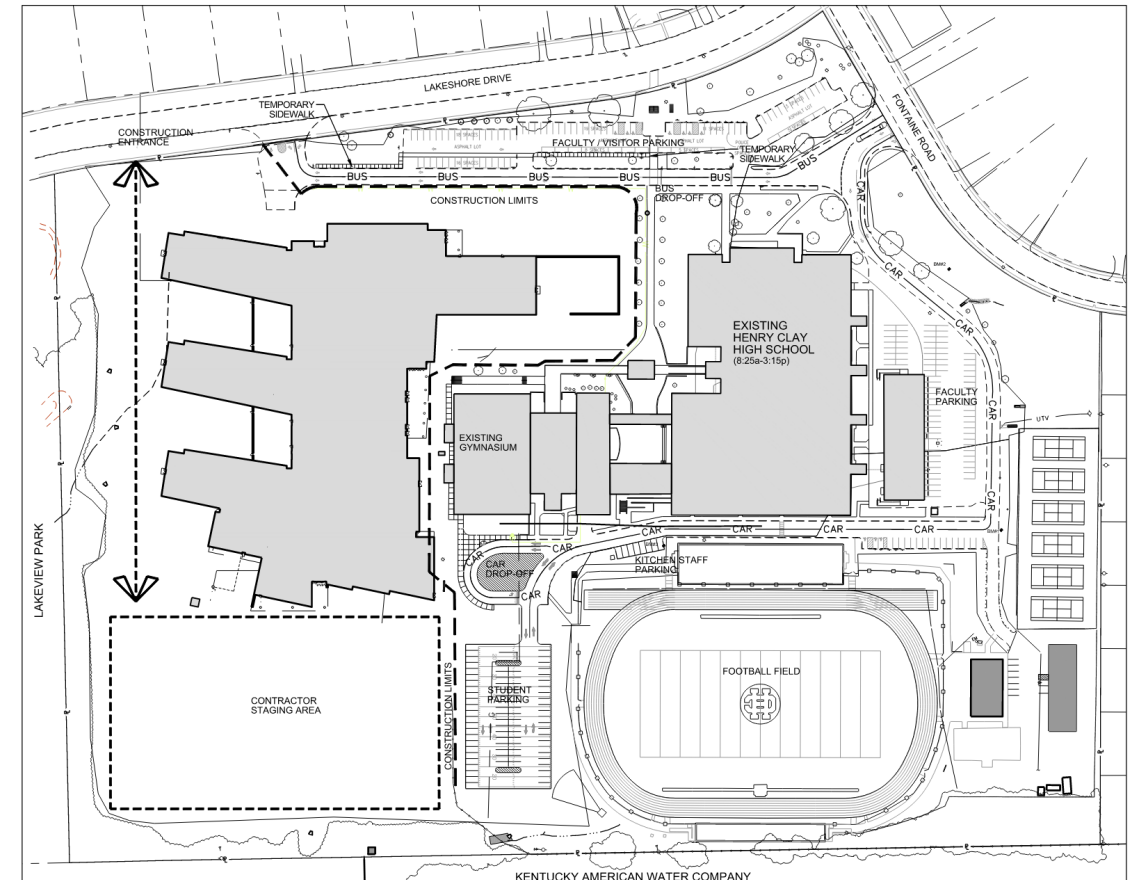

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

ICF Walls, CIP Concrete Walls, Laying CMU and Underground Plumbing in Progress



Week Ending August 15, 2025

New Henry Clay High School

ICF Walls, CIP Concrete Walls, Laying CMU and Underground Plumbing in Progress



New Henry Clay High School



CIP Concrete Walls in Progress



Week Ending August 15, 2025

New Henry Clay High School



Grading for Roadway Underway (West Area of Site)



Week Ending August 15, 2025

New Henry Clay High School



Geothermal Well Drilling Continues (Southwest Area of Site)



Week Ending August 15, 2025

New Henry Clay High School

Foundations and Structural Caisson Drilling Continues (North Area of Site)



Week Ending August 15, 2025
