


New Henry Clay High School

➤ Completed/Work in Progress:

- Site grading work is underway.
- Grading for the roadway to the west of the new building is underway.
- Geothermal well field drilling at south end of site is complete.
- Trenching and gathering of geothermal piping is in progress.
- Structural caisson drilling is underway.
- Foundations are in progress.
- ICF and CIP formwork placing and pouring is in progress.
- Underground / Under-slab plumbing and electrical is in progress.
- Laying of the first coursing of CMU walls is in progress.
- Installation of IFAs (integrated framing assemblies) for framed openings at ICF walls is underway.

➤ Upcoming Look Ahead:


- Site demolition work will continue.
- Continue hauling in fill materials.
- Continue site grading.
- Continue sanitary piping and manholes.
- Continue pouring ICF and CIP concrete walls.
- Continue underground plumbing and electrical.
- Continue laying the first coursing of CMU walls.
- Continue with underground / under-slab plumbing and electrical.
- Begin pouring concrete slabs on grade.
- Continue installing integrated framing assemblies for framed openings at ICF walls.
- Begin installing hollow metal frames.

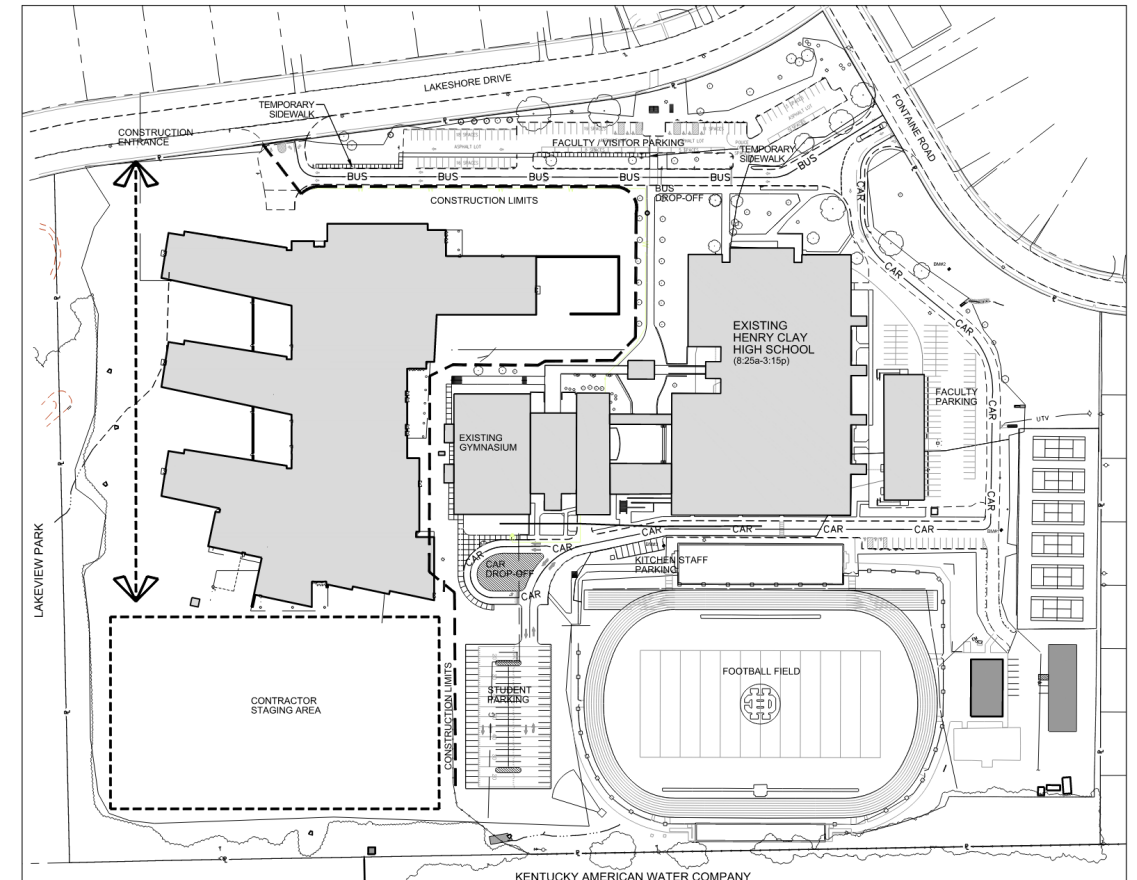

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

ICF & CIP Concrete Walls, IFA Frame Installation, Laying CMU, and Under-Slab Plumbing & Electrical in Progress

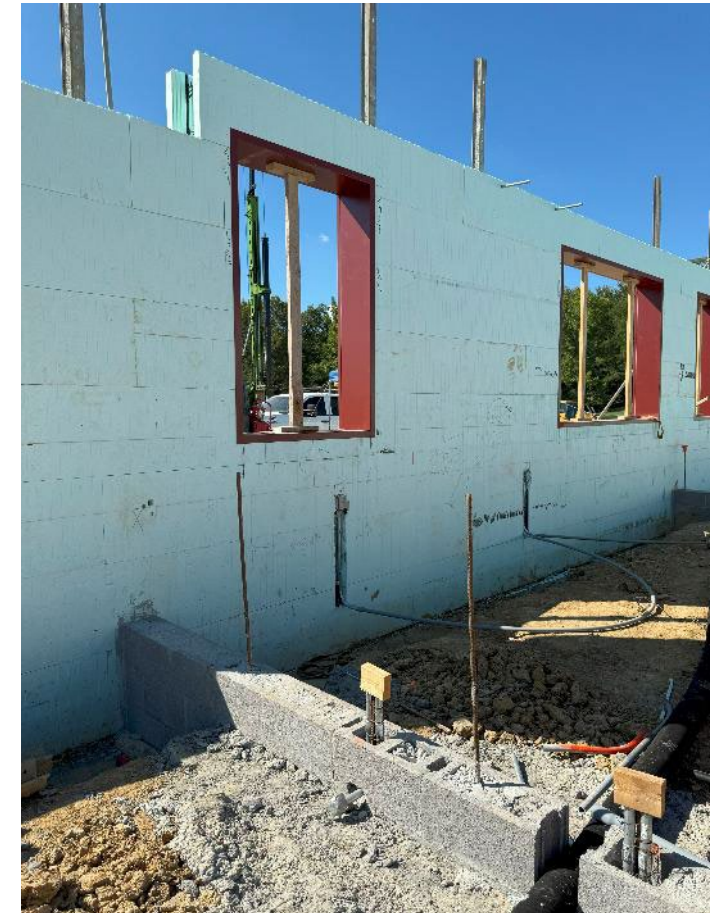

New Henry Clay High School

ICF & CIP Concrete Walls, IFA Frame Installation, Laying CMU, and Under-Slab Plumbing & Electrical in Progress



New Henry Clay High School

ICF & CIP Concrete Walls, IFA Frame Installation, Laying CMU, and Under-Slab Plumbing & Electrical in Progress



New Henry Clay High School

ICF & CIP Concrete Walls, IFA Frame Installation, Laying CMU, and Under-Slab Plumbing & Electrical in Progress



Week Ending August 29, 2025

New Henry Clay High School

ICF & CIP Concrete Walls, IFA Frame Installation, Laying CMU, and Under-Slab Plumbing & Electrical in Progress



New Henry Clay High School



Foundations and Structural Caisson Drilling Continues



Week Ending August 29, 2025
