

Measure BB Bond

21st Century Classroom Improvements
SEPTEMBER 9, 2025




CUMMING
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE



HLPUSD MEASURE BB - SUMMARY

SCHOOLS IN PROGRESS

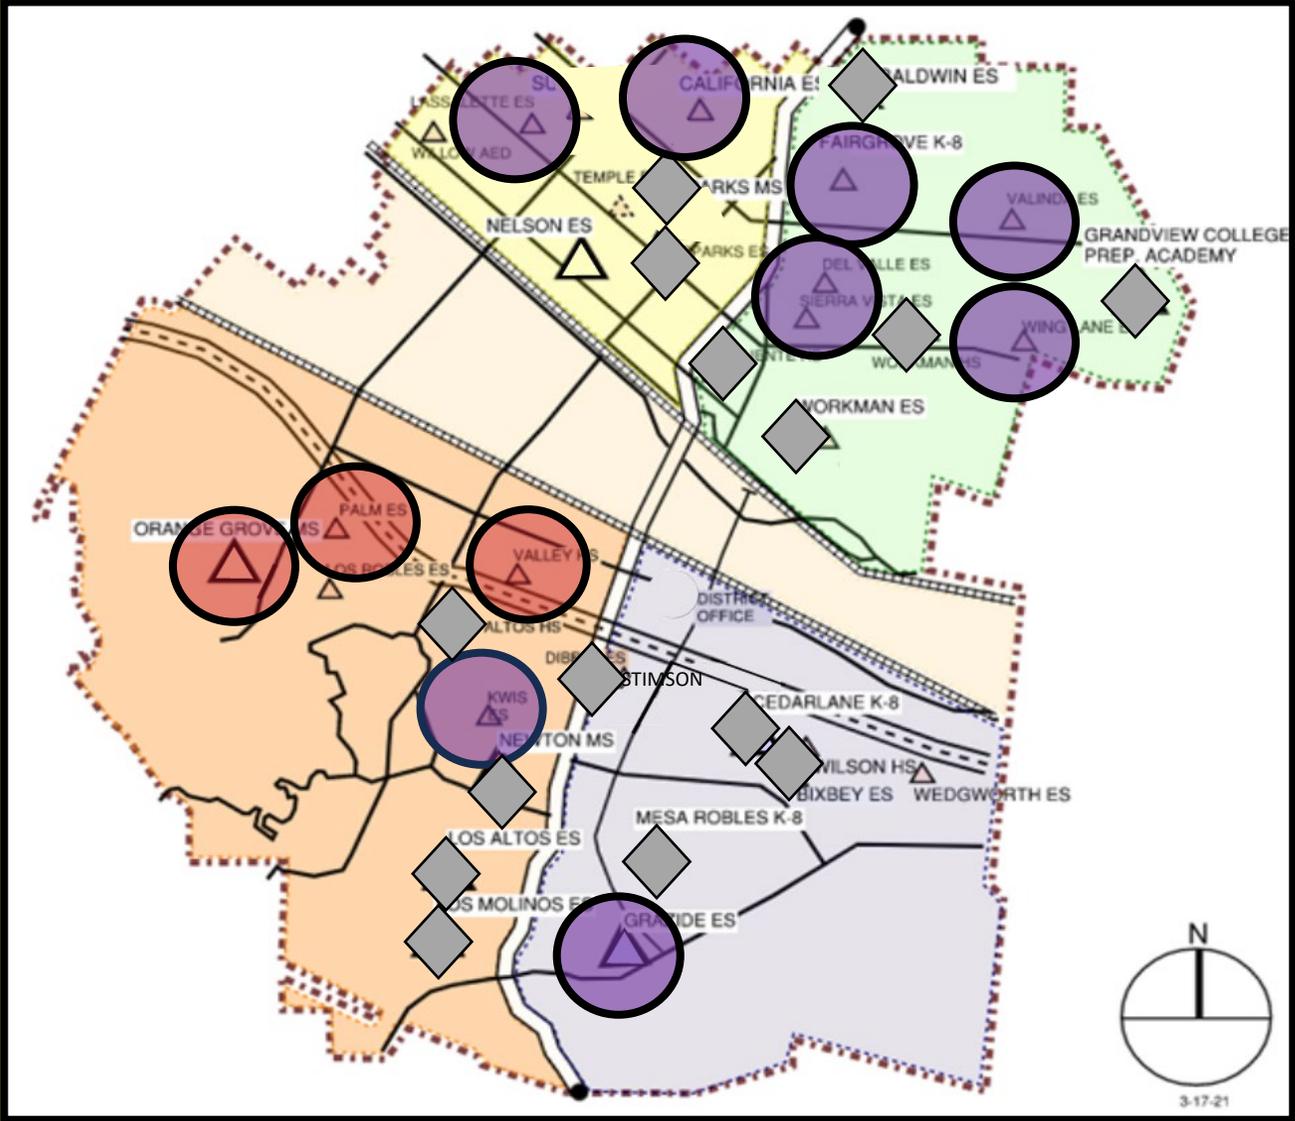

IN PROGRESS CONSTRUCTION

- Grazide ES
- Kwis ES
- Fairgrove K-8
- Lassalette ES
- Sierra Vista MS
- Valinda ES
- Sparks ES
- Wing Lane ES



COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Grandview MS
- Newton MS
- Stimson EC
- Workman HS
- La Puente HS
- Wilson HS
- Los Altos HS
- Los Molinos ES
- Baldwin ES
- California ES




DSA PLAN REVIEW

- Valley Alternative School

- Palm ES

IN DESIGN

- Orange Grove MS




PHASE B PROGRESS

PROJECT STARTS CONSTRUCTION DOCUMENTS TO DSA DSA PLAN REVIEWS COMPLETED PROJECTS BID CONSTRUCTION STARTS (COMPLETED*)

	PROJECT STARTS	CONSTRUCTION DOCUMENTS TO DSA	DSA PLAN REVIEWS COMPLETED	PROJECTS BID	CONSTRUCTION STARTS (COMPLETED*)
Baldwin ES	●	●	●	●	●
California ES	●	●	●	●	●
Grazide ES	●	●	●	●	●
Los Molinos	●	●	●	●	●
Kwis ES	●	●	●	●	●
Lassalette ES	●	●	●	●	●
Fairgrove Academy	●	●	●	●	●
Sierra Vista MS	●	●	●	●	●
Sparks ES	●	●	●	●	●
Palm ES	●	●	●	●	○
Valinda ES	●	●	●	●	●
Wing Lane ES	●	●	●	●	●
Valley Alternative School	●	●	●	⊙	⊙
Orange Grove	●	⊙	⊙	⊙	⊙

Measure BB 21st Century
Classroom Improvements
California Elementary School
Phases 3 & 4

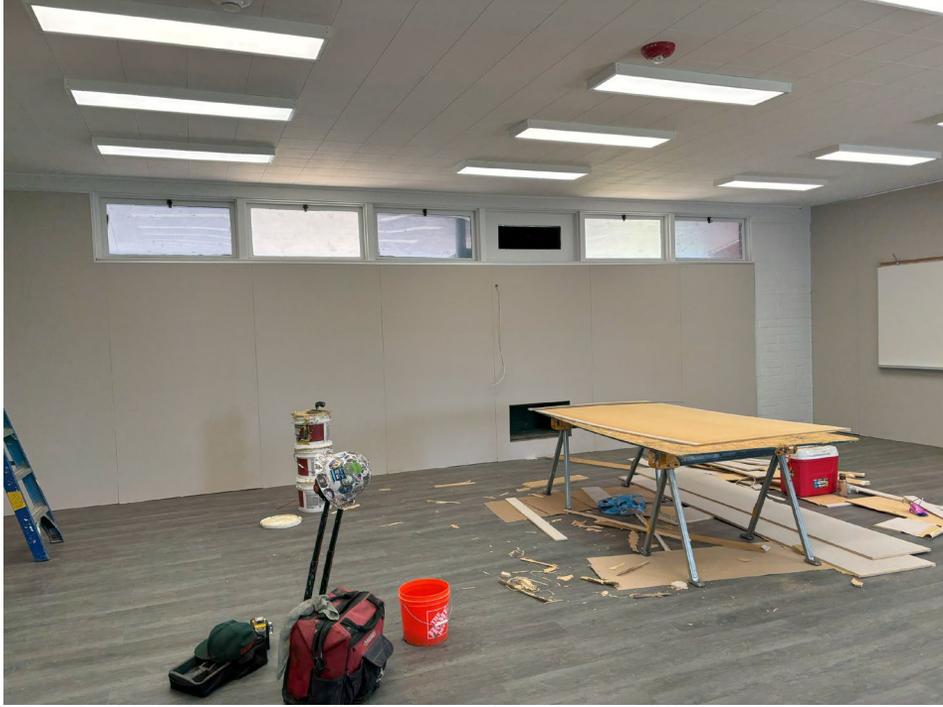

ESTIMATED COMPLETION AUGUST 25, 2025

Measure BB 21st Century
Classroom Improvements
Baldwin Academy School
SUBSTANTIALLY COMPLETE



ESTIMATED PROJECT COMPLETION JULY 30, 2025

Measure BB 21st Century
Classroom Improvements
Los Molinos Elementary Phase 3
SUBSTANTIALLY COMPLETE



ESTIMATED COMPLETION JULY 30, 2025

Measure BB 21st Century
Classroom Improvements
Grazide Elementary
PHASE 1 COMPLETED



ESTIMATED PROJECT COMPLETION JANUARY 23, 2026

Measure BB 21st Century
Classroom Improvements
Kwis Elementary Phase 1 Completed



ESTIMATED PROJECT COMPLETION OCTOBER 2025

CUMMING
GROUP

Measure BB 21st Century
Classroom Improvements
Lassalette Elementary Phase 1



ESTIMATED COMPLETION OCTOBER 2025

Measure BB 21st Century
Classroom Improvements
Sierra Vista Middle School
Phase 1: Completed



ESTIMATED PROJECT COMPLETION OCTOBER 2025

CUMMING
GROUP

Measure BB 21st Century
Classroom Improvements
Fairgrove K-8 Phase 1



ESTIMATED PROJECT COMPLETION DECEMBER 2025

Measure BB 21st Century Classroom Improvements
Valinda, Wing Lane, Sparks

ESTIMATED PROJECT COMPLETION JANUARY 2026
WING LANE ES



DEMOLITION

VALINDA ES
ESTIMATED PROJECT COMPLETION JANUARY 2026



SPARKS ES
ESTIMATED PROJECT COMPLETION JANUARY 2026



CUMMING
GROUP



QUESTIONS
