


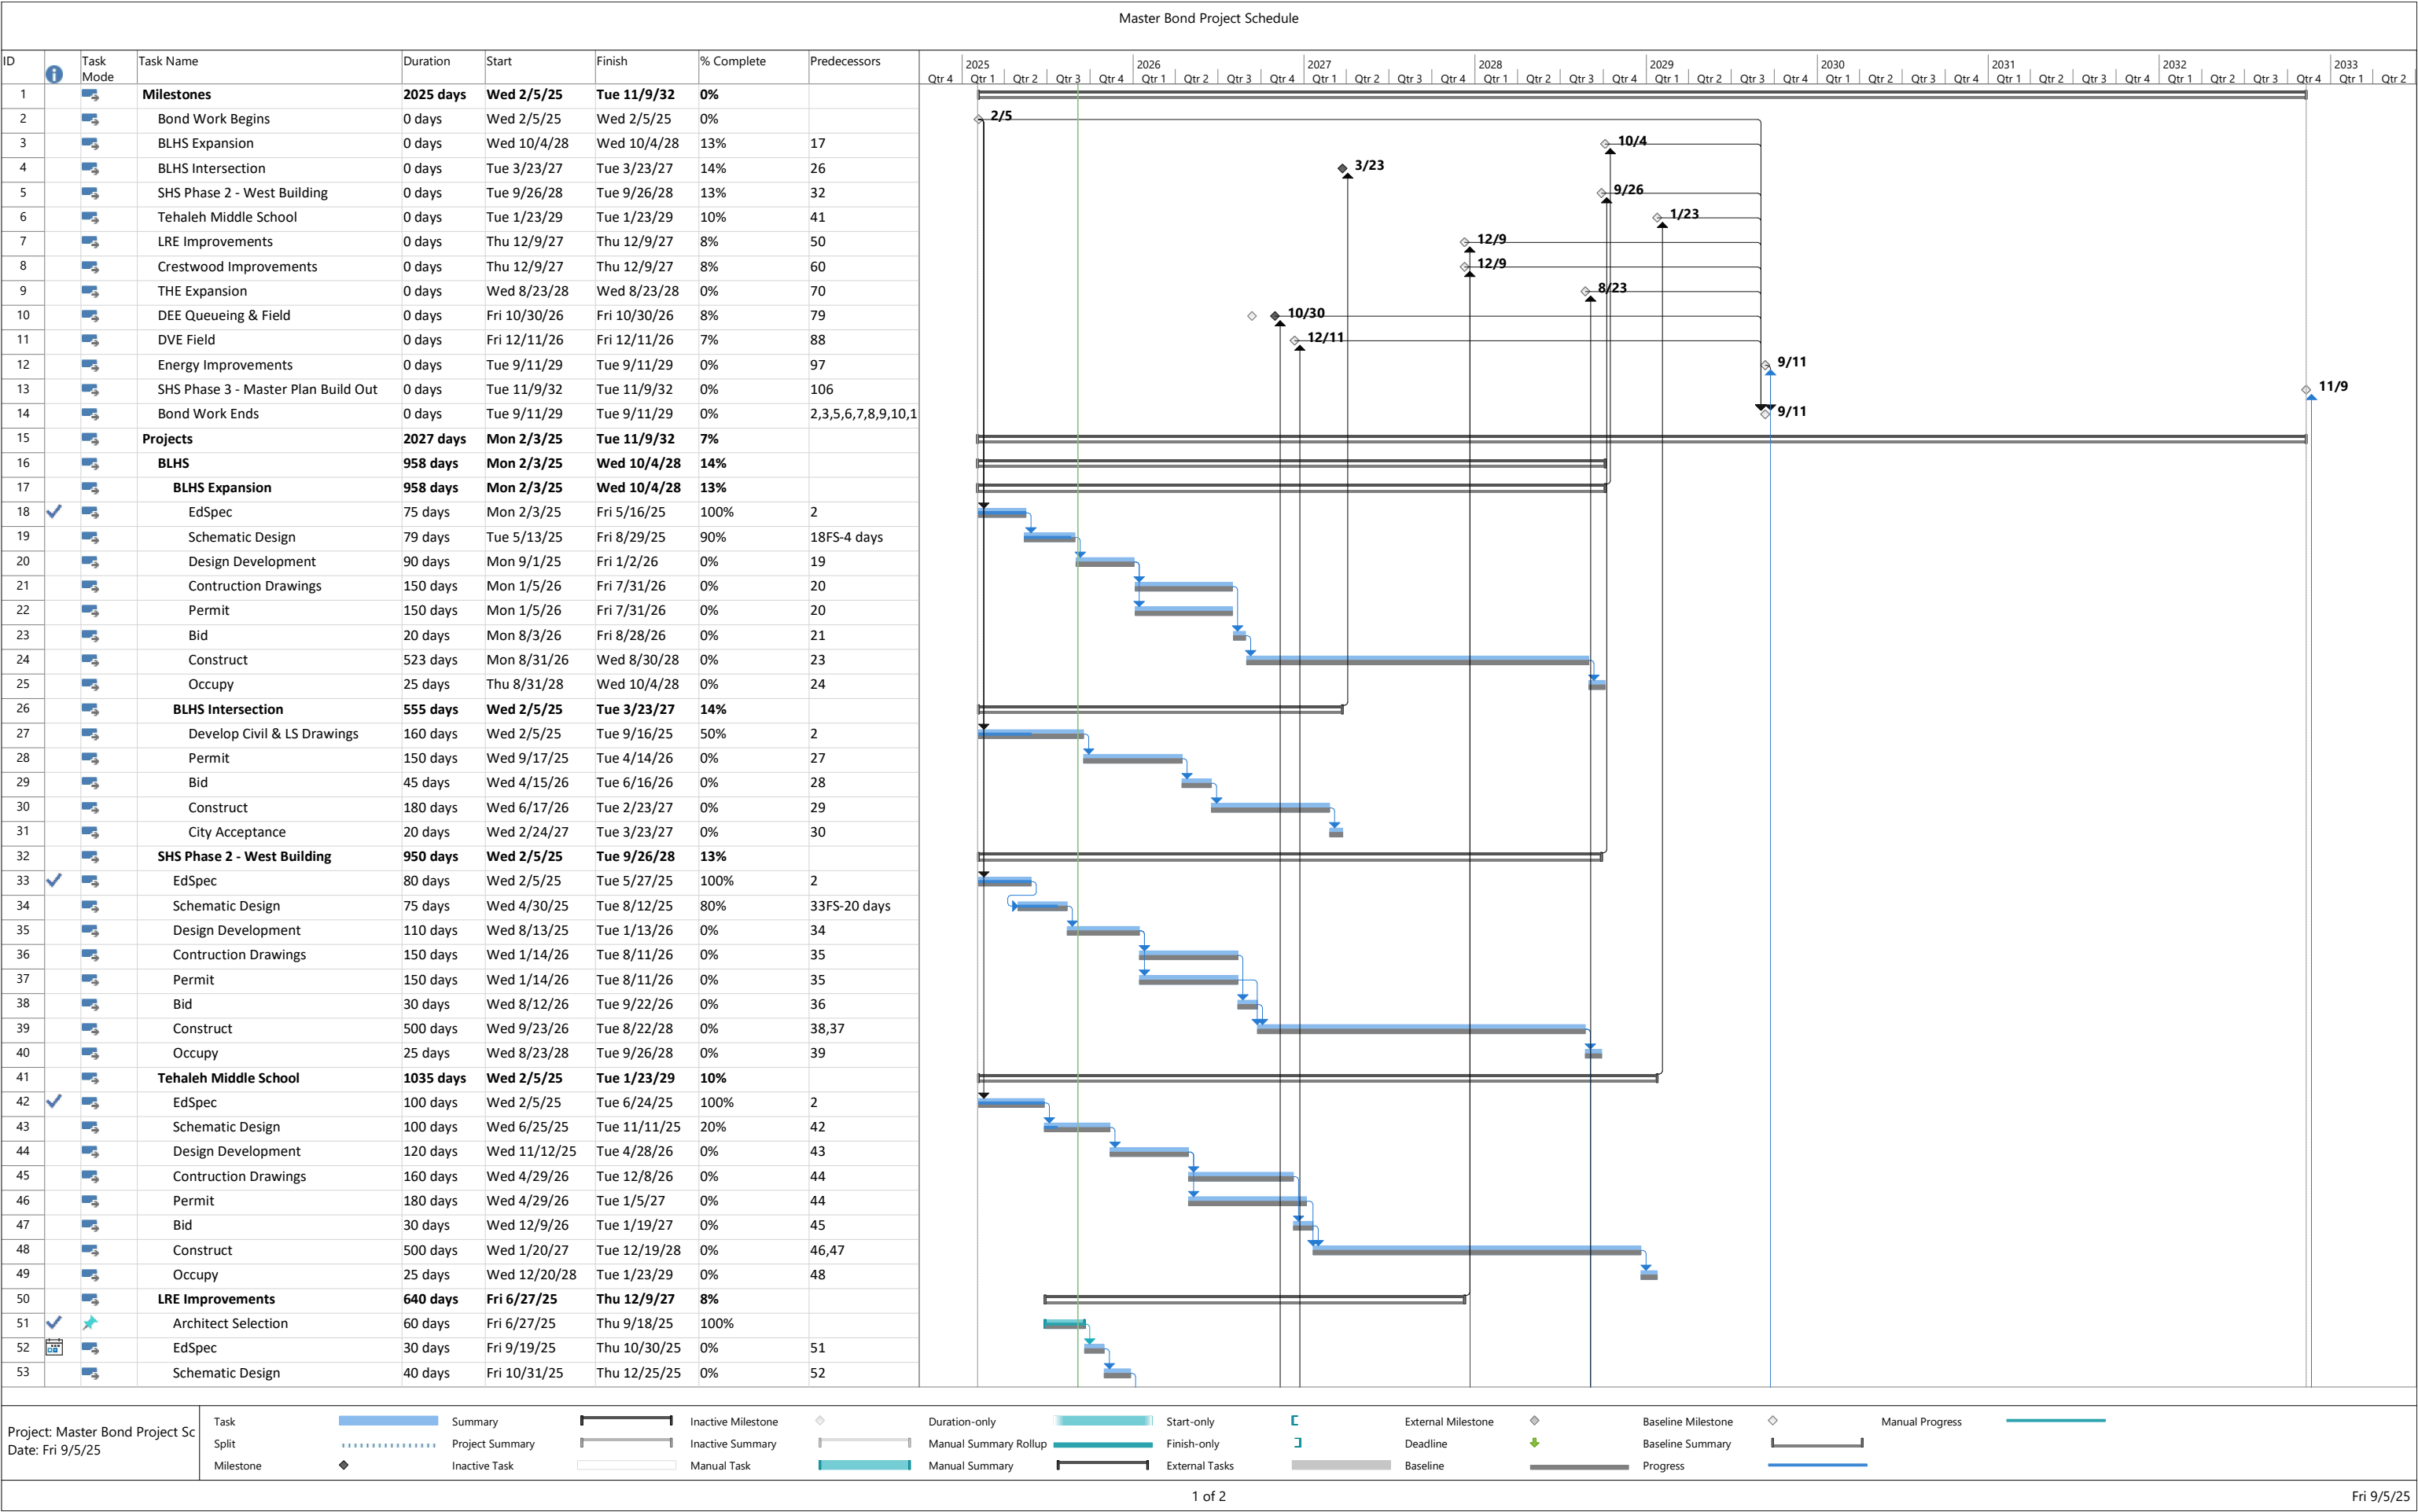

Master Bond Project Schedule									
ID		Task Mode	Task Name	Duration	Start	Finish	% Complete	Predecessors	
54			Design Development	60 days	Fri 12/26/25	Thu 3/19/26	0%	53	
55			Construction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	0%	54	
56			Permit	120 days	Fri 3/20/26	Thu 9/3/26	0%	54	
57			Bid	30 days	Fri 7/24/26	Thu 9/3/26	0%	55	
58			Construct	320 days	Fri 9/4/26	Thu 11/25/27	0%	57	
59			Occupy	10 days	Fri 11/26/27	Thu 12/9/27	0%	58	
60			Crestwood Improvements	640 days	Fri 6/27/25	Thu 12/9/27	8%		
61			Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25	100%		
62			EdSpec	30 days	Fri 9/19/25	Thu 10/30/25	0%	61	
63			Schematic Design	40 days	Fri 10/31/25	Thu 12/25/25	0%	62	
64			Design Development	60 days	Fri 12/26/25	Thu 3/19/26	0%	63	
65			Construction Drawings	90 days	Fri 3/20/26	Thu 7/23/26	0%	64	
66			Permit	120 days	Fri 3/20/26	Thu 9/3/26	0%	64	
67			Bid	30 days	Fri 7/24/26	Thu 9/3/26	0%	65	
68			Construct	320 days	Fri 9/4/26	Thu 11/25/27	0%	67	
69			Occupy	10 days	Fri 11/26/27	Thu 12/9/27	0%	68	
70			Tehaleh Heights Elementary	763 days	Mon 9/22/25	Wed 8/23/28	0%		
71			EdSpec	53 days	Mon 9/22/25	Wed 12/3/25	0%		
72			Schematic Design	60 days	Thu 12/4/25	Wed 2/25/26	0%	71	
73			Design Development	110 days	Thu 2/26/26	Wed 7/29/26	0%	72	
74			Construction Drawings	150 days	Thu 7/30/26	Wed 2/24/27	0%	73	
75			Permit	120 days	Thu 7/30/26	Wed 1/13/27	0%	73	
76			Bid	50 days	Thu 1/14/27	Wed 3/24/27	0%	75	
77			Construct	350 days	Thu 3/25/27	Wed 7/26/28	0%	76	
78			Occupy	20 days	Thu 7/27/28	Wed 8/23/28	0%	77	
79			Donald Eisman Queueing & Field	370 days	Mon 6/2/25	Fri 10/30/26	8%		
80			EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%		
81			Schematic Design	75 days	Mon 6/30/25	Fri 10/10/25	20%	80	
82			Design Development	30 days	Mon 10/13/25	Fri 11/21/25	0%	81	
83			Construction Drawings	45 days	Mon 11/24/25	Fri 1/23/26	0%	82	
84			Permit	120 days	Mon 11/24/25	Fri 5/8/26	0%	82	
85			Bid	30 days	Mon 5/11/26	Fri 6/19/26	0%	84	
86			Construct	90 days	Mon 6/22/26	Fri 10/23/26	0%	85	
87			Occupy	5 days	Mon 10/26/26	Fri 10/30/26	0%	86	
88			Daffodil Valley Field	400 days	Mon 6/2/25	Fri 12/11/26	7%		
89			EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%		
90			Schematic Design	30 days	Mon 9/29/25	Fri 11/7/25	20%	89	
91			Design Development	40 days	Mon 11/10/25	Fri 1/2/26	0%	90	
92			Construction Drawings	60 days	Mon 1/5/26	Fri 3/27/26	0%	91	
93			Permit	120 days	Mon 1/5/26	Fri 6/19/26	0%	91	
94			Bid	30 days	Mon 6/22/26	Fri 7/31/26	0%	93	
95			Construct	90 days	Mon 8/3/26	Fri 12/4/26	0%	94	
96			Occupy	5 days	Mon 12/7/26	Fri 12/11/26	0%	95	
97			Energy Improvements	1200 days	Wed 2/5/25	Tue 9/11/29	0%		
98			SHS Phase 3	1100 days	Wed 8/23/28	Tue 11/9/32	0%		
99			EdSpec	80 days	Wed 8/23/28	Tue 12/12/28	0%	39	
100			Schematic Design	75 days	Wed 11/15/28	Tue 2/27/29	0%	99FS-20 days	
101			Design Development	110 days	Wed 2/28/29	Tue 7/31/29	0%	100	
102			Construction Drawings	150 days	Wed 8/1/29	Tue 2/26/30	0%	101	
103			Permit	150 days	Wed 8/1/29	Tue 2/26/30	0%	101	
104			Bid	30 days	Wed 2/27/30	Tue 4/9/30	0%	102	
105			Construct	650 days	Wed 4/10/30	Tue 10/5/32	0%	103,104	
106			Occupy	25 days	Wed 10/6/32	Tue 11/9/32	0%	105	
Project: Master Bond Project Sc			Task						
Date: Fri 9/5/25			Split						
			Milestone						
2 of 2									
Fri 9/5/25									
