

CBOC Highlights Report – Phase II**February 2021**


- Board of Education Updates – 2/1/21**
 - Approval of Substantial Completion – Benson High School: Capital Improvements and Renovation Project – Hausmann Construction
 - 2018 Bond Program Presentation Update
- Board of Education Updates – 2/18/21**
 - Approval of GMP Amendment #002 – New Middle School: 42nd & Y St. – McCarthy Building Companies \$15,331,762.00
 - Approval of Resolution Authorizing Issuance of 3rd Tranche for Sale of Bonds – Principal amount of not to exceed \$140,000,000.00
- Preliminary Future Board of Education Updates – 3/1/21**
 - Approval of GMP Amendment #001 – South High School: Capital Improvements and Renovation Project – The Weitz Company \$5,847,191.00
 - Approval of Change Order #001 – New Elementary School: 1000 N. Fort Crook Rd. – Hausmann Construction \$87,385.15
- 25 Total Projects**
 - 25 Active Projects / 100% of Total Projects
 - 4 – Bid/Award
 - 5 – Closeout
 - 3 – Complete
 - 9 – Construction
 - 4 – Design
- Program Progress Overview**
 - Total Program Budget: \$409,900,000
 - Total Contract Amounts: \$310,286,194 or 75.70% of Program
 - Total Additional Commitments To Complete (Forecasted): \$99,613,806
 - Total Projected Commitments (Contract Amounts + Additional Commitments To Complete): \$310,286,194 + \$99,613,806 = \$409,900,000
 - Total Expenditure Amounts: \$158,309,766 or 38.62% of Program
- Program Contingency Summary**
 - Program Contingency Original Budget: \$39,764,454 or 9.70% of Program

- Approved Program Contingency Usage: \$35,038,850
- Forecasted Program Contingency: \$0
- Total (Approved + Forecasted) Contingency Usage: \$35,038,850
- $\$35,038,850 / \$409,900,000 = 8.55\%$
 - Current Trend under budget by 1.15%
- Budget Transfers Approved/Completed & Pending – Jan. 2021 to Feb. 2021:
 - Budget Transfer(s) Approved/Completed: #001 thru. #027
 - Budget Transfer(s) Pending: N/A


Economic Inclusion

- Total Applicable Program Contract Commitment Amounts: \$310,286,194
- Tier No. 01 Contract Commitments: \$9,415,674
- Tier No. 02 Contract Commitments: \$11,582,491
- Total SEBs Contract Commitments: \$20,998,165 or 6.77% of Current Contract Commitments
- Tier No. 01 Expenditures To Date: \$4,310,676
- Tier No. 02 Expenditures To Date: \$5,615,634
- Total SEBs Expenditures To Date % of Overall Contract Amount: 3.20%

Of Schools

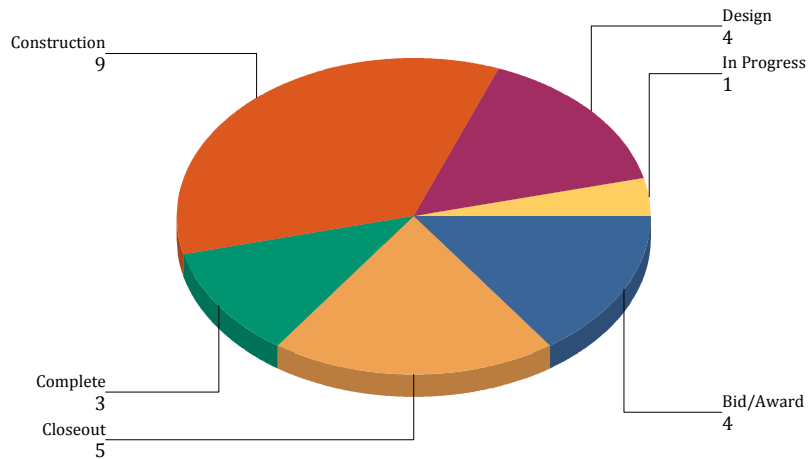

Current Budget

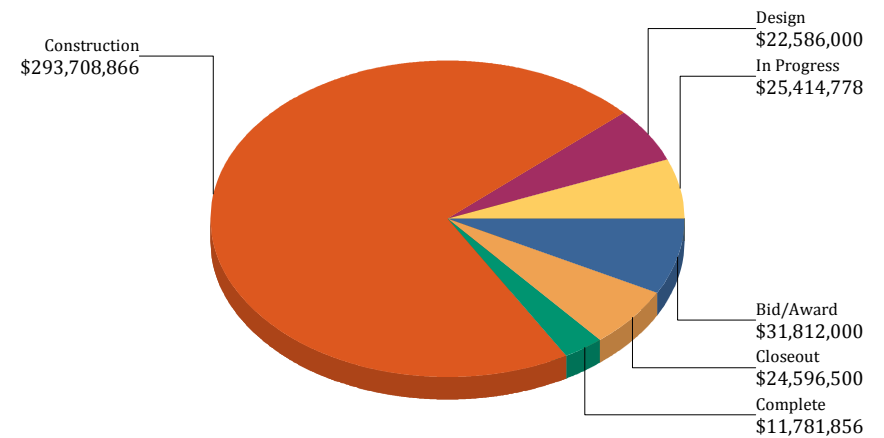

BUDGET

A

COST COMMITMENTS

B

C=B/A


Phase Description	# of Schools	Current Budget	Committed Costs	% Committed
Bid/Award	4	\$31,812,000	\$2,486,427	7.82%
Closeout	5	\$24,596,500	\$23,969,406	97.45%
Complete	3	\$11,781,856	\$11,778,756	99.97%
Construction	9	\$293,708,866	\$255,589,578	87.02%
Design	4	\$22,586,000	\$2,318,187	10.26%
In Progress	1	\$25,414,778	\$14,143,841	55.65%
Grand Totals:	26	\$409,900,000	\$310,286,194	75.70%



2018 Bond Program Program Report By Schools

Report Date: 2/22/2021

Value of Projects by Type

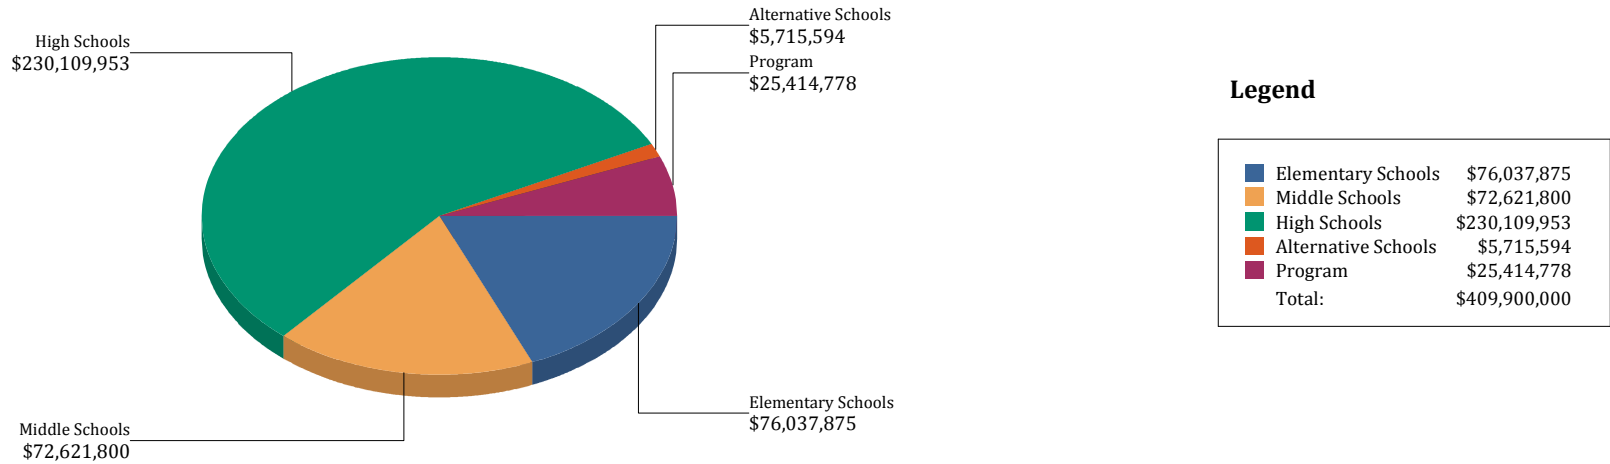

Elementary Schools	\$76,037,875
Middle Schools	\$72,621,800
High Schools	\$230,109,953
Alternative Schools	\$5,715,594
Program	\$25,414,778
Total:	\$409,900,000

Description	Phase	BUDGET			COST COMMITMENTS				EXPENDITURES		
		A	A1	A2=A+A1	B	C=B/A2	D	E=B+D	F=A2-E	G	H=G/A2
		Original Project Budget	Budget Transfer	Current Budget	Committed Cost	% Committed	Additional Commitments To Complete	Projected Commitments	Projected (Over) / Under	Expenditures To Date	% Expended
Elementary Schools											
1000 N. Fort Crook Rd. (New)	Construction	\$18,600,000	\$2,700,000	\$21,300,000	\$19,856,595	93.22%	\$1,443,405	\$21,300,000	\$0	\$12,756,071	59.89%
10th & Pine St. (New)	Construction	\$18,600,000	\$0	\$18,600,000	\$16,890,459	90.81%	\$1,709,541	\$18,600,000	\$0	\$6,131,192	32.96%
Adams	Design	\$1,766,400	\$0	\$1,766,400	\$136,260	7.71%	\$1,630,140	\$1,766,400	\$0	\$51,842	2.93%
Catlin	Closeout	\$2,410,800	\$54,900	\$2,465,700	\$2,385,671	96.75%	\$80,029	\$2,465,700	\$0	\$2,180,757	88.44%
Conestoga	Closeout	\$3,055,200	(\$300,000)	\$2,755,200	\$2,495,097	90.56%	\$260,103	\$2,755,200	\$0	\$2,133,552	77.44%
Edison	Construction	\$4,021,348	\$91,700	\$4,113,048	\$4,098,467	99.65%	\$14,581	\$4,113,048	\$0	\$3,068,577	74.61%
Highland	Construction	\$5,518,400	\$461,300	\$5,979,700	\$5,468,127	91.44%	\$511,573	\$5,979,700	\$0	\$1,264,332	21.14%
King	Complete	\$3,547,200	\$395,800	\$3,943,000	\$3,939,899	99.92%	\$3,101	\$3,943,000	\$0	\$3,935,380	99.81%
Masters	Construction	\$2,382,927	\$354,300	\$2,737,227	\$2,687,127	98.17%	\$50,100	\$2,737,227	\$0	\$1,772,702	64.76%
Pinewood	Closeout	\$5,929,200	(\$300,000)	\$5,629,200	\$5,432,430	96.50%	\$196,770	\$5,629,200	\$0	\$5,389,556	95.74%
Spring Lake	Design	\$6,748,400	\$0	\$6,748,400	\$1,036,292	15.36%	\$5,712,109	\$6,748,400	\$0	\$793,234	11.75%

Description	Phase	BUDGET			COST COMMITMENTS					EXPENDITURES	
		A	A1	A2=A+A1	B	C=B/A2	D	E=B+D	F=A2-E	G	H=G/A2
		Original Project Budget	Budget Transfer	Current Budget	Committed Cost	% Committed	Additional Commitments To Complete	Projected Commitments	Projected (Over) / Under	Expenditures To Date	% Expended
Elementary Schools		\$72,579,875	\$3,458,000	\$76,037,875	\$64,426,423	84.73%	\$11,611,452	\$76,037,875	\$0	\$39,477,194	51.92%
Middle Schools											
42nd & Y St. (New)	Construction	\$34,720,000	\$13,225,000	\$47,945,000	\$28,306,010	59.04%	\$19,638,990	\$47,945,000	\$0	\$3,677,913	7.67%
Lewis & Clark	Construction	\$14,014,800	\$0	\$14,014,800	\$12,860,556	91.76%	\$1,154,244	\$14,014,800	\$0	\$4,923,093	35.13%
Morton	Design	\$10,662,000	\$0	\$10,662,000	\$893,885	8.38%	\$9,768,115	\$10,662,000	\$0	\$248,602	2.33%
Middle Schools		\$59,396,800	\$13,225,000	\$72,621,800	\$42,060,451	57.92%	\$30,561,349	\$72,621,800	\$0	\$8,849,608	12.19%
High Schools											
156th & Ida St. (New)	Construction	\$77,911,087	\$10,649,473	\$88,560,560	\$82,478,634	93.13%	\$6,081,926	\$88,560,560	\$0	\$38,077,089	43.00%
60th & L St. (New)	Construction	\$74,121,660	\$16,336,871	\$90,458,531	\$82,943,604	91.69%	\$7,514,927	\$90,458,531	\$0	\$42,812,520	47.33%
Benson	Closeout	\$9,782,400	(\$1,600,000)	\$8,182,400	\$8,092,590	98.90%	\$89,810	\$8,182,400	\$0	\$7,834,470	95.75%
Bryan High	Closeout	\$6,714,000	(\$1,150,000)	\$5,564,000	\$5,563,618	99.99%	\$382	\$5,564,000	\$0	\$5,271,822	94.75%
Burke	Complete	\$7,161,600	(\$1,629,138)	\$5,532,462	\$5,532,462	100.00%	\$0	\$5,532,462	\$0	\$5,526,282	99.89%
Central	Bid/Award	\$5,872,800	\$0	\$5,872,800	\$782,811	13.33%	\$5,089,989	\$5,872,800	\$0	\$382,213	6.51%
North	Bid/Award	\$6,694,800	\$0	\$6,694,800	\$447,078	6.68%	\$6,247,722	\$6,694,800	\$0	\$281,062	4.20%
Northwest	Bid/Award	\$7,735,200	\$0	\$7,735,200	\$507,788	6.56%	\$7,227,412	\$7,735,200	\$0	\$316,756	4.10%
South	Bid/Award	\$11,509,200	\$0	\$11,509,200	\$748,750	6.51%	\$10,760,450	\$11,509,200	\$0	\$365,511	3.18%
High Schools		\$207,502,747	\$22,607,206	\$230,109,953	\$187,097,334	81.31%	\$43,012,618	\$230,109,953	\$0	\$100,867,726	43.83%
Alternative Schools											
Blackburn	Design	\$3,409,200	\$0	\$3,409,200	\$251,750	7.38%	\$3,157,450	\$3,409,200	\$0	\$74,092	2.17%
Transition Program	Complete	\$1,989,750	\$316,644	\$2,306,394	\$2,306,394	100.00%	\$0	\$2,306,394	\$0	\$2,301,443	99.79%
Alternative Schools		\$5,398,950	\$316,644	\$5,715,594	\$2,558,144	44.76%	\$3,157,450	\$5,715,594	\$0	\$2,375,535	41.56%
Program											
Program - Contingency	In Progress	\$39,764,454	(\$35,038,850)	\$4,725,604	\$0	0.00%	\$4,725,604	\$4,725,604	\$0	\$0	0.00%
Program - Hazardous Mtrls./Remediation	In Progress	\$4,988,600	(\$1,792,400)	\$3,196,200	\$0	0.00%	\$3,196,200	\$3,196,200	\$0	\$0	0.00%
Program - Test, Inspect, & Commish	In Progress	\$4,528,574	(\$2,775,600)	\$1,752,974	\$0	0.00%	\$1,752,974	\$1,752,974	\$0	\$0	0.00%
Program Mgmt. & Admin.	In Progress	\$15,740,000	\$0	\$15,740,000	\$14,143,841	89.86%	\$1,596,159	\$15,740,000	\$0	\$6,739,702	42.82%
Program		\$65,021,628	(\$39,606,850)	\$25,414,778	\$14,143,841	55.65%	\$11,270,936	\$25,414,778	\$0	\$6,739,702	26.52%
Grand Totals:		\$409,900,000	\$0	\$409,900,000	\$310,286,194	75.70%	\$99,613,806	\$409,900,000	\$0	\$158,309,766	38.62%



Program Contingency & Allocation

Usage & Forecast Report#

BT-#	To/From	Description	Test, Inspect, & Commish	Usage & Forecast %	Hazardous Mtrls.	Usage & Forecast %	Program Contingency	Usage & Forecast %	Total	Total Usage & Forecast %
Approved										
BT-001	To	Project #321510 - Transition Program School - Building Construction					(\$385,725)		(\$385,725)	
BT-002	To	Project #321508 - New High School 60th & L St. - Building Construction, Test/Inspect, Hazmat Remediation	(\$1,300,000)		(\$1,500,000)		(\$11,036,871)		(\$13,836,871)	
BT-003	To	Project #321509 - New High School 156th & Ida St. - Building Construction and Test/Inspect.	(\$1,300,000)				(\$9,349,473)		(\$10,649,473)	
BT-004	To	Project #321503 - King ES - Building Construction					(\$490,000)		(\$490,000)	
BT-005	From	Project #321504 - Benson HS - Building Construction					\$1,300,000		\$1,300,000	
BT-006	From	Project #321505 - Bryan HS - Building Construction					\$1,300,000		\$1,300,000	
BT-007	From	Project #321506 - Burke HS - Building Construction					\$900,000		\$900,000	
BT-008	From	Project #321511 - Pinewood ES - Building Construction					\$300,000		\$300,000	
BT-009	To	Project #321507 - New Elementary School 1000 N. Fort Crook Rd. - Building Construction					(\$2,700,000)		(\$2,700,000)	
BT-010	From	Project #321503 - King ES - Building Construction					\$175,000		\$175,000	
BT-011	From	Project #321505 - Benson HS - Building Construction					\$300,000		\$300,000	
BT-012	From	Project #321505 - Bryan HS - Building Construction					\$250,000		\$250,000	
BT-013	From	Project #321506 - Burke HS - Building Construction					\$300,000		\$300,000	
BT-014	To	Project #321518 - New Middle School 42nd & U St. - Building Construction					(\$9,225,000)		(\$9,225,000)	
BT-015	From	Project #321502 - Conestoga ES - Building Construction					\$300,000		\$300,000	
BT-016	To	Project #321514 - Masters ES - Building Construction					(\$300,000)		(\$300,000)	
BT-017	To	Project #321508 - New High School 60th & L St. - Building Construction					(\$2,500,000)		(\$2,500,000)	
BT-018	To	Project #321501 - Catlin ES - Hazmat Remediation and Commissioning	(\$20,600)		(\$34,300)				(\$54,900)	
BT-019	To	Project #321512 - Edison ES - Hazmat Remediation and Commissioning	(\$34,400)		(\$57,300)				(\$91,700)	
BT-020	To	Project #321514 - Masters ES - Hazmat Remediation and Commissioning	(\$20,400)		(\$33,900)				(\$54,300)	




Program Contingency & Allocation

Usage & Forecast Report#

BT-#	To/From	Description	Test, Inspect, & Commish	Usage & Forecast %	Hazardous Mtrls.	Usage & Forecast %	Program Contingency	Usage & Forecast %	Total	Total Usage & Forecast %
BT-021	From	Project #321506 - Burke HS - Building Construction					\$29,138		\$29,138	
BT-022	From	Project #321510 - Transition School - Building Construction					\$69,081		\$69,081	
BT-023	To	Project #321503 - King Elementary - Hazmat Remediation and Commissioning	(\$30,300)		(\$50,500)				(\$80,800)	
BT-024	To	Project #321518 - New Middle School 42nd & U St. - Building Construction					(\$3,000,000)		(\$3,000,000)	
BT-025	To	Project #321513 - Highland Elementary - Hazmat Remediation and Commissioning	(\$69,900)		(\$116,400)				(\$186,300)	
BT-026	To	Project #321518 - New Middle School 42nd & U St. - Building Construction					(\$1,000,000)		(\$1,000,000)	
BT-027	To	Project #321513 - Highland Elementary School - Building Construction					(\$275,000)		(\$275,000)	
Total Approved Changes:			(\$2,775,600)		(\$1,792,400)		(\$35,038,850)		(\$39,606,850)	
Total Changes			(\$2,775,600)		(\$1,792,400)		(\$35,038,850)		(\$39,606,850)	
Original Budget			\$4,528,574		\$4,988,600		\$39,764,454		\$49,281,628	
<i>Approved Budget Changes</i>			(\$2,775,600)	0.7%	(\$1,792,400)	0.4%	(\$35,038,850)	8.3%	(\$39,606,850)	9.7%
<i>Forecast Budget Changes</i>			\$0	0.0%	\$0	0.0%	\$0	0.0%	\$0	0.0%
Revised Projected Budget			\$1,752,974		\$3,196,200		\$4,725,604		\$9,674,778	

Adams

CASH-FLOW

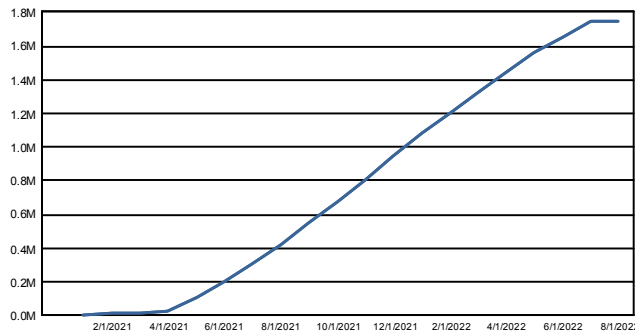

COMMENTS

The Schematic Design package was approved by the Board of Education in January 2021. The project is currently in the design development phase.

SCOPE

3420 North 78th Street
Omaha, NE 68134-5099
Phone: (402) 572-9072

The Adams Elementary School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Adams	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$1,472,000	\$1,472,000	\$0	\$0
Contingency	\$161,920	\$161,920	\$0	\$0
Design	\$125,414	\$125,414	\$0	\$49,282
FF&E	\$0	\$0	\$0	\$0
Misc.	\$7,066	\$7,066	\$0	\$2,560
TOTAL:	\$1,766,400	\$1,766,400	\$0	\$51,842


GENERAL INFORMATION

ARCHITECT: KPE Engineers

CONTRACTOR: CM@R - The Weitz Company

Catlin

CASH-FLOW

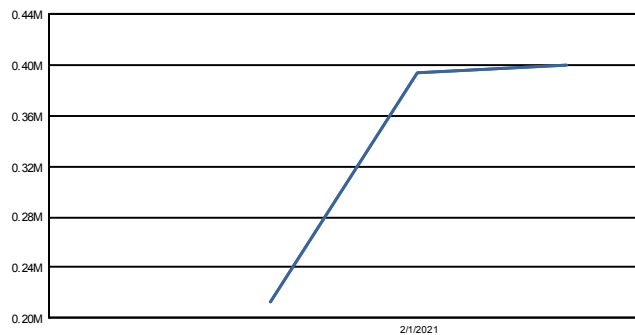

COMMENTS

Substantial completion was approved by the Board of Education on January 21, 2021. The project is currently in the closeout phase with punchlist items being finalized.

SCOPE

12736 Marinda Street
Omaha, NE 68144-2648
Phone: (402) 697-0414

The Catlin Elementary School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Catlin	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$2,232,924	\$2,232,924	\$0	\$1,997,154
Contingency	\$0	\$0	\$0	\$0
Design	\$171,167	\$171,167	\$0	\$134,344
FF&E	\$0	\$0	\$0	\$0
Misc.	\$61,609	\$61,609	\$0	\$49,259
TOTAL:	\$2,465,700	\$2,465,700	\$0	\$2,180,757


GENERAL INFORMATION

ARCHITECT: The Schemmer Associates

CONTRACTOR: CM@R - Boyd Jones

Conestoga

CASH-FLOW

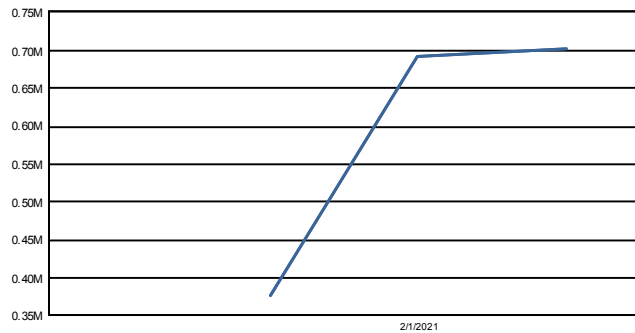

COMMENTS

Substantial completion was approved by the Board of Education on January 21, 2021. The project is currently in the closeout phase with punchlist items being finalized.

SCOPE

2115 Burdette Street
Omaha, NE 68110
Phone: (402) 344-7147

The Conestoga Elementary School scope of work includes capital improvements to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Conestoga	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$2,247,727	\$2,247,727	\$0	\$1,903,699
Contingency	\$217,329	\$217,329	\$0	\$0
Design	\$216,919	\$216,919	\$0	\$170,253
FF&E	\$0	\$0	\$0	\$0
Misc.	\$73,225	\$73,225	\$0	\$59,600
TOTAL:	\$2,755,200	\$2,755,200	\$0	\$2,133,552


GENERAL INFORMATION

ARCHITECT: The Schemmer Associates

CONTRACTOR: CM@R - Boyd Jones

Edison

CASH-FLOW

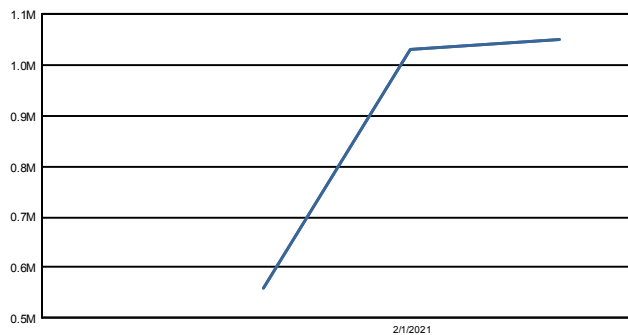

COMMENTS

The construction work on the exterior building, final electrical, and final mechanical is in progress at the mechanical room, new administration addition, and new classroom addition. The substantial completion for the addition work is projected to be submitted in March 2021. The renovation work at the existing administration area and classroom mechanical equipment installation is scheduled to be complete in Summer 2021.

SCOPE

2303 North 97th Street
Omaha, NE 68134-5609
Phone: (402) 392-7310

The Edison Elementary School scope of work includes capital improvement with an addition to the existing building. The plan provides for finishing of the safe area into two (2) classrooms, a three (3) classroom addition, heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Edison	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$3,755,446	\$3,755,446	\$0	\$2,766,239
Contingency	\$0	\$0	\$0	\$0
Design	\$279,530	\$279,530	\$0	\$254,356
FF&E	\$0	\$0	\$0	\$0
Misc.	\$78,072	\$78,072	\$0	\$47,982
TOTAL:	\$4,113,048	\$4,113,048	\$0	\$3,068,577


GENERAL INFORMATION

ARCHITECT: Jackson-Jackson

CONTRACTOR: CM@R - Boyd Jones

Highland

CASH-FLOW

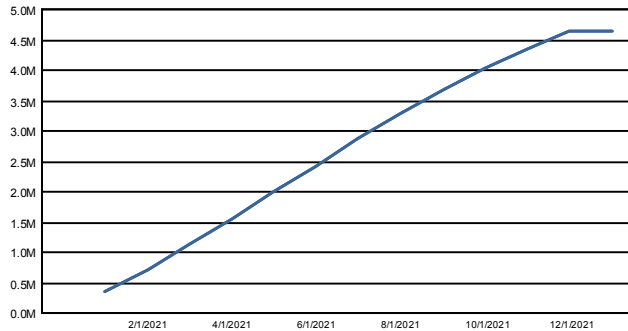

COMMENTS

The construction work is in progress on the new addition building structure and will continue through Spring 2021. The interior renovation scope of work is in progress, and will continue through June 2021.

SCOPE

2625 Jefferson Street
Omaha, NE 68107-2378
Phone: (402) 734-5711

The Highland Elementary School scope of work includes a new addition and capital improvement to the existing building. The plan provides for an eleven (11) classroom addition to alleviate overcrowding along with heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Highland	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,296,414	\$5,296,414	\$0	\$948,843
Contingency	\$0	\$0	\$0	\$0
Design	\$464,926	\$464,926	\$0	\$287,390
FF&E	\$0	\$0	\$0	\$0
Misc.	\$218,360	\$218,360	\$0	\$28,098
TOTAL:	\$5,979,700	\$5,979,700	\$0	\$1,264,332

GENERAL INFORMATION

ARCHITECT: Leo A Daly

CONTRACTOR: CM@R - Hausmann

King

CASH-FLOW

COMMENTS

Substantial completion was approved by the Board of Education on April 15, 2020. Project closeout documents have been submitted and transmitted to OPS.

SCOPE

3706 Maple Street
Omaha, NE 68111-3195
Phone: (402) 457-5723

The King Elementary School scope of work includes capital improvements to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

King	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$3,723,846	\$3,723,846	\$0	\$3,720,745
Contingency	\$0	\$0	\$0	\$0
Design	\$202,189	\$202,189	\$0	\$197,670
FF&E	\$0	\$0	\$0	\$0
Misc.	\$16,965	\$16,965	\$0	\$16,965
TOTAL:	\$3,943,000	\$3,943,000	\$0	\$3,935,380


GENERAL INFORMATION

ARCHITECT: The Schemmer Associates

CONTRACTOR: Elkhorn West Construction

Masters

CASH-FLOW

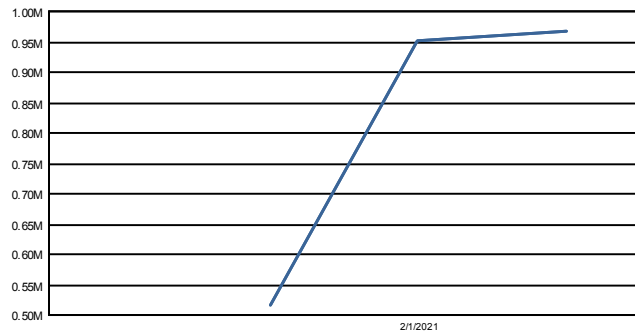

COMMENTS

The interior finish work in the new addition is near completion. The substantial completion for the addition work is projected to be submitted in March 2021.

SCOPE

5505 North 99th Street
Omaha, NE 68134-1599
Phone: (402) 572-1027

The Masters Elementary School scope of work includes capital improvements with an addition to the existing building. The plan provides for finishing of the safe area into two (2) classrooms, a four (4) classroom addition heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Masters	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$2,477,753	\$2,477,753	\$0	\$1,577,939
Contingency	\$0	\$0	\$0	\$0
Design	\$197,503	\$197,503	\$0	\$161,852
FF&E	\$0	\$0	\$0	\$0
Misc.	\$61,971	\$61,971	\$0	\$32,911
TOTAL:	\$2,737,227	\$2,737,227	\$0	\$1,772,702


GENERAL INFORMATION

ARCHITECT: Jackson-Jackson

CONTRACTOR: CM@R - Boyd Jones

Pinewood

CASH-FLOW

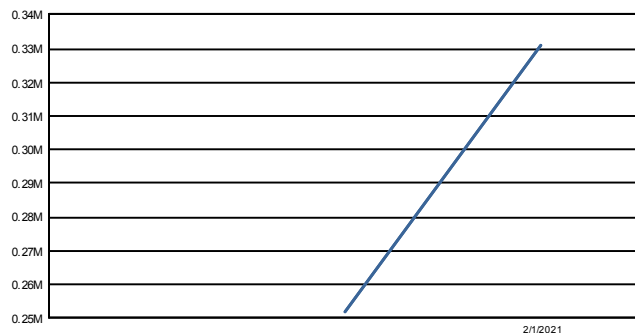

COMMENTS

The substantial completion was approved by the Board of Education on October 19, 2020. The Contractor has moved off-site and is finishing up the remaining punch list items along with additional items that were added to the scope of work due to District request needs.

SCOPE

6717 North 63rd Street
Omaha, NE 68152-2210
Phone: (402) 561-6000

The Pinewood Elementary School scope of work includes capital improvement with an addition to the existing building. The plan will provide for a three (3) classroom addition, interior modifications to eliminate the 'Open Plan' layout, heating, ventilation, air-condition system updates to the existing building along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Pinewood	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,093,751	\$5,093,751	\$0	\$4,884,757
Contingency	\$0	\$0	\$0	\$0
Design	\$436,093	\$436,093	\$0	\$408,323
FF&E	\$0	\$0	\$0	\$0
Misc.	\$99,356	\$99,356	\$0	\$96,476
TOTAL:	\$5,629,200	\$5,629,200	\$0	\$5,389,556


GENERAL INFORMATION

ARCHITECT: Alley Poyner Macchietto

CONTRACTOR: Meco-Henne Contracting

Spring Lake

CASH-FLOW

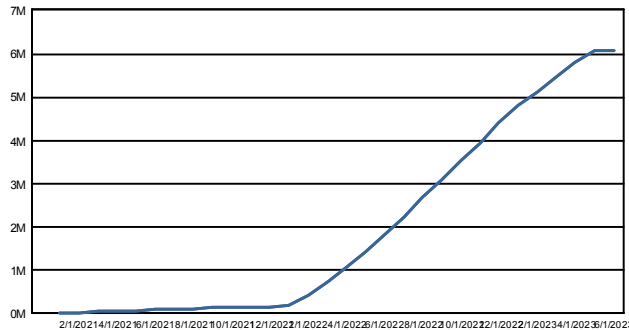

COMMENTS

The project is currently in the construction document phase with the projected bid/award to be completed in Summer 2021. The construction document design package is scheduled to go to the Board of Education in Spring 2021.

SCOPE

4215 South 20th Street
Omaha, NE 68107-2098
Phone: (402) 734-1833

The Spring Lake Elementary School scope of work includes a new addition and capital improvement to the existing building. The plan provides for a ten (10) classroom addition to alleviate overcrowding, heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS


Spring Lake	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,787,000	\$5,787,000	\$0	\$473,000
Contingency	\$382,612	\$382,612	\$0	\$0
Design	\$551,794	\$551,794	\$0	\$308,736
FF&E	\$0	\$0	\$0	\$0
Misc.	\$26,994	\$26,994	\$0	\$11,498
TOTAL:	\$6,748,400	\$6,748,400	\$0	\$793,234

GENERAL INFORMATION

ARCHITECT: The Schemmer Associates
CONTRACTOR: CM@R - Hausmann

10th & Pine St. (New)

CASH-FLOW

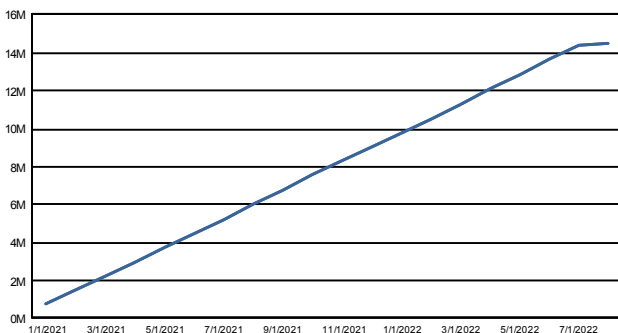

COMMENTS

The lower level slab on grade concrete work is scheduled to be installed along with the 2nd floor deck pour in late February 2021. Starting in March 2021, the exterior framing, final steel and masonry, and interior framing and fire sprinkler pipe work is scheduled to begin.

SCOPE

The 10th and Pine Street Elementary School scope of work includes construction of a new 600-student capacity facility.

BUDGET /COST STATUS


10th & Pine St. (New)	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$15,468,912	\$15,468,912	\$0	\$5,082,095
Contingency	\$857,261	\$857,261	\$0	\$0
Design	\$1,200,000	\$1,200,000	\$0	\$924,522
FF&E	\$825,000	\$825,000	\$0	\$0
Misc.	\$248,827	\$248,827	\$0	\$124,575
TOTAL:	\$18,600,000	\$18,600,000	\$0	\$6,131,192

GENERAL INFORMATION

ARCHITECT: Jackson-Jackson
CONTRACTOR: CM@R - Darland

1000 N. Fort Crook Rd. (New)

CASH-FLOW

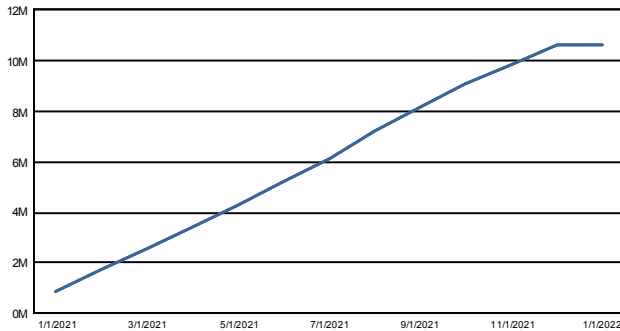

COMMENTS

The drywall installation is ongoing throughout academic wing and the casework is expected to arrive in March 2021. The mechanical equipment including heat pumps continue to be installed and hooked up throughout the building. The rough-in work continues in the administrative wing and the drywall work is scheduled to begin in this area in Spring 2021.

SCOPE

The 1000 North Fort Crook Road Elementary School scope of work includes construction of a new 600-student capacity facility.

BUDGET /COST STATUS


1000 N. Fort Crook Rd. (New)	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$18,313,361	\$18,313,361	\$0	\$11,579,312
Contingency	\$617,594	\$617,594	\$0	\$0
Design	\$1,279,238	\$1,279,238	\$0	\$1,047,554
FF&E	\$825,000	\$825,000	\$0	\$0
Misc.	\$264,807	\$264,807	\$0	\$129,204
TOTAL:	\$21,300,000	\$21,300,000	\$0	\$12,756,071

GENERAL INFORMATION

ARCHITECT: Kenneth Hahn Architects
CONTRACTOR: CM@R - Hausmann

Lewis & Clark

CASH-FLOW

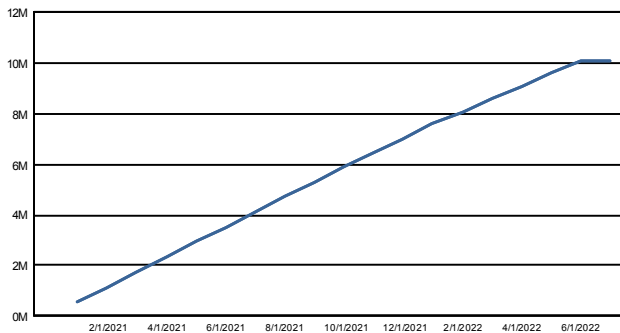

COMMENTS

In the new addition, ongoing interior work continues which includes drywall and painting. The exterior work continues which includes installation of new windows and brick masonry. The boiler room work is scheduled to start in April 2021 which will begin with abatement and demolition work.

SCOPE

6901 Burt Street
Omaha, NE 68132
Phone: (402) 557-4300
The Lewis and Clark Middle School scope of work includes a new addition and capital improvement to the existing building. The plan provides for a fifteen (15) classroom addition, heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS


Lewis & Clark	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$12,104,000	\$12,104,000	\$0	\$4,194,831
Contingency	\$560,124	\$560,124	\$0	\$0
Design	\$1,160,051	\$1,160,051	\$0	\$698,329
FF&E	\$0	\$0	\$0	\$0
Misc.	\$190,625	\$190,625	\$0	\$29,933
TOTAL:	\$14,014,800	\$14,014,800	\$0	\$4,923,093

GENERAL INFORMATION

ARCHITECT: Alley Poyner Macchietto
CONTRACTOR: CM@R - Vrana

Morton

CASH-FLOW

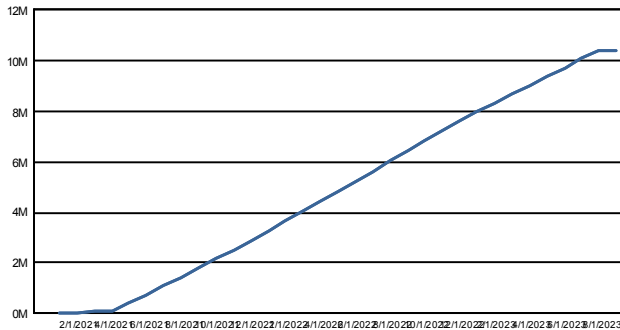

COMMENTS

The project is currently in the construction document phase with the projected bid/award to be completed in Spring 2021. The construction document design package is scheduled to go to the Board of Education in March/April 2021.

SCOPE

4606 Terrace Drive
Omaha, NE 68134
Phone: (402) 557-4700

The Morton Middle School scope of work includes a new addition and capital improvement to the existing building. The plan provides for a nine (9) classroom addition, heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS


Morton	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$9,155,000	\$9,155,000	\$0	\$350
Contingency	\$600,617	\$600,617	\$0	\$0
Design	\$863,735	\$863,735	\$0	\$233,452
FF&E	\$0	\$0	\$0	\$0
Misc.	\$42,648	\$42,648	\$0	\$14,800
TOTAL:	\$10,662,000	\$10,662,000	\$0	\$248,602

GENERAL INFORMATION

ARCHITECT: BVH Architecture
CONTRACTOR: CM@R - MCL Construction

42nd & Y St. (New)

CASH-FLOW

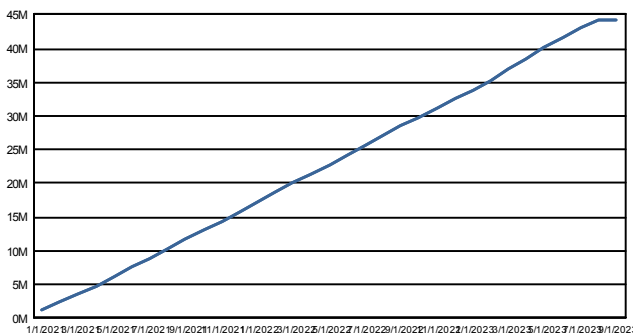

COMMENTS

The project is currently in the final stages of the Construction Document Design Phase. The final permit has been submitted to the City. Footings were finalized in February 2021. Site utilities work has started and is schedule to be substantially complete in February 2021. Precast panels are scheduled to arrive on site in March 2021. Structural steel is also scheduled to arrive on site in March 2021. Structural masonry walls are scheduled to start work in March 2021.

SCOPE

The 42nd and U Street Middle School scope of work includes construction of a new 1000-student capacity facility.

BUDGET /COST STATUS


42nd & Y St. (New)	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$41,025,000	\$41,025,000	\$0	\$2,324,481
Contingency	\$2,548,465	\$2,548,465	\$0	\$0
Design	\$2,281,000	\$2,281,000	\$0	\$1,271,818
FF&E	\$1,740,000	\$1,740,000	\$0	\$0
Misc.	\$350,535	\$350,535	\$0	\$81,615
TOTAL:	\$47,945,000	\$47,945,000	\$0	\$3,677,913

GENERAL INFORMATION

ARCHITECT: RDG Planning & Design
CONTRACTOR: CM@R - McCarthy

Benson

CASH-FLOW

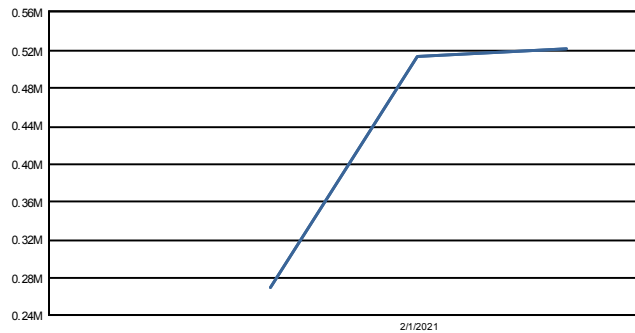

COMMENTS

The construction work is complete and the closeout documentation is being finalized. Substantial completion was approved by the Board of Education on February 1, 2021.

SCOPE

5120 Maple Street
Omaha, NE 68104
Phone: (402) 557-3000

The Benson High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Benson	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$7,403,796	\$7,403,796	\$0	\$7,158,292
Contingency	\$0	\$0	\$0	\$0
Design	\$678,835	\$678,835	\$0	\$583,535
FF&E	\$0	\$0	\$0	\$0
Misc.	\$99,769	\$99,769	\$0	\$92,644
TOTAL:	\$8,182,400	\$8,182,400	\$0	\$7,834,470


GENERAL INFORMATION

ARCHITECT: Leo A Daly

CONTRACTOR: CM@R - Hausmann

Bryan High

CASH-FLOW

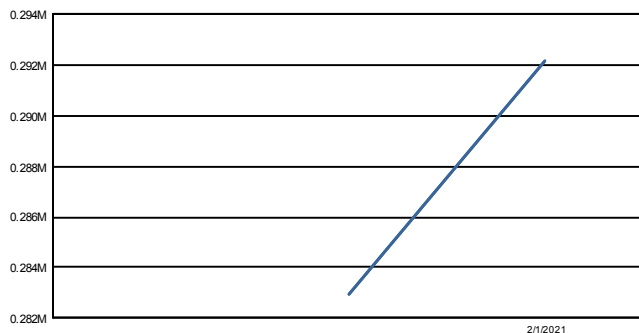

COMMENTS

The construction work is complete and the closeout documentation is being finalized. Substantial completion was approved by the Board of Education on December 14, 2020.

SCOPE

4700 Giles Road
Omaha, NE 68157-2699
Phone: (402) 557-3100

The Bryan High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Bryan High	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,161,730	\$5,161,730	\$0	\$4,949,152
Contingency	\$0	\$0	\$0	\$0
Design	\$398,000	\$398,000	\$0	\$318,400
FF&E	\$0	\$0	\$0	\$0
Misc.	\$4,270	\$4,270	\$0	\$4,270
TOTAL:	\$5,564,000	\$5,564,000	\$0	\$5,271,822

GENERAL INFORMATION

ARCHITECT: TACK Architects

CONTRACTOR: CM@R - Hausmann

Burke

CASH-FLOW

COMMENTS

SCOPE

Substantial completion was approved by the Board of Education on October 21, 2019. Project closeout documents have been submitted and transmitted to OPS.

12200 Burke Blvd.
Omaha, NE 68154
Phone: (402) 557-3200

The Burke High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Burke	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,012,307	\$5,012,307	\$0	\$5,116,970
Contingency	\$0	\$0	\$0	\$0
Design	\$479,336	\$479,336	\$0	\$371,673
FF&E	\$0	\$0	\$0	\$0
Misc.	\$40,819	\$40,819	\$0	\$37,639
TOTAL:	\$5,532,462	\$5,532,462	\$0	\$5,526,282

GENERAL INFORMATION

ARCHITECT: KPE Engineers


CONTRACTOR: CM@R - Weitz

Central

CASH-FLOW

COMMENTS

SCOPE

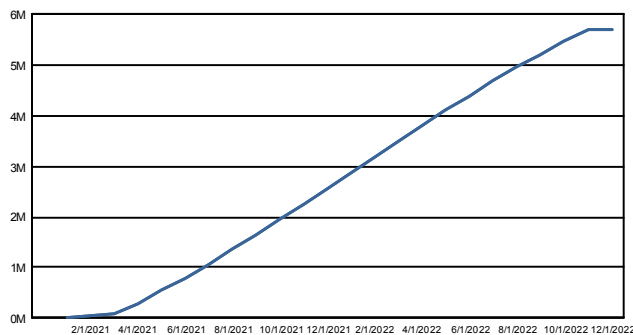

The project is currently in the construction document phase with the projected bid/award to be completed in Spring 2021. The construction document design package is scheduled to go to the Board of Education in March/April 2021.

124 North 20th Street
Omaha, NE 68102
Phone: (402) 557-3300

The Central High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Central	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$4,894,000	\$4,894,000	\$0	\$2,811
Contingency	\$216,349	\$216,349	\$0	\$0
Design	\$738,960	\$738,960	\$0	\$379,402
FF&E	\$0	\$0	\$0	\$0
Misc.	\$23,491	\$23,491	\$0	\$0
TOTAL:	\$5,872,800	\$5,872,800	\$0	\$382,213


GENERAL INFORMATION

ARCHITECT: Alley Poyner Macchietto

CONTRACTOR: CM@R - The Weitz Company

North

CASH-FLOW

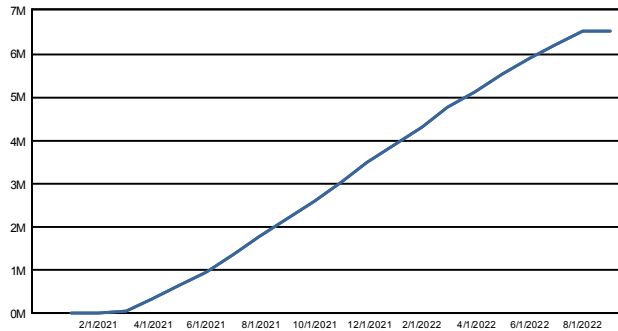

COMMENTS

The project is currently in the construction document phase with the projected bid/award to be completed in Spring 2021. The construction document design package is scheduled to go to the Board of Education in March/April 2021.

SCOPE

4410 North 36th Street
Omaha, NE 68111
Phone: (402) 557-3400

The North High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

North	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$5,579,000	\$5,579,000	\$0	\$0
Contingency	\$613,690	\$613,690	\$0	\$0
Design	\$475,331	\$475,331	\$0	\$274,162
FF&E	\$0	\$0	\$0	\$0
Misc.	\$26,779	\$26,779	\$0	\$6,900
TOTAL:	\$6,694,800	\$6,694,800	\$0	\$281,062


GENERAL INFORMATION

ARCHITECT: Jackson-Jackson

CONTRACTOR: CM@R - Hausmann

Northwest

CASH-FLOW

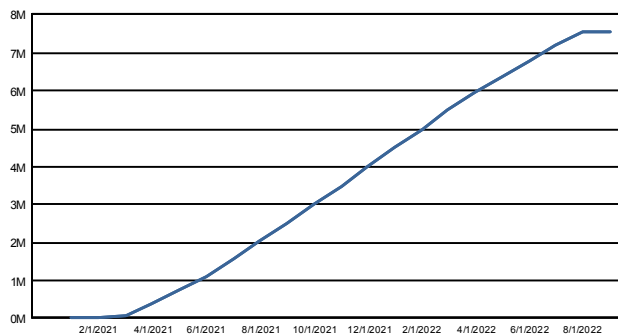

COMMENTS

The project is currently in the construction document phase with the projected bid/award to be completed in Spring 2021. The construction document design package is scheduled to go to the Board of Education in March/April 2021.

SCOPE

8204 Crown Point Avenue
Omaha, NE 68134
Phone: (402) 557-3500

The Northwest High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Northwest	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$6,446,000	\$6,446,000	\$0	\$0
Contingency	\$709,060	\$709,060	\$0	\$0
Design	\$549,199	\$549,199	\$0	\$316,756
FF&E	\$0	\$0	\$0	\$0
Misc.	\$30,941	\$30,941	\$0	\$0
TOTAL:	\$7,735,200	\$7,735,200	\$0	\$316,756


GENERAL INFORMATION

ARCHITECT: Jackson-Jackson

CONTRACTOR: CM@R - Hausmann

South

CASH-FLOW

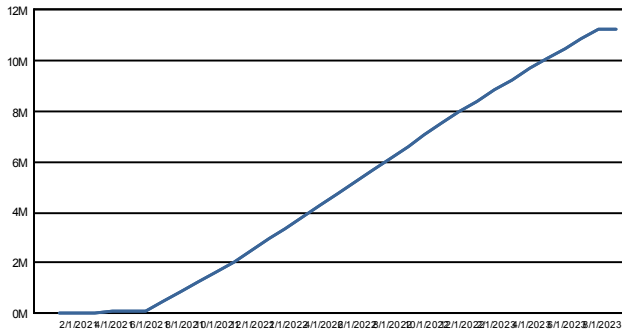

COMMENTS

An early GMP Amendment package for mechanical and electrical work is scheduled to go to the Board of Education for approval in March 2021. The project is currently in the construction document phase with the projected bid/award to be completed in Spring 2021. The construction document design package is scheduled to go to the Board of Education in March/April 2021.

SCOPE

4519 South 24th Street
Omaha, NE 68107
Phone: (402) 557-3600

The South High School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

South	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$9,591,000	\$9,591,000	\$0	\$0
Contingency	\$1,055,010	\$1,055,010	\$0	\$0
Design	\$817,153	\$817,153	\$0	\$365,511
FF&E	\$0	\$0	\$0	\$0
Misc.	\$46,037	\$46,037	\$0	\$0
TOTAL:	\$11,509,200	\$11,509,200	\$0	\$365,511


GENERAL INFORMATION

ARCHITECT: BCDM Architects

CONTRACTOR: CM@R - The Weitz Company

60th & L St. (New)

CASH-FLOW

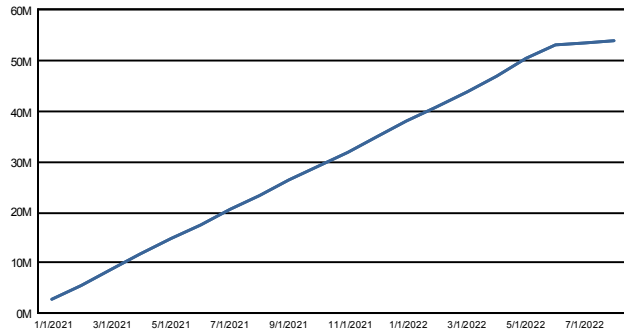

COMMENTS

Miscellaneous steel continues to be installed. The masonry walls continue to be installed in the locker room areas. Framing work for the administration area has started. The site grading is nearing completion with the rough grade for the baseball field, softball field, and the track area being completed. Mechanical, electrical, and plumbing (MEP) rough-in work continues in the west and east academic wings. Drywall work is complete on the 2nd floor and continues on the 1st floor. Painting is complete on the 3rd floor academic wing and painting on the 2nd floor academic wing has started. The restroom tile and corridor tile for the 3rd floor west academic wing is complete and work has now started on the east academic wing. The ceiling grid at the west academic wing 3rd floor is complete and starting on the east academic wing. Light fixture work has started to be installed on the west side of the 3rd floor academic wing. Exterior metal framing and sheathing is complete at the teacher planning area. The storefront windows are installed in the academic wings. Pouring of the concrete floors in the auditorium area is scheduled to start in March 2021. Roofing work at the commons area is complete and has now moved on to the gym area. Brick masonry installation at the dock area is scheduled to start in March 2021. The elevator in the middle of the academic wing continues to be installed.

SCOPE

The 60th and L Street High School scope of work includes construction of a new 1500-student capacity facility.

BUDGET /COST STATUS


60th & L St. (New)	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$79,104,921	\$79,104,921	\$0	\$38,280,155
Contingency	\$2,481,722	\$2,481,722	\$0	\$0
Design	\$5,194,879	\$5,194,879	\$0	\$4,151,094
FF&E	\$3,014,923	\$3,014,923	\$0	\$0
Misc.	\$662,086	\$662,086	\$0	\$381,270
TOTAL:	\$90,458,531	\$90,458,531	\$0	\$42,812,520

GENERAL INFORMATION

ARCHITECT: DLR Group
CONTRACTOR: CM@R - McCarthy

156th & Ida St. (New)

CASH-FLOW

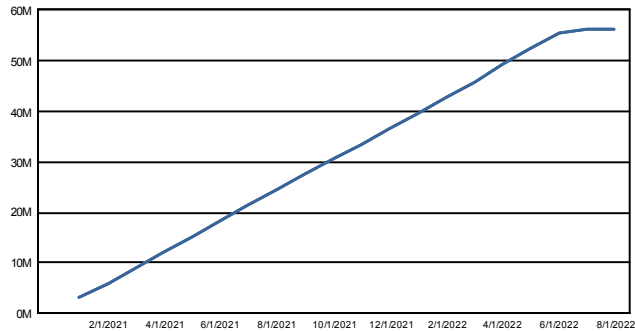

COMMENTS

Masonry walls continue in the YMCA, kitchen area, and locker rooms. Miscellaneous steel continues to be installed. Roofing at the administration area is complete and will move to the kitchen and mechanical room area. Fireproofing is complete in the administration area and will move on to the Auditorium area. The Mechanical, Electrical, and Plumbing (MEP) rough-ins for the administrative area has started. Brick masonry installation is being installed at the music area. The MEP rough-ins continue in the west and east academic wings. Pouring of the concrete floor in the locker room areas is scheduled for March 2021. Storefront windows have been installed in the west and east academic wings. Drywall of the classrooms in the east academic wing is complete. Painting of the drywall in the west academic wing is complete and will move to the east academic wing. The restroom tile and corridor tile in the west academic wing is complete and has moved on to the east academic wing. Casework for the west academic wing has started. Ceiling grid in the west academic wing is complete and moved to the east academic wing. Light fixture work has started to be installed in the west academic wing. Exterior metal panels has started to be installed in the east academic wing. Site grading for the sports fields will continue through March 2021. The pool area in the YMCA has started underground piping.

SCOPE

The 156th and Ida Street High School scope of work includes construction of a new 1500-student capacity facility. Additional square footage has been added to the plan to accommodate a partnership with the YMCA of Greater Omaha (YMCA). Through this partnership, OPS would contribute space for a cycling studio, child watch and YMCA offices, needed by the YMCA for their programs. The YMCA would contribute funds to support the construction of an aquatics center, consisting of a 6 swim lane pool with spectator seating and leisure pool area. The YMCA and OPS would share access to the Auxiliary Gym, Wrestling/Multi-Purpose Room, Weight/Fitness Room, Dance Aerobics/Multi-Purpose Room, Community Room. The shared Weight/Fitness Room and Dance Aerobics/Multi-Purpose Room would increase in size to align with the YMCA programs and equipment needs.

BUDGET /COST STATUS


156th & Ida St. (New)	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$77,242,045	\$77,242,045	\$0	\$32,897,071
Contingency	\$1,939,998	\$1,939,998	\$0	\$0
Design	\$5,717,772	\$5,717,772	\$0	\$4,853,991
FF&E	\$3,003,517	\$3,003,517	\$0	\$0
Misc.	\$657,228	\$657,228	\$0	\$326,027
TOTAL:	\$88,560,560	\$88,560,560	\$0	\$38,077,089

GENERAL INFORMATION

ARCHITECT: BCDM Architects
CONTRACTOR: CM@R - Sampson

Blackburn

CASH-FLOW

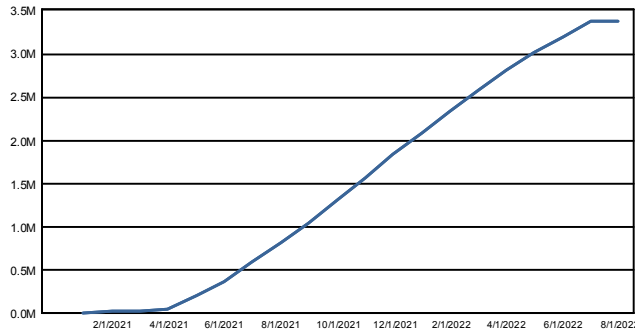

COMMENTS

The Schematic Design package was approved by the Board of Education in January 2021. The project is currently in the design development phase.

SCOPE

2606 Hamilton Street
Omaha, NE 68131
Phone: (402) 344-3385

The Blackburn Alternative School scope of work includes capital improvement to the existing building. The plan provides for heating, ventilation and air-condition system updates along with other improvements to increase building system efficiencies.

BUDGET /COST STATUS

Blackburn	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$2,841,000	\$2,841,000	\$0	\$0
Contingency	\$312,510	\$312,510	\$0	\$0
Design	\$242,053	\$242,053	\$0	\$72,142
FF&E	\$0	\$0	\$0	\$0
Misc.	\$13,637	\$13,637	\$0	\$1,950
TOTAL:	\$3,409,200	\$3,409,200	\$0	\$74,092

GENERAL INFORMATION

ARCHITECT: KPE Engineers

CONTRACTOR: CM@R - The Weitz Company

Transition Program

CASH-FLOW

COMMENTS

SCOPE

The construction work is complete and the closeout documentation is being finalized. Substantial completion was approved by the Board of Education on October 21, 2019.

The Transition program scope of work includes the capital to complete tenant improvement work needed to accommodate the relocation of the transition program from the Paralyzed Veterans of America location as well as the relocation of the transition program from the Career Center.

BUDGET /COST STATUS

Transition Program	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Construction	\$2,089,176	\$2,089,176	\$0	\$2,084,225
Contingency	\$0	\$0	\$0	\$0
Design	\$154,548	\$154,548	\$0	\$154,548
FF&E	\$61,520	\$61,520	\$0	\$61,520
Misc.	\$1,151	\$1,151	\$0	\$1,151
TOTAL:	\$2,306,394	\$2,306,394	\$0	\$2,301,443

GENERAL INFORMATION

ARCHITECT: BVH Architecture


CONTRACTOR: Midwest DCM

Program Mgmt. & Admin.

CASH-FLOW

COMMENTS

SCOPE

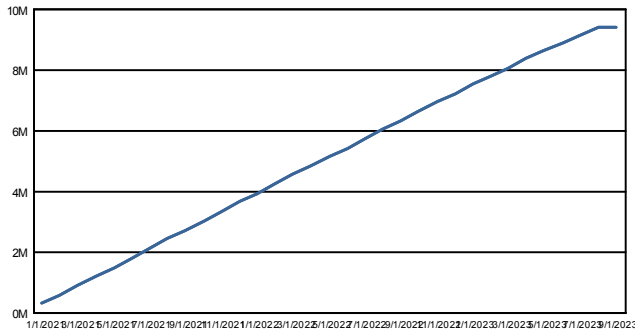

Program Management and Administration is for the general bond program construction management and administration services.

BUDGET /COST STATUS

Program Mgmt. & Admin.	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Contingency	\$443,318	\$443,318	\$0	\$0
FF&E	\$150,000	\$150,000	\$0	\$2,745
Misc.	\$15,146,682	\$15,146,682	\$0	\$6,736,957
TOTAL:	\$15,740,000	\$15,740,000	\$0	\$6,739,702

GENERAL INFORMATION


ARCHITECT: N/A
CONTRACTOR: Jacobs

Program - Contingency

CASH-FLOW

COMMENTS

SCOPE

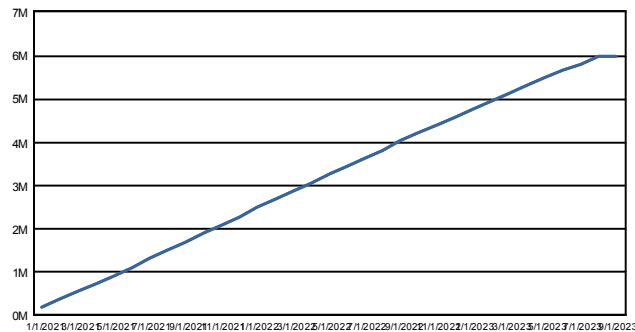

Program Non-Spend Contingency is for the general bond program general contingency budget allocations; testing, inspection, and commissioning budget allocations; hazardous materials remediation budget allocations.

BUDGET /COST STATUS

Program - Contingency	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Contingency	\$4,725,604	\$4,725,604	\$0	\$0
TOTAL:	\$4,725,604	\$4,725,604	\$0	\$0

GENERAL INFORMATION


ARCHITECT: N/A
CONTRACTOR: N/A

Program - Hazardous Mtrls./Remediation

CASH-FLOW

COMMENTS

SCOPE

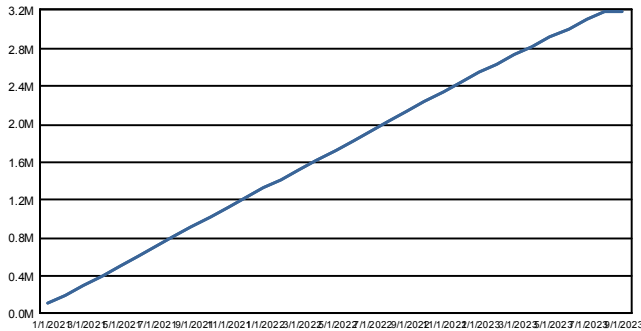

Program Non-Spend Contingency is for the general bond program general contingency budget allocations; testing, inspection, and commissioning budget allocations; hazardous materials remediation budget allocations.

BUDGET /COST STATUS

Program - Hazardous Mtrls./Remediation	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Misc.	\$3,196,200	\$3,196,200	\$0	\$0
TOTAL:	\$3,196,200	\$3,196,200	\$0	\$0

GENERAL INFORMATION


ARCHITECT: N/A
CONTRACTOR: N/A

Program - Test, Inspect, & Commish

CASH-FLOW

COMMENTS

SCOPE

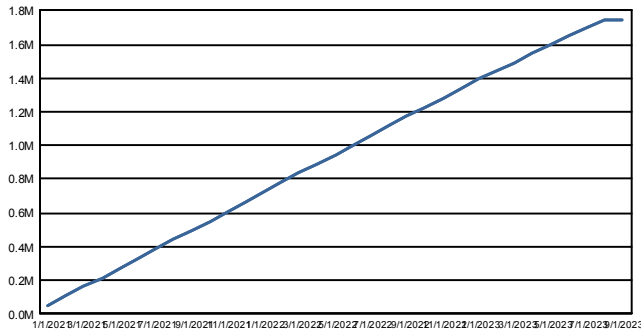

Program Non-Spend Contingency is for the general bond program general contingency budget allocations; testing, inspection, and commissioning budget allocations; hazardous materials remediation budget allocations.

BUDGET /COST STATUS

Program - Test, Inspect, & Commish	BUDGET	PROJECTED COSTS	(OVER)/UNDER	ACTUALS
Misc.	\$1,752,974	\$1,752,974	\$0	\$0
TOTAL:	\$1,752,974	\$1,752,974	\$0	\$0

GENERAL INFORMATION

ARCHITECT: N/A
CONTRACTOR: N/A



2018 Bond Program - Summary By Category

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Category	CONTRACT COMMITMENTS					EXPENDITURES				
	A Total Contract Amount (\$)	B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$) Amount	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$) Amount	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Architect/Engineer:	\$23,962,370	\$377,066	\$1,455,692	\$1,832,758	7.65%	\$301,507	79.96%	\$599,350	41.17%	3.76%
Construction:	\$268,747,372	\$7,605,471	\$9,521,628	\$17,127,099	6.37%	\$3,510,292	46.15%	\$4,866,725	51.11%	3.12%
Owner Administration:	\$512,565	\$0	\$312,598	\$312,598	60.99%	\$0	0.00%	\$31,158	9.97%	6.08%
Printing & Advertisement:	\$72,586	\$5,864	\$0	\$5,864	8.08%	\$5,864	100.00%	\$0	0.00%	8.08%
Program Mgmt & Admin:	\$13,558,690	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Temp Housing, Utilities, Moves:	\$203,274	\$6,938	\$24,619	\$31,557	15.52%	\$6,938	100.00%	\$24,379	99.03%	15.41%
Testing, Inspection, Geotechnical:	\$3,229,337	\$1,420,335	\$267,955	\$1,688,290	52.28%	\$486,075	34.22%	\$94,022	35.09%	17.96%
Grand Total	\$310,286,194	\$9,415,674	\$11,582,491	\$20,998,165	6.77%	\$4,310,676	45.78%	\$5,615,634	48.48%	3.20%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Architect/Engineer											
Catlin Elementary	The Schemmer Associates Inc.	\$137,415	\$9,619	\$0	\$9,619	7.00%	\$16,511	171.65%	\$0	0.00%	12.02%
Conestoga Elementary	The Schemmer Associates Inc.	\$174,145	\$12,190	\$0	\$12,190	7.00%	\$16,511	135.45%	\$0	0.00%	9.48%
King Elementary	The Schemmer Associates Inc.	\$202,189	\$1,553	\$0	\$1,553	0.77%	\$1,553	100.00%	\$0	0.00%	0.77%
Benson High	Leo A. Daly	\$589,025	\$4,103	\$0	\$4,103	0.70%	\$0	0.00%	\$0	0.00%	0.00%
Bryan High	TACK Architects	\$398,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$2,282	0.00%	0.57%
Burke High	KPE Consulting Engineers	\$371,673	\$5,000	\$0	\$5,000	1.35%	\$33,750	675.00%	\$0	0.00%	9.08%
New ES 1000 N Ft Crook Rd.	Kenneth Hahn Architects	\$1,279,238	\$0	\$130,680	\$130,680	10.22%	\$0	0.00%	\$136,130	104.17%	10.64%
New HS 60th & L St.	DLR Group	\$5,177,210	\$161,000	\$195,500	\$356,500	6.89%	\$154,649	96.06%	\$98,480	50.37%	4.89%
New HS 60th & L St.	DVS Security	\$17,669	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	BCDM Architects	\$5,700,103	\$0	\$322,000	\$322,000	5.65%	\$0	0.00%	\$195,499	60.71%	3.43%
New HS 156th & Ida St.	DVS Security	\$17,669	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Bahr Varmeer Haecker Architects	\$154,548	\$0	\$5,406	\$5,406	3.50%	\$0	0.00%	\$4,120	76.21%	2.67%
Pinewood Elementary	Alley-Poyner Macchietto Architecture	\$424,180	\$28,361	\$2,884	\$31,245	7.37%	\$26,616	93.85%	\$4,500	156.03%	7.34%
Edison Elementary	Jackson-Jackson & Associates, Inc.	\$279,530	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Leo A. Daly	\$364,191	\$16,900	\$87,880	\$104,780	28.77%	\$14,940	88.40%	\$96,463	109.77%	30.59%
Masters Elementary	Jackson-Jackson & Associates, Inc.	\$177,870	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Architect/Engineer											
Spring Lake Elementary	The Schemmer Associates Inc.	\$551,794	\$33,200	\$29,050	\$62,250	11.28%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Alley-Poyner Macchietto Architecture	\$867,000	\$25,410	\$50,820	\$76,230	8.79%	\$28,644	112.73%	\$11,813	23.24%	4.67%
Central High	Alley-Poyner Macchietto Architecture	\$735,000	\$0	\$72,250	\$72,250	9.83%	\$0	0.00%	\$5,939	8.22%	0.81%
New MS 42nd & Y St.	RDG	\$2,281,000	\$67,830	\$90,440	\$158,270	6.94%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Jackson-Jackson & Associates, Inc.	\$1,172,720	\$0	\$132,863	\$132,863	11.33%	\$0	0.00%	\$0	0.00%	0.00%
Adams Elementary	KPE Consulting Engineers	\$123,700	\$3,850	\$7,150	\$11,000	8.89%	\$2,100	54.55%	\$8,447	118.14%	8.53%
Northwest High	Jackson-Jackson & Associates, Inc.	\$507,788	\$0	\$91,735	\$91,735	18.07%	\$0	0.00%	\$0	0.00%	0.00%
Morton Middle	Bahr Varmeer Haecker Architects	\$863,735	\$0	\$47,469	\$47,469	5.50%	\$0	0.00%	\$0	0.00%	0.00%
North High	Jackson-Jackson & Associates, Inc.	\$440,178	\$0	\$79,400	\$79,400	18.04%	\$0	0.00%	\$0	0.00%	0.00%
Blackburn School	KPE Consulting Engineers	\$239,800	\$8,050	\$14,950	\$23,000	9.59%	\$2,130	26.46%	\$14,192	94.93%	6.81%
South High	BCDM Architects	\$715,000	\$0	\$95,215	\$95,215	13.32%	\$0	0.00%	\$21,487	22.57%	3.01%
Total For Architect/Engineer:		\$23,962,370	\$377,066	\$1,455,692	\$1,832,758	7.65%	\$301,507	79.96%	\$599,350	41.17%	3.76%
Construction											
Catlin Elementary	American Boiler Company	\$13,101	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Catlin Elementary	Boyd Jones Construction	\$2,123,959	\$0	\$40,275	\$40,275	1.90%	\$0	0.00%	\$46,070	114.39%	2.17%
Catlin Elementary	Buller Fixture Company	\$30,750	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Catlin Elementary	Harold K. Scholz, Co.	\$800	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Catlin Elementary	Jamco Abatement Services	\$12,200	\$0	\$12,200	\$12,200	100.00%	\$0	0.00%	\$12,200	100.00%	100.00%
Catlin Elementary	Jesse L Gibson	\$2,140	\$0	\$2,140	\$2,140	100.00%	\$0	0.00%	\$2,140	100.00%	100.00%
Catlin Elementary	Prime Communications Inc.	\$1,389	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Catlin Elementary	Security Equipment, Inc.	\$1,834	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Allegiance Restortation, LLC	\$3,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	ASI Signage	\$842	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Boyd Jones Construction	\$2,171,217	\$0	\$47,790	\$47,790	2.20%	\$0	0.00%	\$64,236	134.41%	2.96%
Conestoga Elementary	Buller Fixture Company	\$30,750	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Downs Electric Inc.	\$6,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Electronic Sound Inc	\$4,290	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Electronic Sound Inc	\$6,300	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Jamco Abatement Services	\$9,792	\$0	\$9,792	\$9,792	100.00%	\$0	0.00%	\$9,792	100.00%	100.00%
Conestoga Elementary	Mechanical Systems, Inc.	\$328	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Mustang Electric Inc.	\$1,500	\$0	\$1,500	\$1,500	100.00%	\$0	0.00%	\$1,500	100.00%	100.00%
Conestoga Elementary	Prime Communications Inc.	\$2,084	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Security Equipment, Inc.	\$6,473	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$) Amount	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$) Amount	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Conestoga Elementary	Security Equipment, Inc.	\$2,951	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Verne Simmonds Company	\$1,700	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	A United Automatic Doors & Glass	\$6,782	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Elkhorn West Construction, Inc.	\$3,497,311	\$95,650	\$28,500	\$124,150	3.55%	\$84,616	88.46%	\$31,000	108.77%	3.31%
King Elementary	Fisher Fixture Company	\$31,768	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Grunwald Mechanical Contractors	\$510	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Haddock Education Technologies	\$1,229	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Hillyard	\$7,865	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Jamco Abatement Services	\$32,125	\$0	\$32,125	\$32,125	100.00%	\$0	0.00%	\$32,125	100.00%	100.00%
King Elementary	Mechanical Systems, Inc.	\$835	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Mechanical Systems, Inc.	\$69,750	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Miller Electric Company	\$20,751	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Miller Electric Company	\$1,069	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Omaha Stage Equipment Inc.	\$3,234	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Prime Communications Inc.	\$403	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Ready To Kool	\$2,155	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$) Amount	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$) Amount	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Benson High	Hausmann Construction, Inc.	\$7,353,742	\$357,648	\$73,138	\$430,786	5.86%	\$357,573	99.98%	\$58,070	79.40%	5.65%
Benson High	Heartland Scenic Studio	\$1,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Benson High	Jamco Abatement Services	\$37,690	\$0	\$37,690	\$37,690	100.00%	\$0	0.00%	\$37,690	100.00%	100.00%
Benson High	Johnson Hardware Company	\$364	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Bryan High	Hausmann Construction, Inc.	\$5,158,498	\$0	\$62,500	\$62,500	1.21%	\$0	0.00%	\$0	0.00%	0.00%
Bryan High	Heartland Scenic Studio	\$1,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Bryan High	Jamco Abatement Services	\$1,350	\$0	\$1,350	\$1,350	100.00%	\$0	0.00%	\$1,350	100.00%	100.00%
Burke High	Heartland Scenic Studio	\$1,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Jamco Abatement Services	\$7,819	\$0	\$7,819	\$7,819	100.00%	\$0	0.00%	\$7,819	100.00%	100.00%
Burke High	Johnson Hardware Company	\$5,406	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Johnson Hardware Company	\$252	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Mechanical Systems, Inc.	\$21,195	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Prime Communications Inc.	\$43,578	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	SunCo	\$107	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	The Weitz Company	\$4,742,424	\$0	\$831,107	\$831,107	17.52%	\$0	0.00%	\$838,656	100.91%	17.68%
Burke High	Trane	\$181,075	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Burke High	Trane	\$4,270	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Tred-Mark Communications	\$11,116	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	City of Bellevue	\$64,519	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Cox Contracting Co.	\$813,210	\$0	\$813,210	\$813,210	100.00%	\$0	0.00%	\$813,210	100.00%	100.00%
New ES 1000 N Ft Crook Rd.	Cox Contracting Co.	\$600	\$0	\$600	\$600	100.00%	\$0	0.00%	\$600	100.00%	100.00%
New ES 1000 N Ft Crook Rd.	Hausmann Construction, Inc.	\$17,200,000	\$0	\$912,038	\$912,038	5.30%	\$0	0.00%	\$786,614	86.25%	4.57%
New ES 1000 N Ft Crook Rd.	J&R Mechanical, Inc.	\$42,123	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Jamco Abatement Services	\$103,673	\$0	\$103,673	\$103,673	100.00%	\$0	0.00%	\$103,673	100.00%	100.00%
New ES 1000 N Ft Crook Rd.	Outback Fence Co.	\$28,375	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Bockmann Inc	\$870,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	City of Omaha Public Works	\$117,661	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Jamco Abatement Services	\$20,700	\$0	\$20,700	\$20,700	100.00%	\$0	0.00%	\$20,700	100.00%	100.00%
New HS 60th & L St.	McCarthy Building Companies, Inc.	\$76,051,848	\$4,541,266	\$319,150	\$4,860,416	6.39%	\$2,491,068	54.85%	\$213,975	67.05%	3.56%
New HS 156th & Ida St.	City of Omaha Planning	\$438,640	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Metropolitan Utilities District	\$140,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Sampson Construction	\$75,528,140	\$2,345,490	\$3,824,794	\$6,170,284	8.17%	\$253,463	10.81%	\$249,655	6.53%	0.67%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Transition Program	A United Automatic Doors & Glass	\$5,265	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Allegiance Restortation, LLC	\$9,426	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Binyard Specialty Cleaning	\$1,176	\$1,176	\$0	\$1,176	100.00%	\$1,176	100.00%	\$0	0.00%	100.00%
Transition Program	GovConnection, Inc.	\$1,498	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Hillyard	\$7,554	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	KE Flex Contracting	\$1,690	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Midwest DCM	\$2,042,526	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Nebraska Furniture Mart	\$1,824	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Nebraska Furniture Mart	\$3,197	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Prime Communications Inc.	\$4,718	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Security Equipment, Inc.	\$4,951	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Sirius Computer Solutions	\$61,520	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Sirius Computer Solutions	\$1,725	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	All Makes Office Equipment Co	\$16,638	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Centaur Electric Inc.	\$7,918	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Christopherson Plumbing, LLC	\$3,520	\$0	\$3,520	\$3,520	100.00%	\$0	0.00%	\$3,520	100.00%	100.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Pinewood Elementary	Future Construction Specialties	\$22,962	\$22,962	\$0	\$22,962	100.00%	\$22,962	100.00%	\$0	0.00%	100.00%
Pinewood Elementary	Grunwald Mechanical Contractors	\$15,021	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Hillyard	\$7,100	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Independent Roofing Company	\$547	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Jamco Abatement Services	\$15,230	\$0	\$15,230	\$15,230	100.00%	\$0	0.00%	\$15,230	100.00%	100.00%
Pinewood Elementary	Johnson Controls	\$12,985	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Johnson Hardware Company	\$1,736	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Meco-Henne Contracting, Inc.	\$4,641,892	\$0	\$289,000	\$289,000	6.23%	\$25,428	0.00%	\$322,018	111.42%	7.49%
Pinewood Elementary	Metropolitan Utilities District	\$4,571	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Porter Trustin Carlson Company	\$7,600	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Prime Communications Inc.	\$5,984	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Revolution Wraps	\$9,841	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	River City Barricade Company	\$175	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	SportsCon LLC	\$16,295	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Virco Inc	\$44,061	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Xtreme Heating & Cooling	\$3,728	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Edison Elementary	Allegiance Restoration, LLC	\$3,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Amazon Business Service	\$723	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Boyd Jones Construction	\$3,631,534	\$0	\$500,357	\$500,357	13.78%	\$0	0.00%	\$526,854	105.30%	14.51%
Edison Elementary	Buller Fixture Company	\$30,750	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Jamco Abatement Services	\$45,450	\$0	\$45,450	\$45,450	100.00%	\$0	0.00%	\$45,450	100.00%	100.00%
Edison Elementary	Mechanical Systems, Inc.	\$328	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Mustang Electric Inc.	\$1,500	\$0	\$1,500	\$1,500	100.00%	\$0	0.00%	\$1,500	100.00%	100.00%
Edison Elementary	Prime Communications Inc.	\$6,057	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Security Equipment, Inc.	\$3,806	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Hausmann Construction, Inc.	\$4,986,439	\$70,600	\$536,190	\$606,790	12.17%	\$214,007	303.13%	\$15,460	2.88%	4.60%
Masters Elementary	American Trailer & Storage Inc.	\$3,900	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Anderson Excavating Co.	\$13,920	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Boyd Jones Construction	\$2,368,107	\$0	\$342,444	\$342,444	14.46%	\$0	0.00%	\$306,793	89.59%	12.96%
Masters Elementary	Electronic Sound Inc	\$1,680	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Electronic Sound Inc	\$9,183	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Jamco Abatement Services	\$12,860	\$0	\$12,860	\$12,860	100.00%	\$0	0.00%	\$12,860	100.00%	100.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$) Amount	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$) Amount	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
Masters Elementary	Omaha Stage Equipment Inc.	\$9,638	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Palmer Hamilton LLC	\$23,907	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Prime Communications Inc.	\$845	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Security Equipment, Inc.	\$1,819	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Spring Lake Elementary	McKinnis Inc.	\$473,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Allegiance Restortation, LLC	\$2,658	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Grunwald Mechanical Contractors	\$17,700	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Jamco Abatement Services	\$5,400	\$0	\$5,400	\$5,400	100.00%	\$0	0.00%	\$5,400	100.00%	100.00%
Lewis & Clark Middle	Kellys Carpet	\$1,289	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Mid-Plains Insulation	\$1,465	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Miller Electric Company	\$1,778	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Vrana Construction	\$11,759,276	\$98,780	\$133,138	\$231,918	1.97%	\$0	0.00%	\$44,550	33.46%	0.38%
Central High	Mechanical Systems, Inc.	\$891	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Central High	The Weitz Company	\$45,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	McCarthy Building Companies, Inc.	\$25,674,475	\$71,900	\$249,893	\$321,793	1.25%	\$60,000	83.45%	\$129,565	51.85%	0.74%
New ES 10th & Pine St.	Anderson Excavating Co.	\$65,800	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Darland Construction Co	\$15,252,661	\$0	\$98,345	\$98,345	0.64%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Construction											
New ES 10th & Pine St.	Jamco Abatement Services	\$106,210	\$0	\$106,210	\$106,210	100.00%	\$0	0.00%	\$106,210	100.00%	100.00%
New ES 10th & Pine St.	McGill Asbestos Abatement	\$28,140	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Adams Elementary	The Weitz Company	\$10,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Morton Middle	MCL Construction	\$10,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Morton Middle	Vinny's Tree Service	\$5,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Blackburn School	The Weitz Company	\$10,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
South High	The Weitz Company	\$33,750	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Total For Construction:		\$268,747,372	\$7,605,471	\$9,521,628	\$17,127,099	6.37%	\$3,510,292	46.15%	\$4,866,725	51.11%	3.12%
Owner Administration											
Program Mgmt. & Admin.	Baird-Holm	\$121,829	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	ieDesign, LLC	\$12,358	\$0	\$12,358	\$12,358	100.00%	\$0	0.00%	\$12,358	100.00%	100.00%
Program Mgmt. & Admin.	ieDesign, LLC	\$29,280	\$0	\$29,280	\$29,280	100.00%	\$0	0.00%	\$7,300	24.93%	24.93%
Program Mgmt. & Admin.	ieDesign, LLC	\$14,400	\$0	\$14,400	\$14,400	100.00%	\$0	0.00%	\$3,500	24.31%	24.31%
Program Mgmt. & Admin.	ieDesign, LLC	\$45,600	\$0	\$45,600	\$45,600	100.00%	\$0	0.00%	\$8,000	17.54%	17.54%
Program Mgmt. & Admin.	ieDesign, LLC	\$38,640	\$0	\$38,640	\$38,640	100.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	ieDesign, LLC	\$38,640	\$0	\$38,640	\$38,640	100.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	ieDesign, LLC	\$38,640	\$0	\$38,640	\$38,640	100.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	ieDesign, LLC	\$47,520	\$0	\$47,520	\$47,520	100.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$) Amount	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$) Amount	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Owner Administration											
Program Mgmt. & Admin.	ieDesign, LLC	\$47,520	\$0	\$47,520	\$47,520	100.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	Omaha Public Schools	\$78,139	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Total For Owner Administration:		\$512,565	\$0	\$312,598	\$312,598	60.99%	\$0	0.00%	\$31,158	9.97%	6.08%
Printing & Advertisement											
Program Mgmt. & Admin.	A&D Technical Supply	\$27,010	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	Design 4 Screenprinting & More, Inc.	\$5,864	\$5,864	\$0	\$5,864	100.00%	\$5,864	100.00%	\$0	0.00%	100.00%
Program Mgmt. & Admin.	Simplified Office Solutions	\$6,716	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	Standard Digital Imaging	\$32,996	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Total For Printing & Advertisement:		\$72,586	\$5,864	\$0	\$5,864	8.08%	\$5,864	100.00%	\$0	0.00%	8.08%
Program Mgmt & Admin											
Program Mgmt. & Admin.	Bluebeam Software Inc	\$2,745	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	CDW Government	\$2,795	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	Jacobs	\$13,548,800	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	Microsoft Corporation	\$4,030	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Program Mgmt. & Admin.	SoftChoice Corporation	\$320	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Total For Program Mgmt & Admin:		\$13,558,690	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Temp Housing, Utilities, Moves											
Catlin Elementary	Waste Management	\$473	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Jesse L Gibson	\$240	\$0	\$240	\$240	100.00%	\$0	0.00%	\$240	100.00%	100.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Temp Housing, Utilities, Moves											
King Elementary	Omaha Public Schools	\$219	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Omaha Public Schools	\$3,078	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Metropolitan Utilities District	\$11,320	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Omaha Public Power District	\$49,290	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Omaha Public Schools	\$138	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Cox Business Services	\$300	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Metropolitan Utilities District	\$2,581	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Omaha Public Schools	\$746	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Cox Business Services	\$5,171	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Cox Contracting Co.	\$4,394	\$0	\$4,394	\$4,394	100.00%	\$0	0.00%	\$4,394	100.00%	100.00%
Pinewood Elementary	Husker Tree & Landscaping	\$5,510	\$5,510	\$0	\$5,510	100.00%	\$5,510	100.00%	\$0	0.00%	100.00%
Pinewood Elementary	Jesse L Gibson	\$1,185	\$0	\$1,185	\$1,185	100.00%	\$0	0.00%	\$1,185	100.00%	100.00%
Pinewood Elementary	Omaha Public Power District	\$30,868	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Omaha Public Schools	\$2,153	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Scribs House Moving Inc	\$7,071	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Unite Private Networks	\$14,738	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Cox Business Services	\$7,145	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Temp Housing, Utilities, Moves											
Edison Elementary	Unite Private Networks	\$10,572	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Cox Contracting Co.	\$10,000	\$0	\$10,000	\$10,000	100.00%	\$0	0.00%	\$10,000	100.00%	100.00%
Highland Elementary	Omaha Public Power District	\$4,527	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Omaha Public Schools	\$660	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Binyard Specialty Cleaning	\$1,428	\$1,428	\$0	\$1,428	100.00%	\$1,428	100.00%	\$0	0.00%	100.00%
Lewis & Clark Middle	Abe's Portables	\$315	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Cox Contracting Co.	\$8,800	\$0	\$8,800	\$8,800	100.00%	\$0	0.00%	\$8,800	100.00%	100.00%
Lewis & Clark Middle	J&R Mechanical, Inc.	\$4,250	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	American Fence Company	\$11,896	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Omaha Public Power District	\$4,206	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Total For Temp Housing, Utilities, Moves:		\$203,274	\$6,938	\$24,619	\$31,557	15.52%	\$6,938	100.00%	\$24,379	99.03%	15.41%
Testing, Inspection, Geotechnical											
Catlin Elementary	Optimized Systems	\$44,000	\$44,000	\$0	\$44,000	100.00%	\$35,200	80.00%	\$0	0.00%	80.00%
Catlin Elementary	Optimized Systems	\$14,200	\$14,200	\$0	\$14,200	100.00%	\$10,650	75.00%	\$0	0.00%	75.00%
Catlin Elementary	Terracon Consultants, Inc.	\$1,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Catlin Elementary	Thiele Geotech Inc	\$2,409	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Optimized Systems	\$49,000	\$49,000	\$0	\$49,000	100.00%	\$39,200	80.00%	\$0	0.00%	80.00%
Conestoga Elementary	Optimized Systems	\$15,300	\$15,300	\$0	\$15,300	100.00%	\$11,475	75.00%	\$0	0.00%	75.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
Conestoga Elementary	Terracon Consultants, Inc.	\$6,760	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Conestoga Elementary	Thiele Geotech Inc	\$2,165	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Four Corners Restoration	\$2,526	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
King Elementary	Optimized Systems	\$44,500	\$44,500	\$0	\$44,500	100.00%	\$44,500	100.00%	\$0	0.00%	100.00%
King Elementary	Terracon Consultants, Inc.	\$14,439	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Benson High	Aerotech Laboratories, Inc.	\$99	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Benson High	Optimized Systems	\$49,500	\$49,500	\$0	\$49,500	100.00%	\$49,500	100.00%	\$0	0.00%	100.00%
Benson High	Optimized Systems	\$47,500	\$47,500	\$0	\$47,500	100.00%	\$40,375	85.00%	\$0	0.00%	85.00%
Benson High	Terracon Consultants, Inc.	\$12,446	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Benson High	Thiele Geotech Inc	\$724	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Bryan High	Terracon Consultants, Inc.	\$4,270	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Alpha Land Surveying	\$4,950	\$0	\$4,950	\$4,950	100.00%	\$0	0.00%	\$4,950	100.00%	100.00%
Burke High	Alpha Land Surveying	\$5,350	\$0	\$5,350	\$5,350	100.00%	\$0	0.00%	\$5,350	100.00%	100.00%
Burke High	Ambassador Title Services	\$500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	ATC Group Services LLC	\$2,300	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Optimized Systems	\$49,000	\$49,000	\$0	\$49,000	100.00%	\$49,000	100.00%	\$0	0.00%	100.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
Burke High	Optimized Systems	\$46,150	\$46,150	\$0	\$46,150	100.00%	\$46,150	100.00%	\$0	0.00%	100.00%
Burke High	Terracon Consultants, Inc.	\$27,094	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Terracon Consultants, Inc.	\$625	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Burke High	Thompson Dreessen Dorner Inc.	\$3,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	First American Title Insurance Company	\$250	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Lamp Ryneerson & Associates	\$10,400	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Olsson Associates	\$9,450	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Olsson Associates	\$79,928	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Optimized Systems	\$92,980	\$92,980	\$0	\$92,980	100.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	R.W. Engineering & Surveying, Inc.	\$19,800	\$0	\$19,800	\$19,800	100.00%	\$0	0.00%	\$19,432	98.14%	98.14%
New ES 1000 N Ft Crook Rd.	R.W. Engineering & Surveying, Inc.	\$14,948	\$0	\$14,948	\$14,948	100.00%	\$0	0.00%	\$12,918	86.42%	86.42%
New ES 1000 N Ft Crook Rd.	Terracon Consultants, Inc.	\$36,080	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 1000 N Ft Crook Rd.	Thiele Geotech Inc	\$410	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Optimized Systems	\$245,210	\$245,210	\$0	\$245,210	100.00%	\$20,650	8.42%	\$0	0.00%	8.42%
New HS 60th & L St.	R.W. Engineering & Surveying, Inc.	\$3,613	\$0	\$3,458	\$3,458	95.71%	\$0	0.00%	\$3,613	104.48%	100.00%
New HS 60th & L St.	R.W. Engineering & Surveying, Inc.	\$32,400	\$0	\$32,400	\$32,400	100.00%	\$0	0.00%	\$12,000	37.04%	37.04%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
New HS 60th & L St.	Terracon Consultants, Inc.	\$134,965	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$36,250	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$7,825	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$16,065	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$14,536	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$20,725	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$162,495	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 60th & L St.	Terracon Consultants, Inc.	\$14,295	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Lamp Rynearson & Associates	\$125,158	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Optimized Systems	\$181,215	\$181,215	\$0	\$181,215	100.00%	\$20,155	11.12%	\$0	0.00%	11.12%
New HS 156th & Ida St.	R.W. Engineering & Surveying, Inc.	\$39,300	\$0	\$39,300	\$39,300	100.00%	\$0	0.00%	\$14,250	36.26%	36.26%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$21,890	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$6,920	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$29,219	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$154,843	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$20,778	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$25,434	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$19,395	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Terracon Consultants, Inc.	\$11,000	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New HS 156th & Ida St.	Thiele Geotech Inc	\$18,929	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Transition Program	Thiele Geotech Inc	\$1,151	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Alpha Land Surveying	\$7,250	\$0	\$7,250	\$7,250	100.00%	\$0	0.00%	\$7,250	100.00%	100.00%
Pinewood Elementary	Optimized Systems	\$71,600	\$71,600	\$0	\$71,600	100.00%	\$68,720	95.98%	\$0	0.00%	95.98%
Pinewood Elementary	Terracon Consultants, Inc.	\$11,075	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Thiele Geotech Inc	\$2,600	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Pinewood Elementary	Thiele Geotech Inc	\$6,831	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Boundaryline Surveys	\$3,800	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Olsson Associates	\$2,471	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Optimized Systems	\$57,090	\$0	\$57,090	\$57,090	100.00%	\$27,000	0.00%	\$0	0.00%	47.29%
Edison Elementary	Terracon Consultants, Inc.	\$3,650	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Edison Elementary	Terracon Consultants, Inc.	\$6,668	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
Edison Elementary	Terracon Consultants, Inc.	\$4,394	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Cornerstone Surveying LLC	\$11,400	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Optimized Systems	\$70,250	\$70,250	\$0	\$70,250	100.00%	\$3,500	4.98%	\$0	0.00%	4.98%
Highland Elementary	Terracon Consultants, Inc.	\$100	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Thiele Geotech Inc	\$3,975	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Highland Elementary	Thiele Geotech Inc	\$16,585	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Boundaryline Surveys	\$2,900	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Olsson Associates	\$2,423	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Optimized Systems	\$49,060	\$0	\$49,060	\$49,060	100.00%	\$20,000	0.00%	\$0	0.00%	40.77%
Masters Elementary	Terracon Consultants, Inc.	\$3,650	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Terracon Consultants, Inc.	\$1,445	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Masters Elementary	Terracon Consultants, Inc.	\$2,493	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Spring Lake Elementary	Terracon Consultants, Inc.	\$2,298	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Spring Lake Elementary	Thiele Geotech Inc	\$9,200	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Cornerstone Surveying LLC	\$10,350	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Optimized Systems	\$151,940	\$151,940	\$0	\$151,940	100.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
Lewis & Clark Middle	Terracon Consultants, Inc.	\$595	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Terracon Consultants, Inc.	\$24,490	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Lewis & Clark Middle	Thiele Geotech Inc	\$3,250	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Central High	Heartland Scenic Studio	\$1,920	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Lamp Rynearson & Associates	\$13,900	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Olsson Associates	\$32,960	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Olsson Associates	\$20,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Olsson Associates	\$5,990	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Olsson Associates	\$7,305	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Olsson Associates	\$87,730	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	Optimized Systems	\$156,650	\$156,650	\$0	\$156,650	100.00%	\$0	0.00%	\$0	0.00%	0.00%
New MS 42nd & Y St.	R.W. Engineering & Surveying, Inc.	\$25,500	\$0	\$25,500	\$25,500	100.00%	\$0	0.00%	\$2,850	11.18%	11.18%
New ES 10th & Pine St.	Ehrhart Griffin & Associates	\$8,276	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Felsburg Holt & Ullevig	\$14,500	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Olsson Associates	\$16,283	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Optimized Systems	\$91,340	\$91,340	\$0	\$91,340	100.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Terracon Consultants, Inc.	\$69,719	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%



2018 Bond Program

Report Date 2/22/2021

Economic Inclusion Plan & Commitment Monitoring Report

The 15% EI Plan Goal is an overall Bond Program Goal which is applied to all account codes except Land Acquisition and Builders' Risk Insurance

Bid Package	Vendor	A Total Contract Amount (\$)	CONTRACT COMMITMENTS				EXPENDITURES				
			B Tier #1 Contract Commitment (\$)	C Tier #2 Contract Commitment (\$)	D=B+C Tier #1 & #2 Contract Commitment (\$)	E=D/A Tier #1 & #2 % of Contract Amount	F Tier #1 ETD (\$ Amount)	G=F/B Tier #1 ETD % Contract Commitment (\$)	H Tier #2 ETD (\$ Amount)	I=H/C Tier #2 ETD % Contract Commitment (\$)	J=(F+H)/A Tier #1 & #2 ETD % of Overall Contract
Testing, Inspection, Geotechnical											
New ES 10th & Pine St.	Thiele Geotech Inc	\$8,725	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
New ES 10th & Pine St.	Thiele Geotech Inc	\$39,984	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Adams Elementary	R.W. Engineering & Surveying, Inc.	\$2,560	\$0	\$0	\$0	0.00%	\$0	0.00%	\$2,560	0.00%	100.00%
Morton Middle	Cornerstone Surveying LLC	\$10,400	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Morton Middle	Independent Roofing Company	\$350	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
Morton Middle	Thiele Geotech Inc	\$4,400	\$0	\$0	\$0	0.00%	\$0	0.00%	\$0	0.00%	0.00%
North High	R.W. Engineering & Surveying, Inc.	\$6,900	\$0	\$6,900	\$6,900	100.00%	\$0	0.00%	\$6,900	100.00%	100.00%
Blackburn School	R.W. Engineering & Surveying, Inc.	\$1,950	\$0	\$1,950	\$1,950	100.00%	\$0	0.00%	\$1,950	100.00%	100.00%
Total For Testing, Inspection, Geotechnical:		\$3,229,337	\$1,420,335	\$267,955	\$1,688,290	52.28%	\$486,075	34.22%	\$94,022	35.09%	17.96%
Grand Total		\$310,286,194	\$9,415,674	\$11,582,491	\$20,998,165	6.77%	\$4,310,676	45.78%	\$5,615,634	48.48%	3.20%



2018 Bond Program

Report Date: 2/23/2021

Bond Sales Premium Proceeds and Earnings Interest Report

Description	Phase	BUDGET			COST COMMITMENTS				EXPENDITURES		
		A	A1	A2=A+A1	B	C=B/A2	D	E=B+D	F=A2-E	G	H = G/A2
		Original Project Budget	Budget Transfer	Current Budget	Committed Cost	% Committed	Additional Commitments To Complete	Projected Commitments	Projected (Over) / Under	Expenditures To Date	% Expended
Bond Sale Additional Premium Proceeds											
Total Tranche Sale Premium - #001 (Par Amount of Bonds = \$80M)	Complete	\$0	\$1,366,900	\$1,366,900	\$328,388	24.02%	\$0	\$328,388	\$1,038,512	\$328,388	24.02%
Total Tranche Sale Premium - #002 (Par Amount of Bonds = \$125M)	Complete	\$0	\$10,942,515	\$10,942,515	\$578,555	5.29%	\$0	\$578,555	\$10,363,960	\$578,555	5.29%
Total Tranche Sale Premium - #003	Not Started	\$0	\$0	\$0	\$0	0.00%	\$0	\$0	\$0	\$0	0.00%
Total Tranche Sale Premium - #004	Not Started	\$0	\$0	\$0	\$0	0.00%	\$0	\$0	\$0	\$0	0.00%
Bond Earnings Interest To Date											
Tranche #001 - Total Investment Results - Interest, Dividends, and Other Income	In Progress	\$0	\$1,765,794	\$1,765,794	\$0	0.00%	\$0	\$0	\$1,765,794	\$0	0.00%
Tranche #002 - Total Investment Results - Interest, Dividends, and Other Income	In Progress	\$0	\$777,459	\$777,459	\$0	0.00%	\$0	\$0	\$777,459	\$0	0.00%
Tranche #003 - Total Investment Results - Interest, Dividends, and Other Income	Not Started	\$0	\$0	\$0	\$0	0.00%	\$0	\$0	\$0	\$0	0.00%
Tranche #004 - Total Investment Results - Interest, Dividends, and Other Income	Not Started	\$0	\$0	\$0	\$0	0.00%	\$0	\$0	\$0	\$0	0.00%
Grand Totals:		\$0	\$14,852,668	\$14,852,668	\$906,943	6.11%	\$0	\$906,943	\$13,945,724	\$906,943	6.11%

Budget Transfer Information: Increase To Program Contingency (Project #321599)

Budget Transfer # ____: Increase To Project #321599 Program Contingency	\$0
---	-----

TOTAL:	\$0
---------------	------------
