


New Henry Clay High School

➤ Completed/Work in Progress:

- Site grading work is underway.
- Geothermal well field drilling at south end of site is complete.
- Trenching and gathering of geothermal piping is in progress.
- Area B structural caisson drilling is complete and grade beams and slabs are in progress.
- ICF and CIP formwork placing and pouring is in progress.
- Laying of CMU walls is in progress.
- Installation of IFAs (integrated framing assemblies) for framed openings at ICF walls is underway.
- Area A, B, C (Level 1) concrete slab and under-slab plumbing and electrical is in progress
- Installation of hollow metal frames is in progress.
- KAWC installation of main waterline is complete.

➤ Upcoming Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue pouring ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs at ICF walls.
- Continue installing hollow metal frames.
- Continue with grade beams and slabs in Areas B & D.

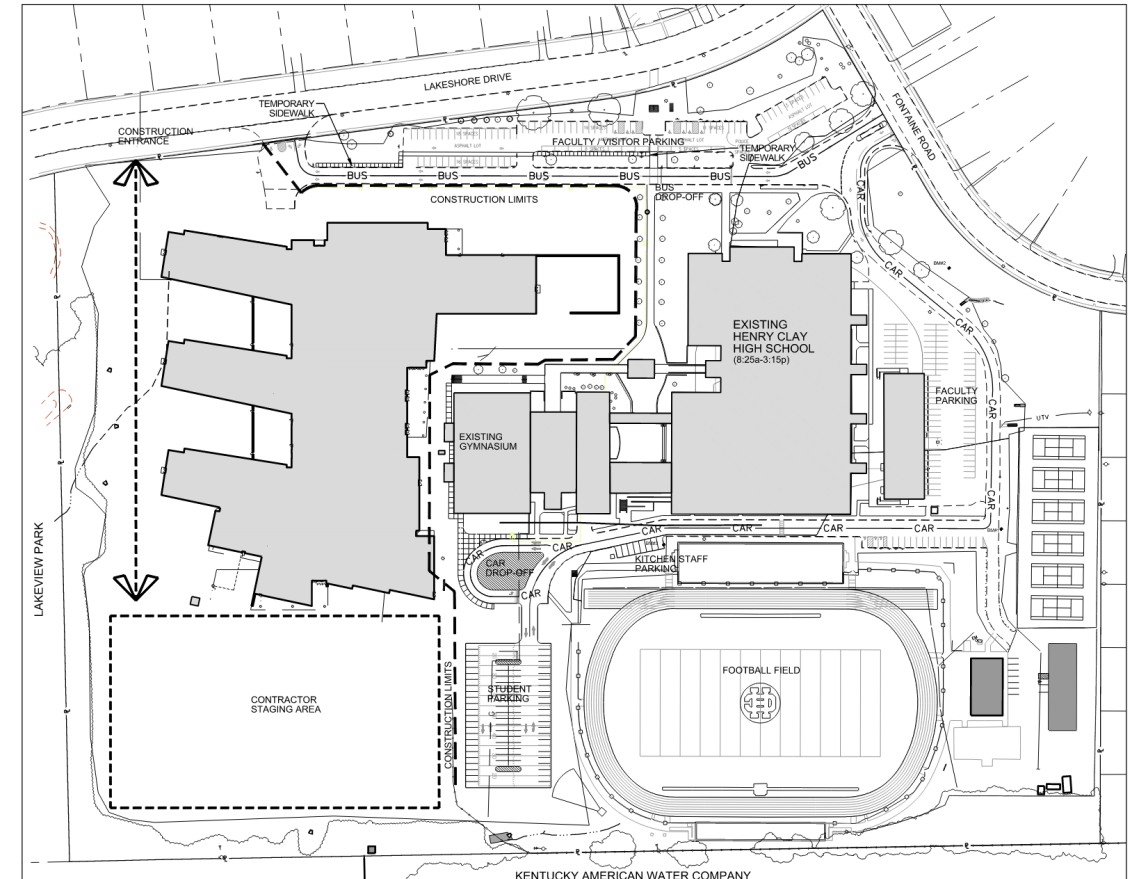

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Area A - ICF Walls, Laying CMU Walls, Installation of Hollow Metal and IFA Frames



New Henry Clay High School


Area A - ICF Walls, Laying CMU Walls, Installation of Hollow Metal and IFA Frames



Week Ending October 10, 2025

New Henry Clay High School

Area D Grade Beams and Cast-In-Place Concrete Walls in Progress

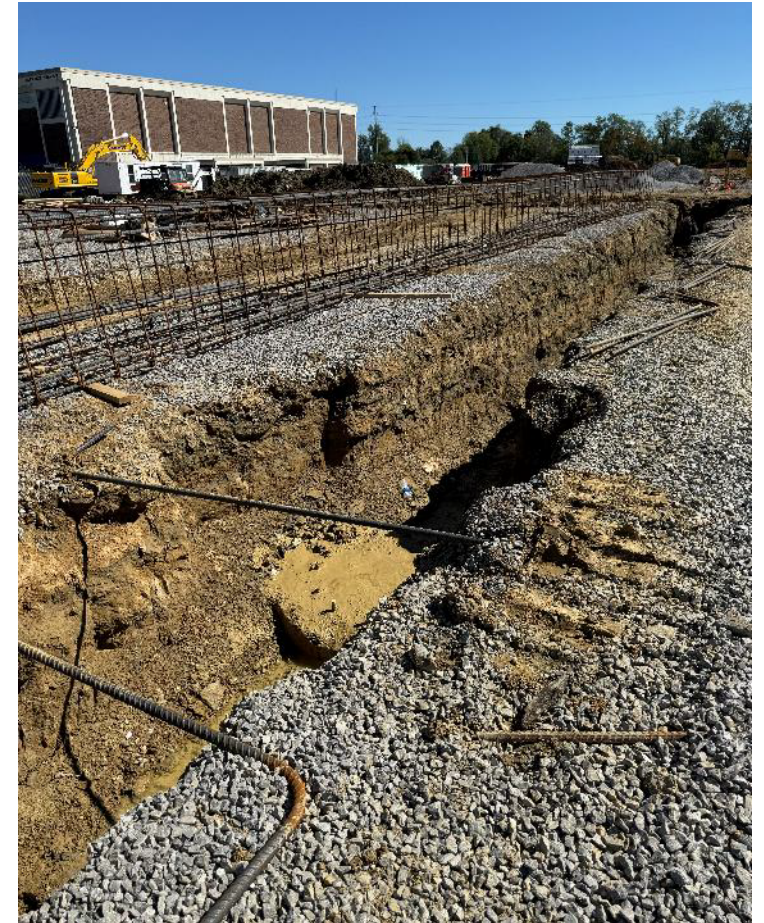

New Henry Clay High School



Area B Slab, Grade Beams, Under-Slab Plumbing and Electrical Underway



New Henry Clay High School

Area C (Level 1) Foundations, ICF Walls & IFA Frames, Under-Slab Plumbing & Electrical Underway



New Henry Clay High School



Overview of Construction Progress in Areas A, B, C



New Henry Clay High School

Overview of Construction Progress in Areas A, B, C



Week Ending October 10, 2025
