



Projects in Construction

Cherokee HS Replacement

Replacement Facility





Carroll Daniel Construction

Substantial Completion: 12.2025

Anticipated Occupancy: 08.2026

- Installation of the casework, marker/tack boards, and ceiling grid continues, along with installation of lighting, painting, and flooring in the main academic building.
- Preliminary punch list in the CTAE building continues. Installation of the casework, flooring, doors, and door hardware is complete. Installation of marker/tack boards and CTAE equipment is underway.
- The bus canopy, glass railing, and ceiling tile installation at the auxiliary gym/auditorium are nearing completion. Installation of the stage flooring, LVT flooring, and sealed concrete floor is underway. The auditorium seating installation has been scheduled.
- Flooring installation in the cafeteria is complete. Kitchen equipment and casework installation, along with wood door placement, are underway.
- Gym railing and ceiling grid installation are ongoing in the main gym. Scoreboard installation is complete and the jumbotron installation is underway. The wood floor delivery has been scheduled.
- Prep for synthetic turf continues. The baseball and softball bleacher installation has begun. Installation of the football press box and tennis court asphalt is scheduled to begin soon.
- Installation of the sidewalks continues, as well as sodding and tree installation for the entire campus. The courtyard concrete and parking lot stripping are underway.



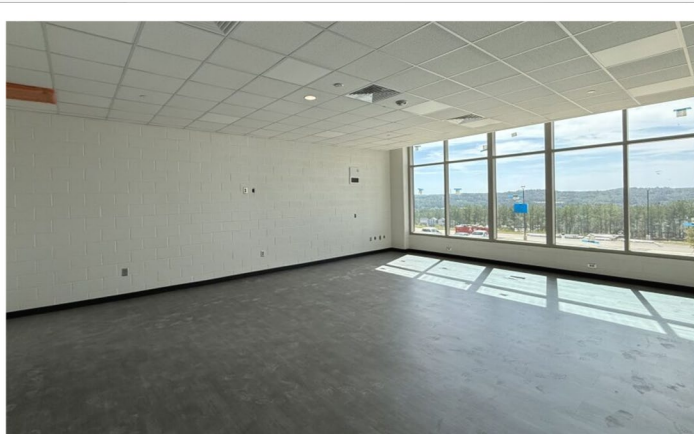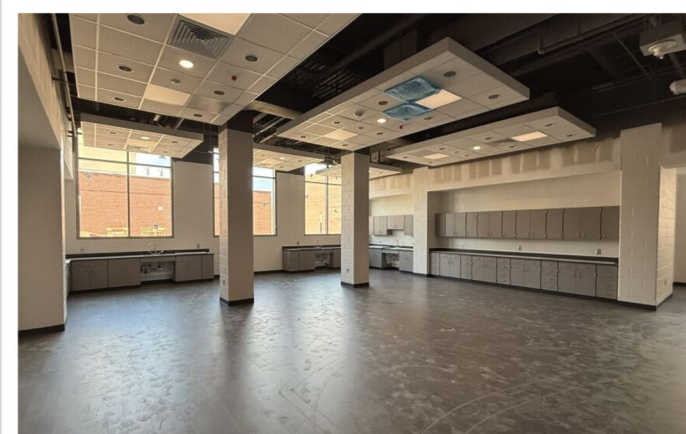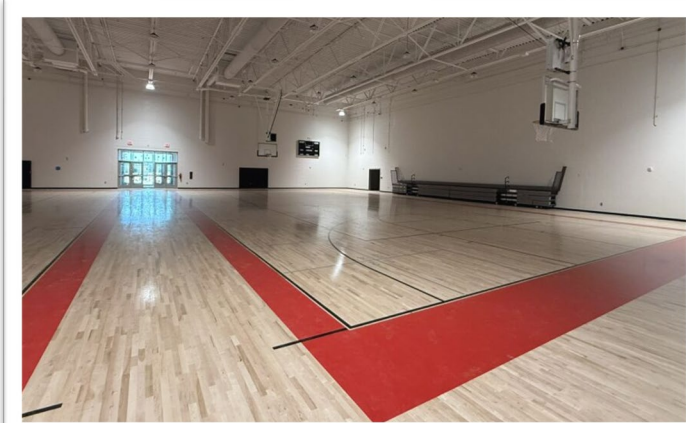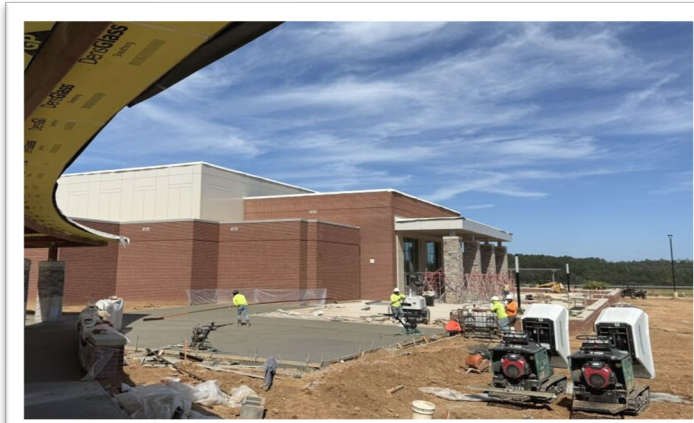



Creekview HS



Classroom Addition ~ Auxiliary Gym

McKnight Construction Company

Substantial Completion: 05.2025

Anticipated Occupancy: 10.2025

- The auxiliary gym's interior finishes are nearing completion, and the landscaping has begun. Receipt of the temporary certificate of occupancy is expected soon, and the gym is anticipated to be ready for student use mid-October.
- The interior renovation of the 1300 hall is nearing completion and final inspections are expected in the next two (2) weeks.

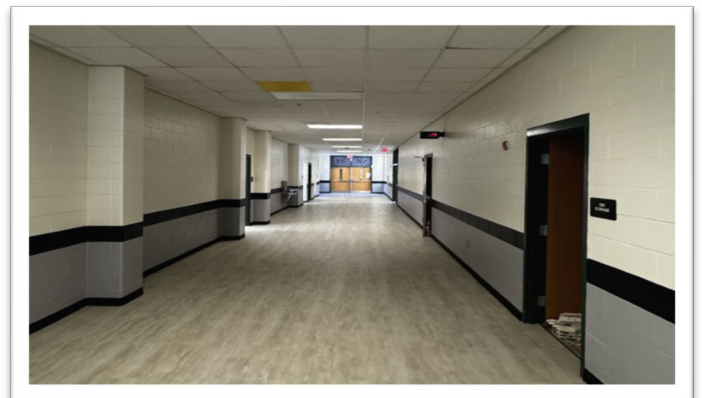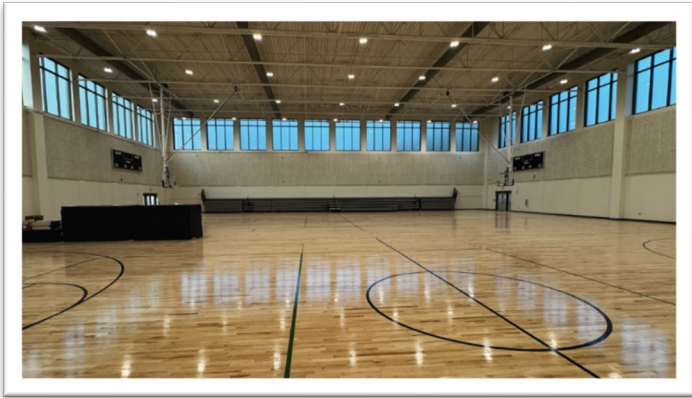



River Ridge HS



Auxiliary Gymnasium

SmithBuilt Construction Group

Substantial Completion: 04.2026

Anticipated Occupancy: 08.2026

- Interior and exterior CMU wall placement continues.
- Fireproofing, MEP rough-in, and placement of hollow metal door frames are ongoing.
- Installation of the roofing TPO has been scheduled.
- Exterior brick installation has been scheduled.

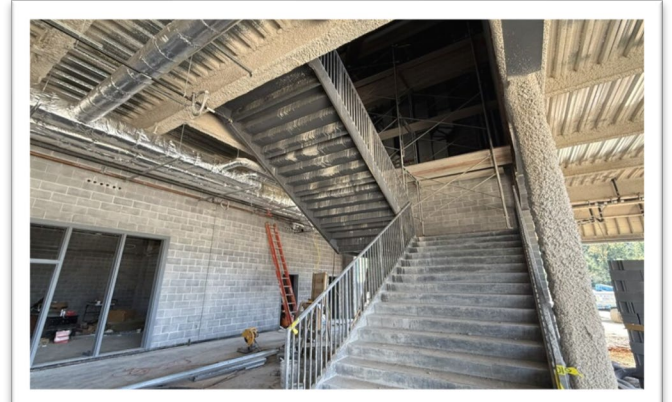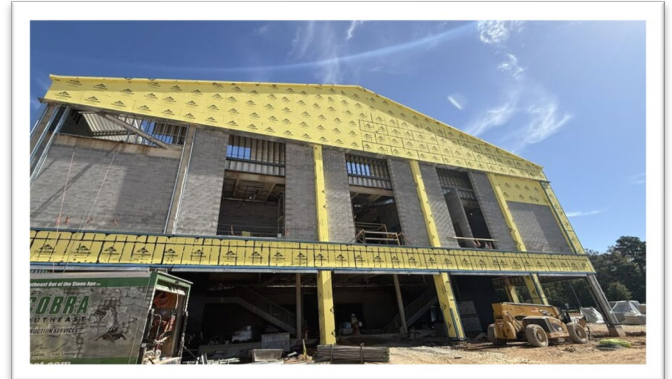



Sequoyah HS

Auxiliary Gym and Facility Improvements

(Press Box & Field House)

Carroll Daniel Construction

Substantial Completion: 11.2026

Anticipated Occupancy: 01.2027

- Installation of the underground utilities at the auxiliary gym is underway.
- Atlanta Gas Light has scheduled the relocation of the underground gas line at the field house.
- Installation of the perimeter wall for the foundation at the auxiliary gym is complete, and site prep is underway to pour the foundation.
- Rough grade for the home field house has been scheduled.





Teasley MS

Driveway Improvements

Summit Construction and Development

Substantial Completion: 10.2025

Anticipated Occupancy: 11.2025

- Excess dirt removal and prep work for GA Power utility relocation are ongoing.
- Underground storm and curb and gutter installation are underway.



Capital Outlay Report

Work Session | 10.16.2025



Woodstock HS

Classroom Addition

SmithBuilt Construction Group

Substantial Completion: 01.2026

Anticipated Occupancy: 08.2026

- Landscaping and hardscaping are ongoing.
- Final painting and wall repair have begun.
- Test and balance of the mechanical systems is underway.
- Final inspections have been scheduled.

