


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- ICF and CIP formwork placing and pouring is in progress.
- Laying of CMU walls is in progress.
- Installation of IFAs (integrated framing assemblies) for framed openings at ICF walls is underway.
- Area A,B,C (Level 1) concrete slab and under-slab plumbing and electrical is in progress
- Installation of hollow metal frames is in progress.
- KAWC installation of main waterline is complete.
- Steel erection for Level 2 at Area A is in progress.
- Area G foundations are in progress.
- Area D grade beams are complete and ICF walls in this area are underway.

➤ Upcoming Look Ahead:


- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue pouring ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs at ICF walls.
- Continue installing hollow metal frames.
- Continue with ICF walls in Area D and foundations in Area G.
- Continue with steel erection for Level 2.

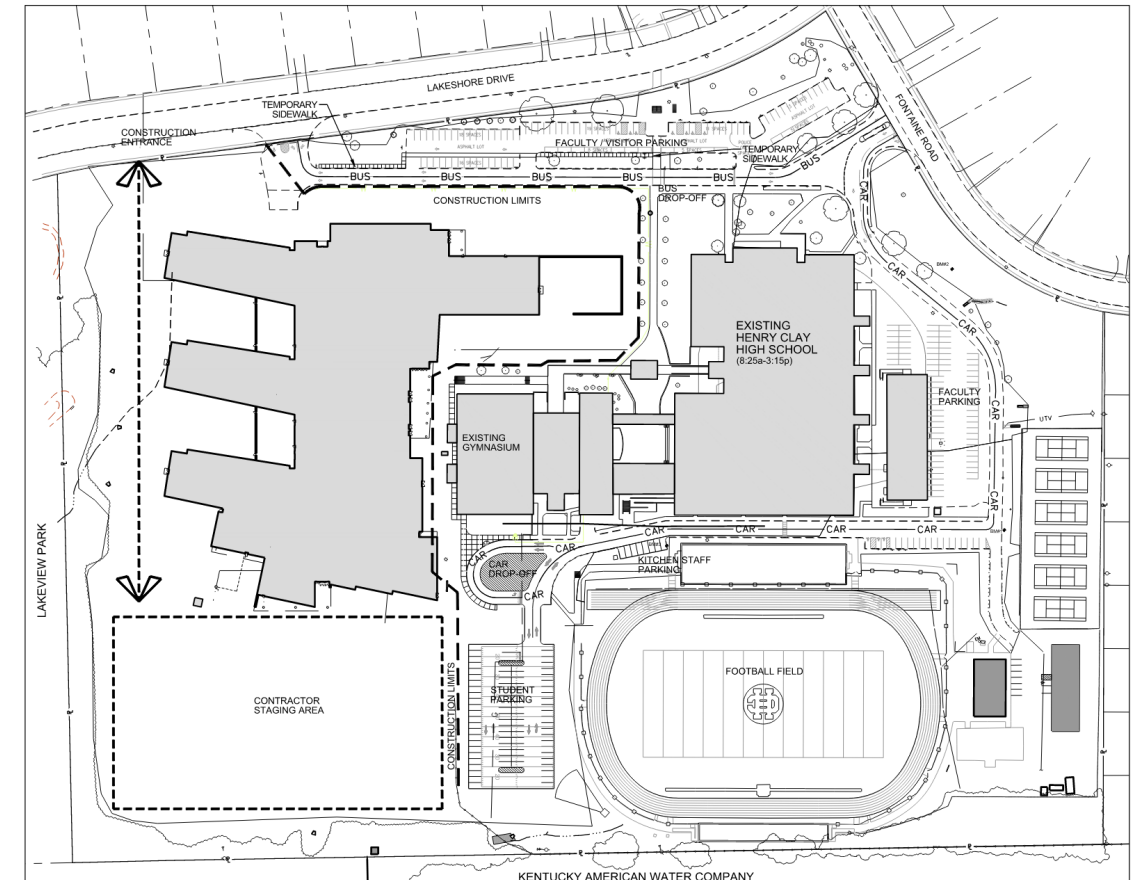

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School


Area A – Level 2 Steel Erection, Laying CMU Walls, Installation of Hollow Metal and IFA Frames

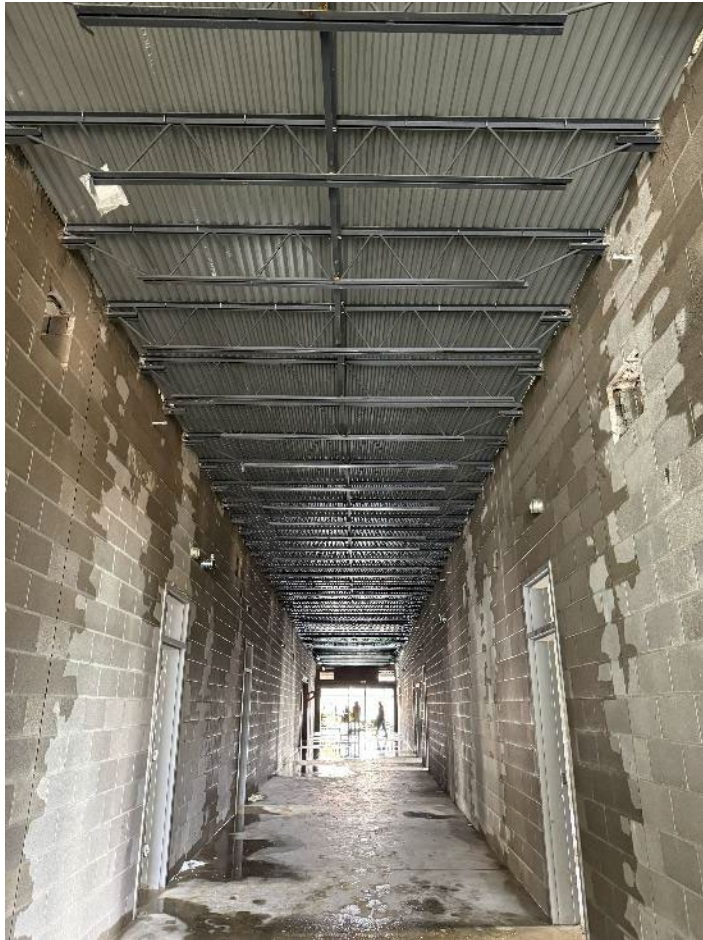

Week Ending October 31, 2025

New Henry Clay High School

Area A – Level 2 Steel Erection, Laying CMU Walls, Installation of Hollow Metal and IFA Frames

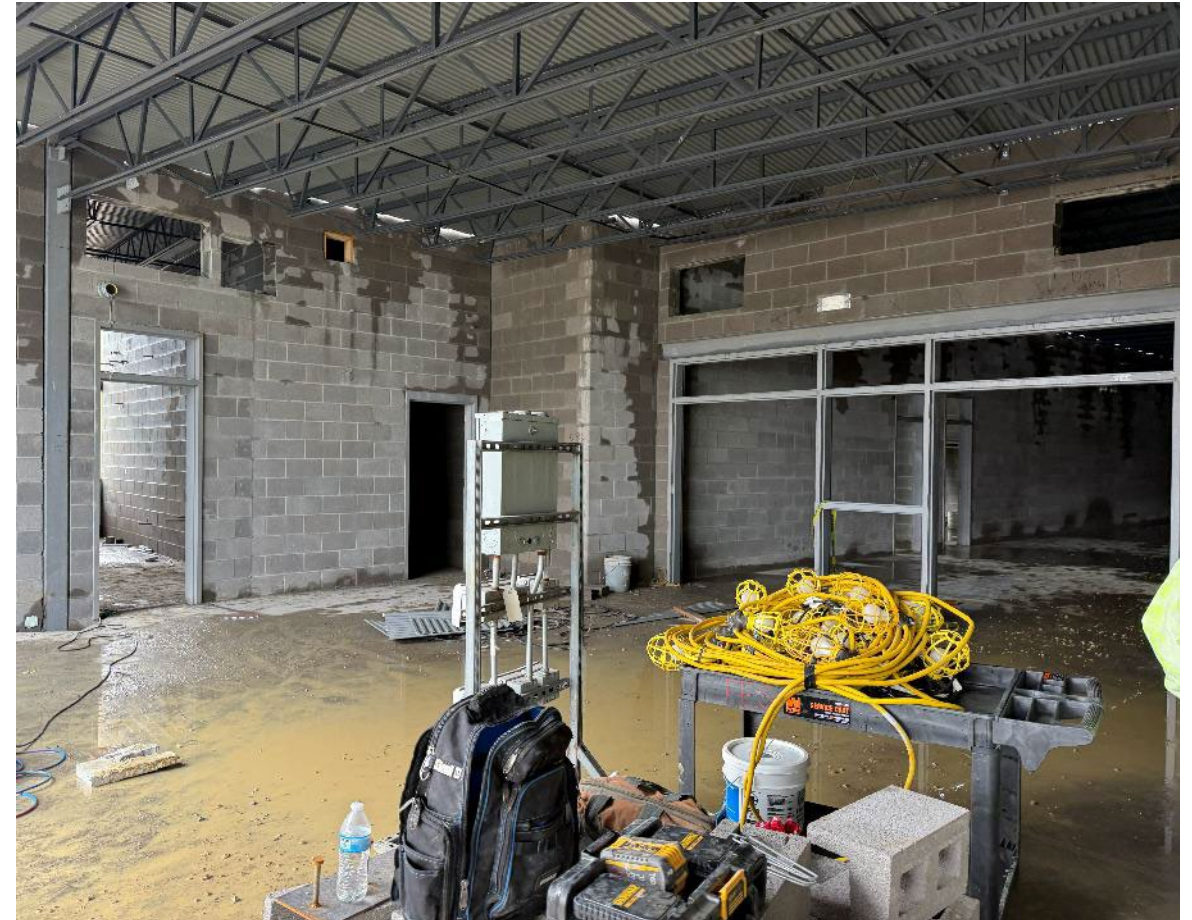

New Henry Clay High School

Area A – Level 2 Steel Erection, Laying CMU Walls, Installation of Hollow Metal and IFA Frames



Week Ending October 31, 2025

New Henry Clay High School

Area D ICF and IFA Frame Installation in Progress



Week Ending October 31, 2025

New Henry Clay High School

Area D ICF and IFA Frame Installation in Progress



Week Ending October 31, 2025

New Henry Clay High School

Area B Slab, IFA Walls, IFA Frames and Laying CMU Walls in Progress



Week Ending October 31, 2025

New Henry Clay High School

Area C (Level 1) Floor Slab, ICF Walls & IFA Frames in Progress



New Henry Clay High School

Overview of Construction Progress in Areas A, B, C



Week Ending October 31, 2025

New Henry Clay High School

Overview of Construction Progress in Areas A, B, C, D, G



Week Ending October 31, 2025
