




# Monthly Progress Report

November 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress **November 2025**

**Section III** – Work Projected for **December 2025**

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary

### November 2025

#### Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
  - Staircase railings upgrades.
  - Classroom wall upgrades per code.
  - Install eye wash stations.
  - Install new exhaust fans.
  - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
  - Remove old asphalt tennis grounds.
  - Install new tennis courts with bleachers.
  - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
  - Removal of caulking under abatement.
  - Removal of existing windows.
  - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – In Progress**
  - Boiler and piping replacement.
- **Hempstead UFSD – IAQ at Various School – In Progress**
  - Indoor air quality and mechanical upgrades.
  - Electrical upgrades.



## Section II - Work Progress November 2025

### **Hempstead UFSD – HS Priority Infrastructure Upgrades**

- **Total:**
  - Completed 75% of the installation and ran into fabrication issue. Work is currently on hold.

### **Hempstead UFSD – HS Tennis Courts**

- **United Paving:**
  - Completed cutting of 2 tree branches.
  - Completed bridge footings.

### **Hempstead UFSD – Window replacement**

- **Arrow Steel Windows:**
  - Continued replacing windows at McNeil ES.
  - About 75% of the building was completed.

### **Hempstead UFSD – Boiler replacement**

- **Thermotech:**
  - Installed new boiler.
  - Installed new fresh air intake and new flue.
  - Completed associated boiler piping and controls.
  - Completed electrical work.

### **Hempstead UFSD – IAQ at Various Schools**

- **Reliance:**
  - Started low voltage wiring in McNeil ES, Paterson ES, and Prospect.
  - Completed installing split units and refrigerant piping at McNeil ES.
  - Completed installing split units and refrigerant piping at Paterson ES.
- **Eldor:**
  - Continued roughing in ceilings and on walls at Paterson ES.



## Section III - Work Planned December 2025

### **Hempstead UFSD – HS Priority Infrastructure Upgrades**

- **Total:**
  - Complete Handi-lift work.

### **Hempstead UFSD – HS Tennis Courts**

- **United Paving**
  - Complete remaining punch list items.
  - Complete bridge Installation beginning of January.

### **Hempstead UFSD – Window replacement**

- **Arrow steel windows**
  - Complete replacing windows at McNeil ES.
  - Complete window tinting at McNeil ES.

### **Hempstead UFSD – Boiler replacement**

- **Thermotech:**
  - Complete boiler startup.
  - Complete electrical lighting in boiler room.

### **Hempstead UFSD – IAQ at Various Schools**

- **Reliance:**
  - Install chiller pad and bollards at Prospect ES.
  - Continue low voltage roughing.
  - UV valve survey and valve replacement to take place during holiday break.
- **Eldor:**
  - Continue to rough in ceilings at Paterson ES and McNeil ES.



## Section IV – Progress Photos



## Hempstead McNeil ES – Window Replacement



## Section IV – Progress Photos



## Hempstead McNeil ES – Window Replacement



## Section IV – Progress Photos



## Hempstead McNeil ES – Boiler Replacement



## Section IV – Progress Photos



## Hempstead McNeil ES – Boiler Replacement



## Section IV – Progress Photos



## Hempstead Paterson ES – IAQ



## Section IV – Progress Photos




## Hempstead Prospect ES – IAQ



## Section V – Workforce Summary – Company/Hours

### November 2025

▼ MANPOWER GRAPH

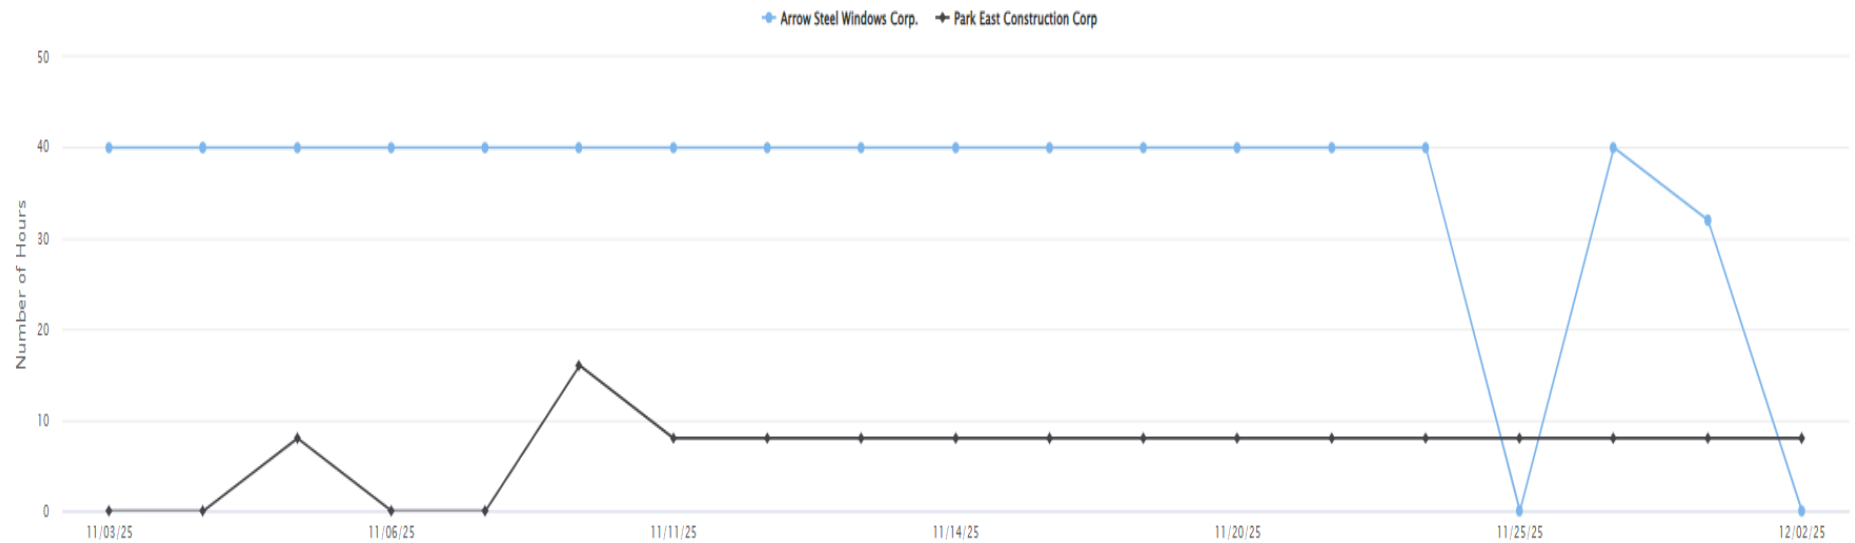


### Hempstead UFSD – Window Replacement



## Section V – Workforce Summary – Company/Hours

### November 2025

MANPOWER GRAPH

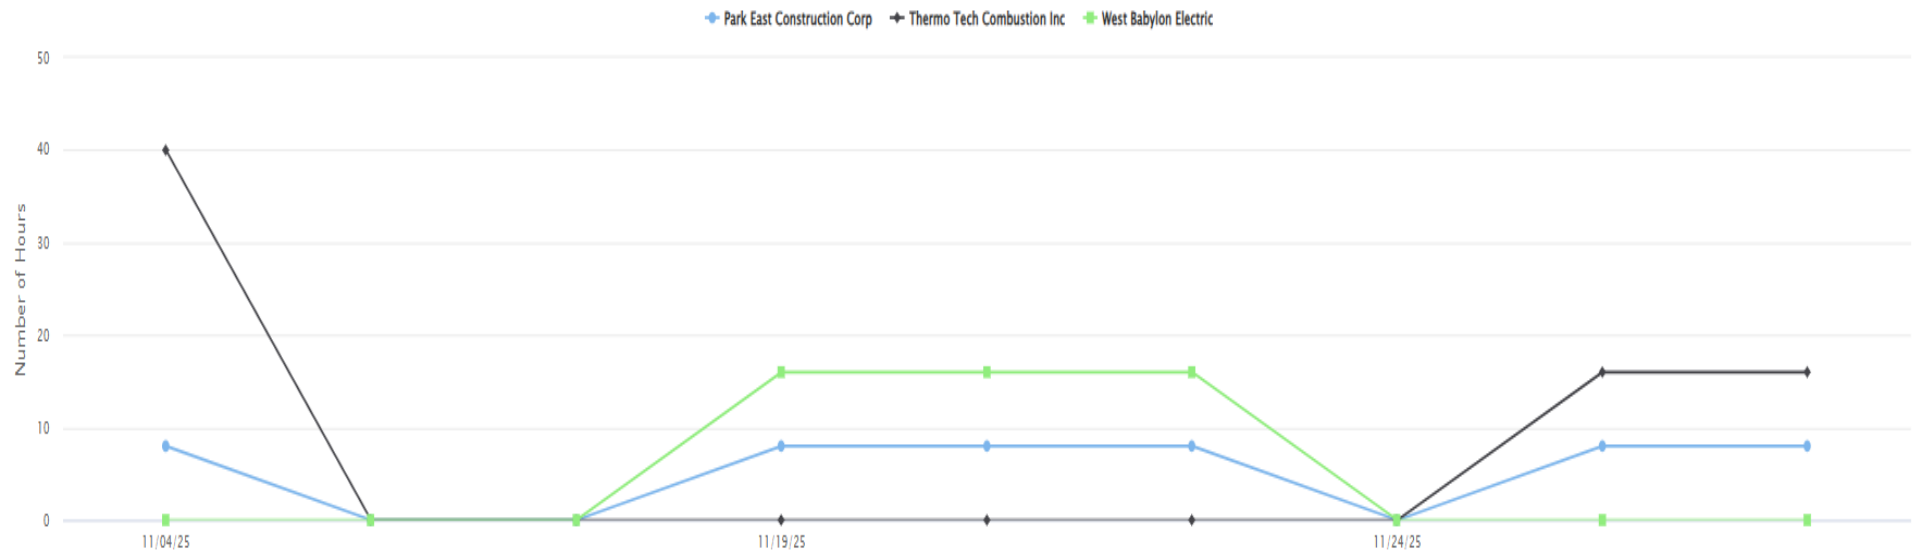


Hempstead McNeil – Boiler Replacement



## Section V – Workforce Summary – Company/Hours

### November 2025

#### MANPOWER GRAPH

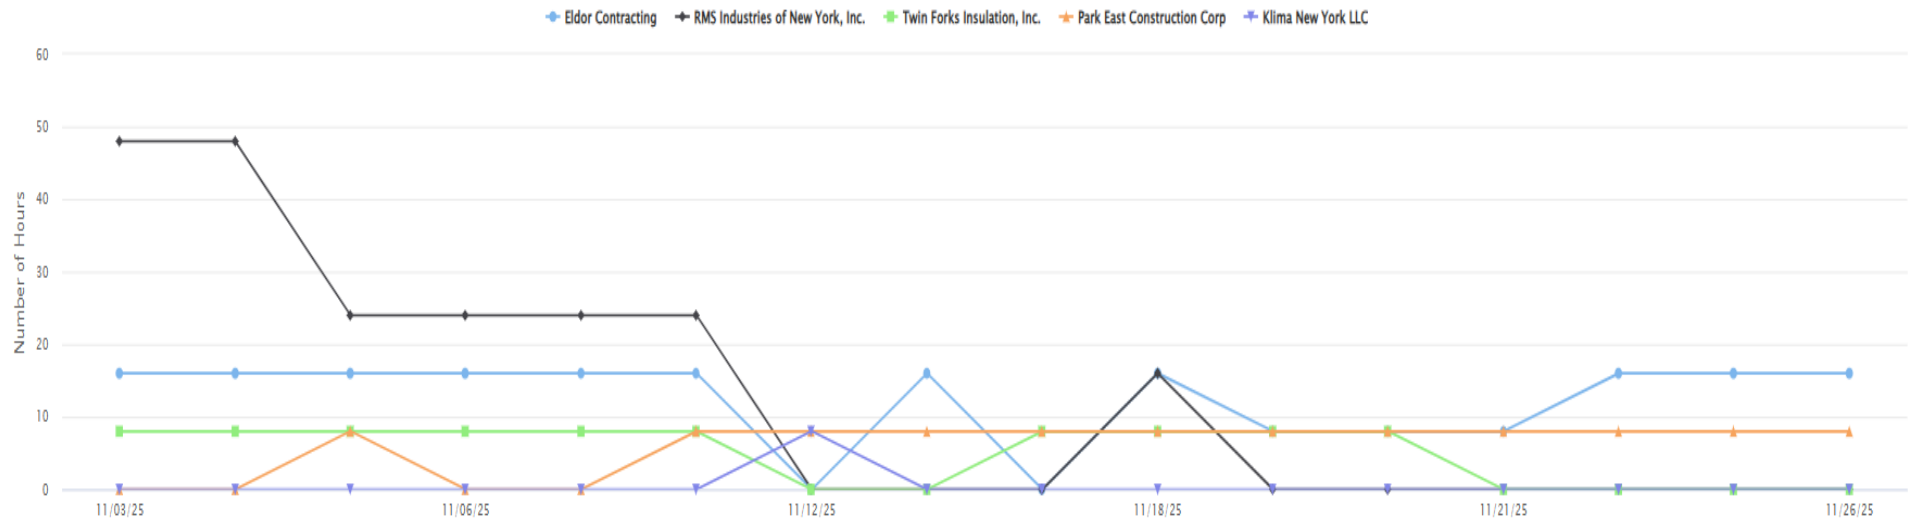

### Hempstead UFSD – IAQ at Various Schools



Hempstead Union Free School District  
November 2025

**End of Progress Report**
