


ALTERATIONS AT THE STEEL CENTER CTE

PROJECT UPDATE #2 as of October 25, 2023:

1. **Matt Fusco** continues providing daily coordination and construction observations.
2. Progress meetings are held every two (2) weeks on Tuesdays at 1:30 PM in Conference Room 'A'. **The next scheduled meeting is Tuesday, October 31, 2023.**
3. General Contractor **DiMarco's** Work Summary
 - a) Removed the ceiling grid and tile on the 1st floor corridors.
 - b) Removed the floor tile on the 2nd floor, working on the grid.
 - c) Removed block walls.
 - d) Removed ceilings.
 - e) Grid and plaster light and skylights' pockets on the 2nd floor.
4. HVAC/Plumbing Contractor **First American Industries'** Work Summary
 - a) Submittals.
 - b) Coordination drawings.
 - c) Purchasing and releasing equipment.
 - d) Powerhouse hot water rough in.
 - e) Grid demolition.
 - f) Gas work through the tunnel into the powerhouse.
 - g) Coordination of chiller/chilled water shutdown.
 - h) Tunnel hot water rough in.
 - i) Demolition in area "A."
 - j) Begin layout and rough ins.
5. Electrical Contractor **Merit's** Work Summary
 - a) Procurement, planning, and submittals.
 - b) Completed removing the lights and devices from corridor ceilings.
 - c) Began installing racks and feeder conduit in the new main electrical room.
 - d) Continue installing feeder conduit.
 - e) Begin coordination drawings.
6. OCIP – **Willis Towers Watson**
 - a) Continues to provide safety assessments of the work, workers, and equipment.

#4566 Steel Center CTE - Alterations
Project Update #2: First American Industries HVAC Heating

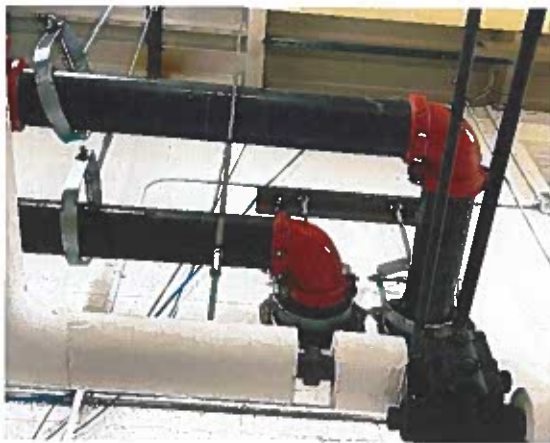

#4566 Steel Center CTE- Alterations
Project Update #2: First American Industries Plumbing Installation and Demolition



#4566 Steel Center CTE- Alterations
Project Update #2: First American Industries Plumbing Installation and Demolition



#4566 Steel Center CTE - Alterations
Project Update #2: Merit Electrical Group Electrical Conduit Installation

