

New Elementary School on Greendale Road



➤ **Completed Work:**

- Installation of the Insulated Concrete Forms (ICF) is near completion at the first floor. The installation of the ICF at the east face of the building to Mechanical Room 120. Placement of the ICF forms at the gymnasium has begun.
- Laying of interior CMU masonry and setting door frames is in progress in the east side of Area A. The MEP was observed following the Mason.
- Placement of the brick seat has started around the building. The foundation drain was observed and backfilling had begun.
- The placing of the geothermal tendons appears to be complete. The well field has been back filled. The tendons are installed to the building but not back filled.
- The retention pond appears to be operating properly. Water was not observed in the lower pond.

➤ **Upcoming Work / Look Ahead:**

- Complete the installation of the geothermal system.
- Continue setting and filling the ICF forms.
- Begin placement of the footing for the gymnasium.
- Continue placing concrete floor slabs.
- Continue laying of masonry in the kitchen area.
- Continue placement of the hollow core planks.

New Elementary School on Greendale Road



Backfill at the Geothermal Well Field



Week Ending January 16, 2026

New Elementary School on Greendale Road



Laying of Interior CMU Area A



Week Ending January 16, 2026

New Elementary School on Greendale Road



ICF forms at the east side of the building at Mechanical 120




Week Ending January 16, 2026

New Elementary School on Greendale Road



Brick Ledge along the North Face of the Building

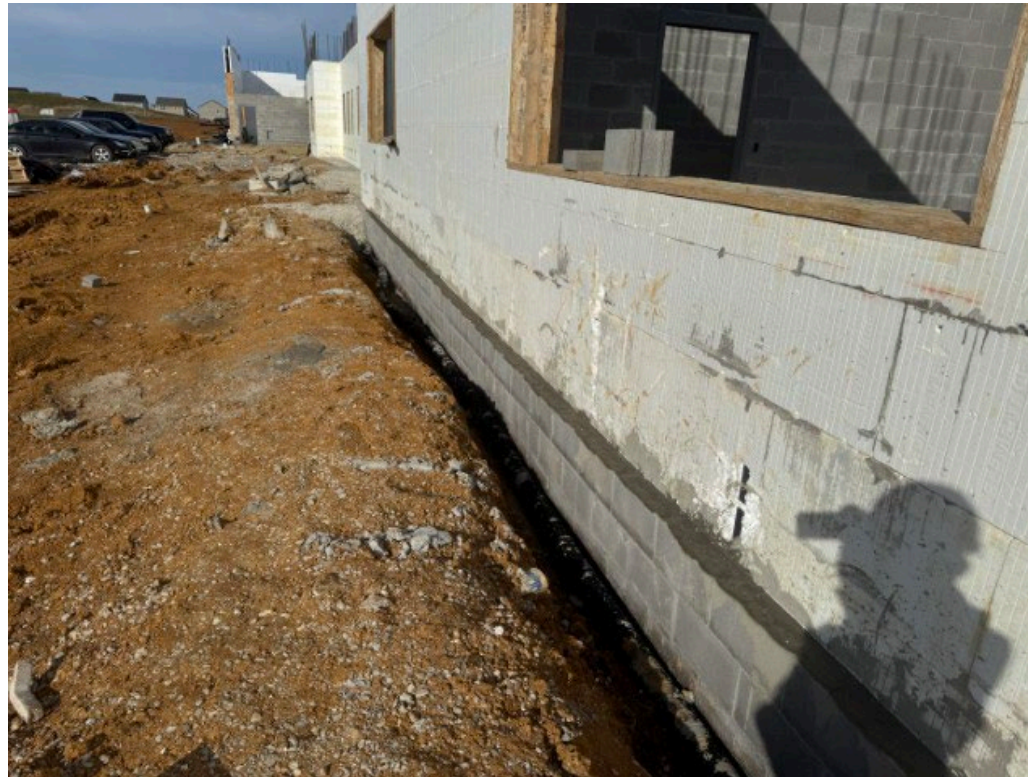

Week Ending January 16, 2026

New Elementary School on Greendale Road



Upper Retention Pond



Week Ending January 16, 2026

New Elementary School on Greendale Road



Lower Retaining Pond



Week Ending January 16, 2026
