

New Elementary School on Greendale Road



➤ **Completed Work:**

- The geothermal contractor has de-mobilized. The site appears to have been left in a clean and professional condition.
- Laying of interior CMU masonry and setting door frames continues in the kitchen area. Due to the cold weather, the masonry work was suspended.
- Lobby 100A was reviewed for the anticipated placement of the concrete floor slab. The Architect requested the Construction Manager to review the vapor details with the installer to ensure full coverage.
- Placement of the second concrete planks was in progress.
- The retention pond appears to be operating properly. Water was not observed in the lower pond.

➤ **Upcoming Work / Look Ahead:**

- Temporary power to be connected to the building.
- Continue setting and filling the ICF forms.
- Continue placing concrete floor slabs.
- Continue laying of masonry in the kitchen area.
- Continue placement of the hollow core planks.

New Elementary School on Greendale Road



Remaining Site After Geothermal Contractor Demobization



Week Ending January 23, 2026

New Elementary School on Greendale Road



Laying of Interior CMU Area A



Week Ending January 23, 2026

New Elementary School on Greendale Road



ICF forms at the east side of the building at West Face of Gymnasium 131



Week Ending January 23, 2026

New Elementary School on Greendale Road



Setting of the Hollow Core Planks at Lobby 100A



Week Ending January 23, 2026

New Elementary School on Greendale Road



Preparation for Placement of Concrete Floor Slab Lobby 100A



Week Ending January 23, 2026

New Elementary School on Greendale Road



Upper Retention Pond




Week Ending January 23, 2026

New Elementary School on Greendale Road



Lower Retention Pond

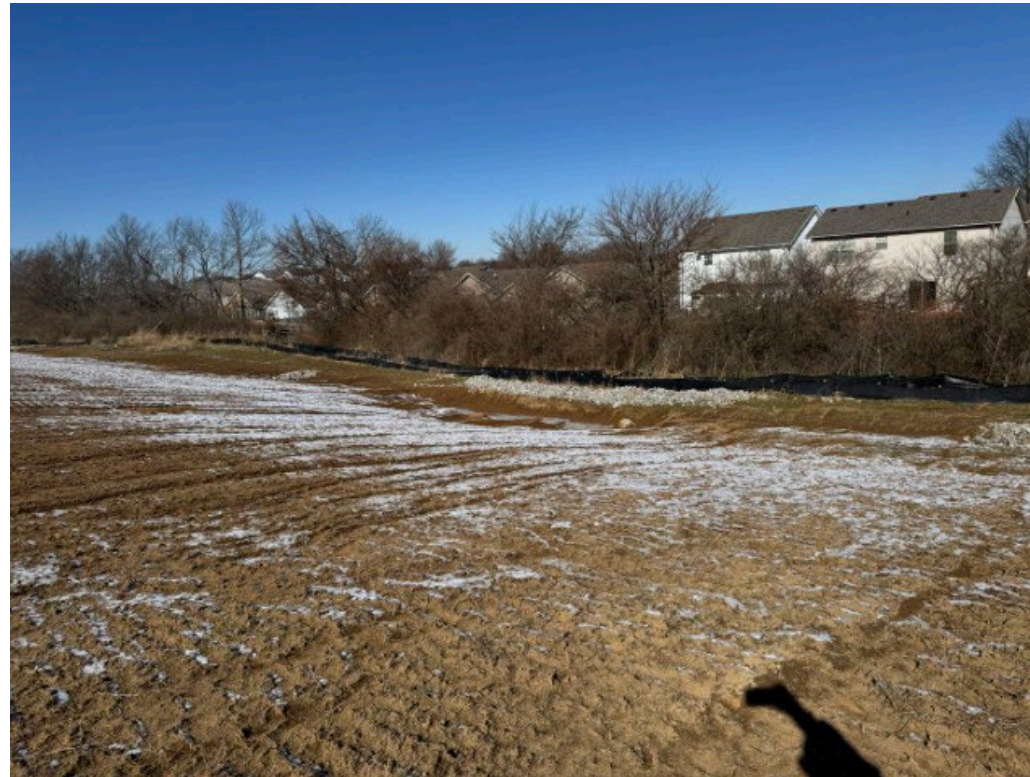

Week Ending January 23, 2026

New Elementary School on Greendale Road



Northwest Corner of the Building



Week Ending January 23, 2026
