


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP concrete formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in areas A, B and C.
- Placing of Area D hollowcore is complete.
- Area A Level 1 ductwork and cable tray installation is in progress.
- Installation of Stair A is complete.

➤ Upcoming Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with ductwork and cable tray installation at Area A Lvl 1.
- Begin retaining wall construction.

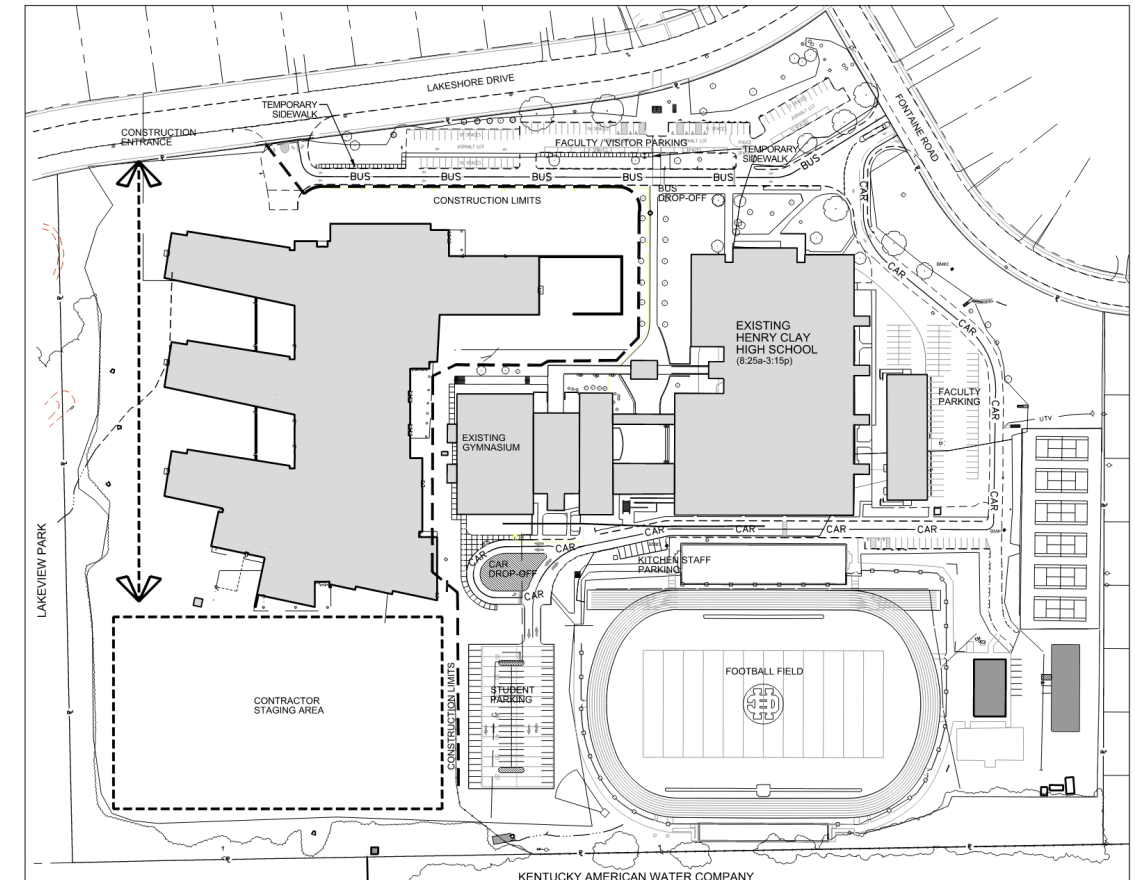

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School



Construction Progress Overview



Week Ending January 23, 2026

New Henry Clay High School

Level 2 (Areas A, B, D): Steel Erection, Floor Slabs, CMU Walls, IFA & Hollow Metal Frame Installation in Progress



New Henry Clay High School

Level 2 (Area A & D): Steel Erection, Floor Slabs, CMU Walls, IFA & Hollow Metal Frame Installation in Progress



New Henry Clay High School



Area A – Level 3 ICF in Progress



New Henry Clay High School


Area B and E at North-South Corridor: ICF, CMU and Hollow Metal Frame Installation in Progress



Week Ending January 23, 2026

New Henry Clay High School

Area C – Steel Deck Installation for Level 2, Laying CMU Walls and HM Frame Installation

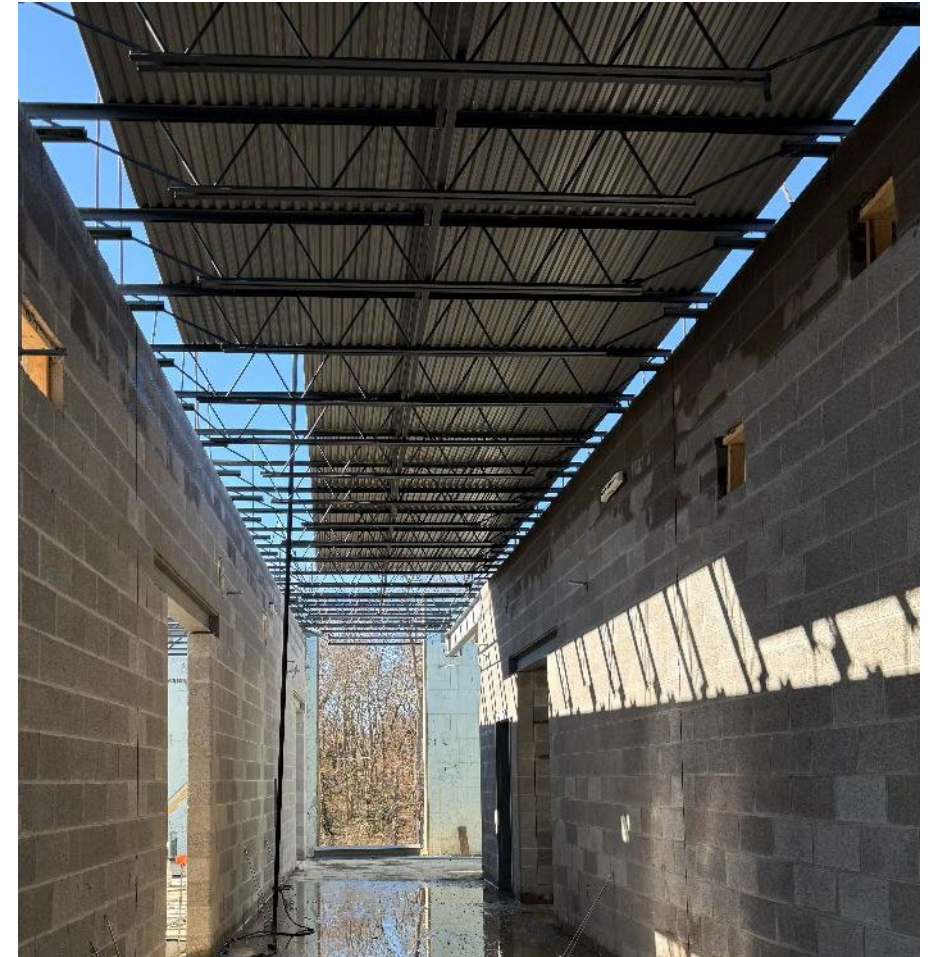

Week Ending January 23, 2026

New Henry Clay High School

Area G: First Course of CMU, CMU Veneer Wall, and Pouring Level 1 Floor Slab in Progress



Week Ending January 23, 2026
