



Foster School Construction Update

January 2026



EVANSTON/SKOKIE
SCHOOL DISTRICT 65

Every Child, Every Day, Whatever it Takes

Foster School Construction Update



Completed	Current	Next Up
<ul style="list-style-type: none">● Storm traps -- playfield and parking lot● Steel erection & detailing● Precast panels● Underground electric & plumbing● RTU's & cooling units set on roofs● Passed all water main inspections● Roofing● Permanent power from ComEd● Exterior painting● Sprinkler system● Dock lift	<ul style="list-style-type: none">● Roofing canopies● Prime and paint interior walls● Window & storefront frames● Insulation inside building● Ceiling grids and lighting fixtures● Ceramic floor tiles & wall wainscot installation● Ceiling light installation● Toilets & sinks installation● Classroom & office millwork cabinetry● Elevator install	<ul style="list-style-type: none">● Site improvements● Locker delivery & install● Bathroom partitions● Door installations● HVAC system start-up

Foster School Construction Update



West atrium looking south

Awaits metal panel installation at the roof for the last external building facade work to be completed



South facing second floor

Insulated metal panels are installed for the exterior walls of the future Drama and music classrooms.

Foster School Construction Update



4-5 grade science classroom facing SE

Porcelain tile floor, drop ceiling grid with lights, and classroom cabinetry have been installed



4-5 grade science classroom facing NE

Cabinetry includes a classroom sink and a solid core countertop

Foster School Construction Update



Low voltage wiring

Two views of the extensive wiring that is organized and spread throughout the building.



Elevator

Installing the mechanical and structural components inside the elevator shaft

Foster School Construction Update




Bathrooms

Epoxy flooring has been poured and set with fixtures being installed



Tiles

Porcelain tile sections in the bathrooms and hallways set in place and spaced, ready to be grouted and finished.

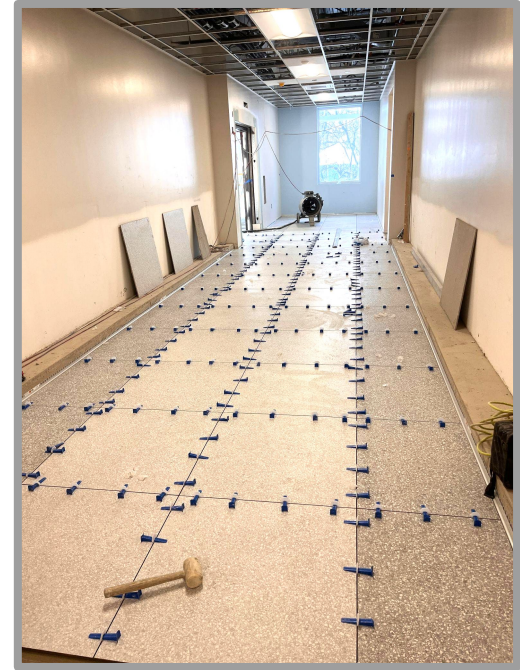

Financial Update



Remaining Construction Work: **\$10,540,807 (28.7%)**

● General Trades	39%	● Kitchen Equipment	100%
● Paint	42%	● Playground	100%
● Plumbing	16%	● Sidewalks/Curbs	100%
● Electrical	31%	● Landscaping	100%
● Flooring	44%	● Fencing	100%
● Fire Prevention Systems	11%	● Site Work	100%
● HVAC/Mechanical	16%	● Mixed Metals	100%
● Roofing	10%	● Moving	100%
● Windows	9%	● Safe Walk Routes	100%
