


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP concrete formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in areas A, B and C.
- Area D hollowcore and joist erection is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Stair A installation is complete and Stair B installation is in progress.

➤ Upcoming Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with above ceiling MEP installation.
- Begin retaining wall construction.

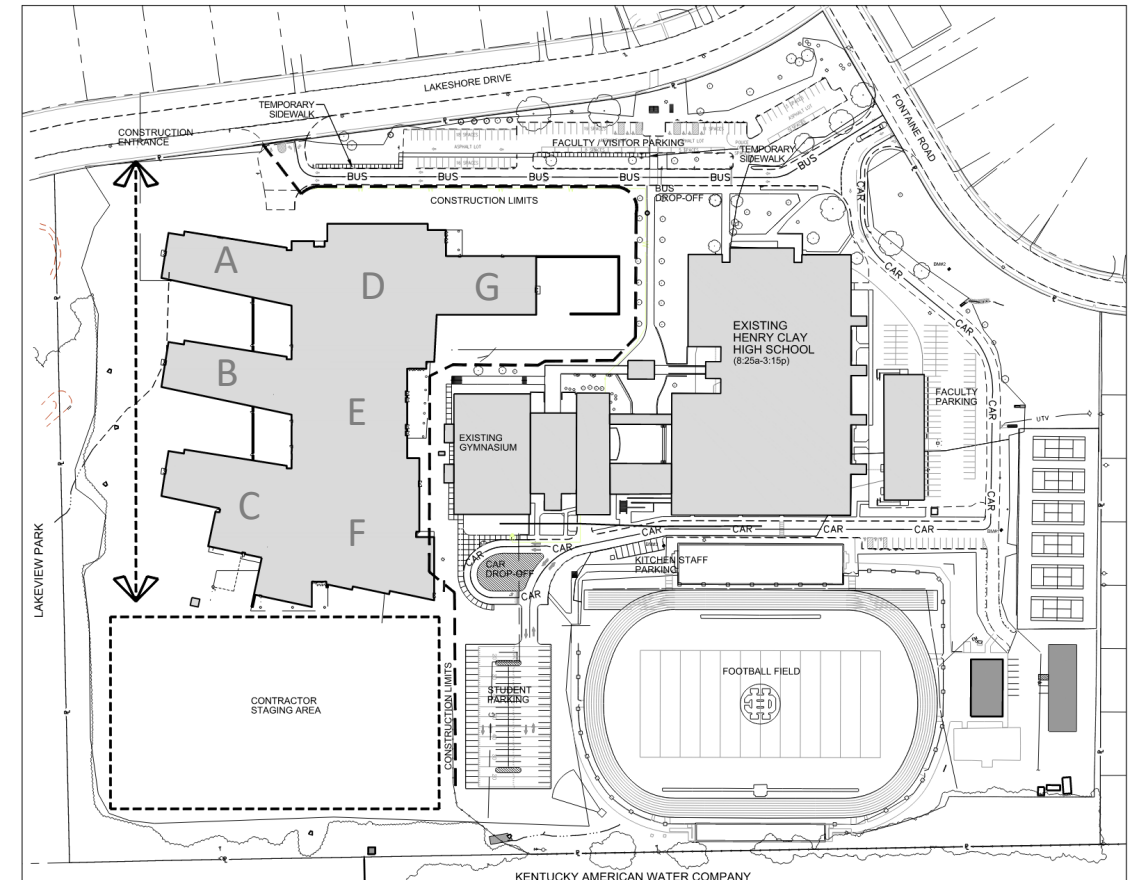

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School

Area D (Storm Shelter): Steel Joist Erection Complete & Installation of Metal Decking in Progress



Week Ending February 6, 2026


New Henry Clay High School

Area D (Storm Shelter): Steel Joist Erection Complete & Installation of Metal Decking in Progress



Week Ending February 6, 2026

New Henry Clay High School




Area B (Classroom Wing) at North-South Corridor: ICF, CMU and Hollow Metal Frame Installation in Progress



Week Ending February 6, 2026

New Henry Clay High School

Area B (Classroom Wing): Stair B Installation in Progress

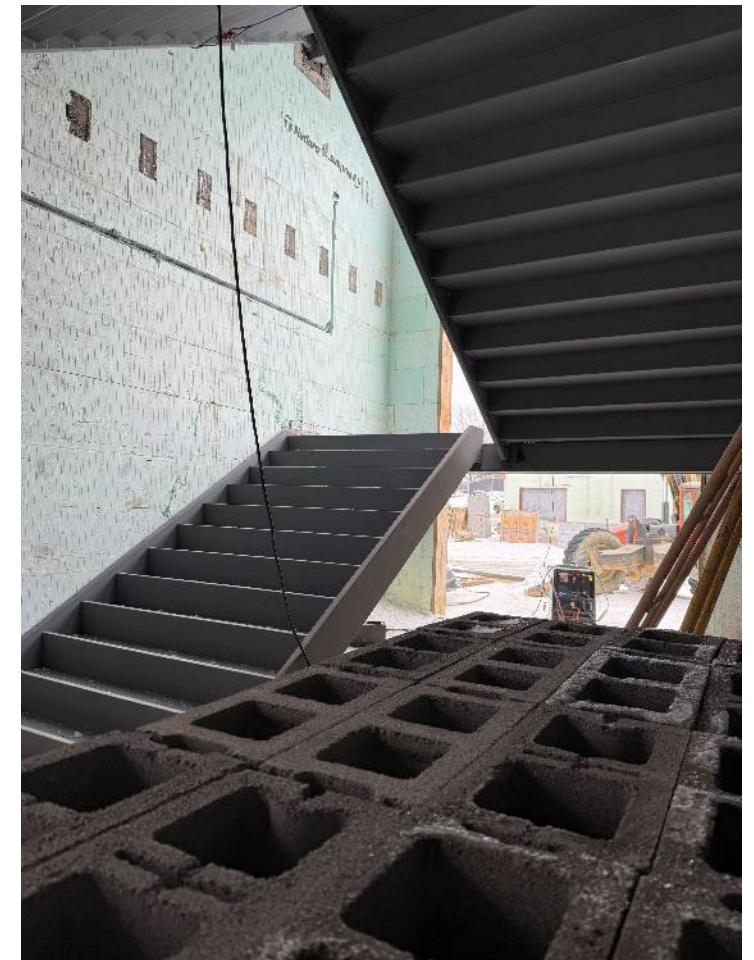

Week Ending February 6, 2026

New Henry Clay High School

Area B (Classroom Wing): Ductwork and Cable Tray Installation in Progress at Level 1



Week Ending February 6, 2026

New Henry Clay High School

Area C (Classroom Wing): Level 2 Steel Erection Complete; Cable Tray & Ductwork Installation in Progress



Week Ending February 6, 2026

New Henry Clay High School

Area A (Classroom Wing): Level 2 Above Ceiling Installation of Mechanical, Electrical, and Plumbing in Progress

