


New Henry Clay High School

➤ Completed/Work in Progress:

- Geothermal well field drilling at the south end of the site is complete.
- KAWC installation of main waterline is complete.
- ICF and CIP concrete formwork placing and pouring, and the installation of IFAs at ICF walls is in progress.
- Laying of CMU walls and the installation of hollow metal frames is underway.
- Under-slab plumbing/electrical and concrete slabs are in progress.
- Steel erection is underway in areas A, B and C.
- Area D hollowcore and joist erection is complete.
- Above ceiling MEP installation is in progress at areas A,B and C.
- Installation of Stairs A and B is complete.
- West driveway retaining wall construction is in progress.

➤ Upcoming Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with above ceiling MEP installation.
- Continue retaining wall construction.

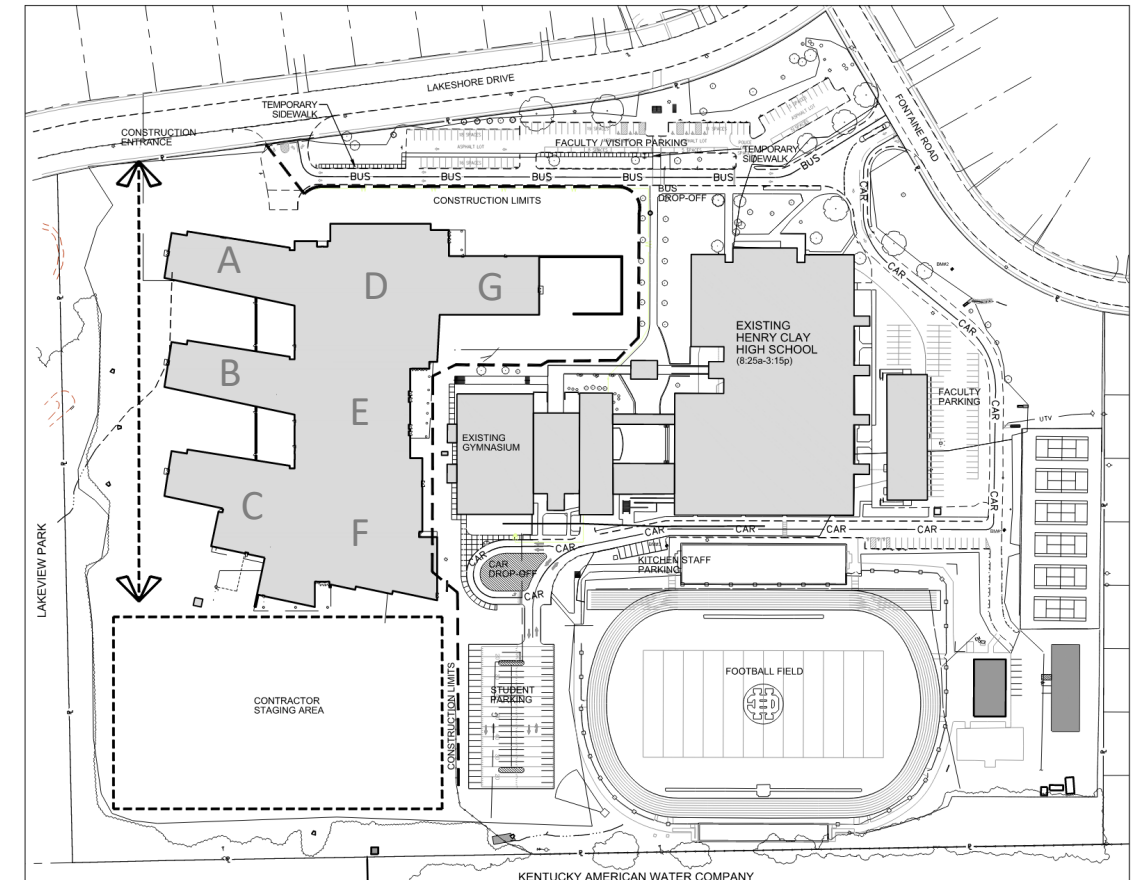

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

New Henry Clay High School


HCHS Living Lab Students Tour the New HCHS Construction Site
[Discussing and Observing Steel Structure in Place to Support Level 2 Above at the North-South Corridor]



Week Ending March 6, 2026

New Henry Clay High School


North-South Corridor: ICF, CMU and Hollow Metal Frame Installation and Steel Erection for Level 2 Underway

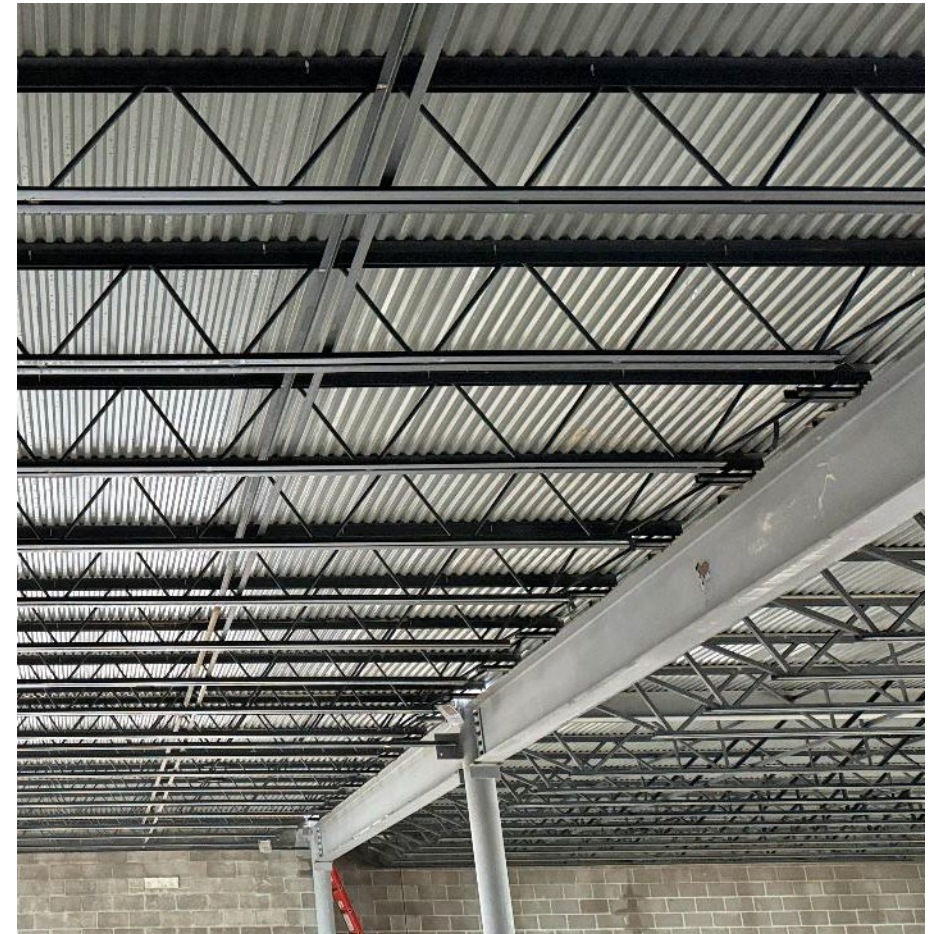

Week Ending March 6, 2026

New Henry Clay High School

HCHS Living Lab Students Tour the New HCHS Construction Site
[Observing Concrete Masonry Block Walls Being Constructed at Area A Level 3]

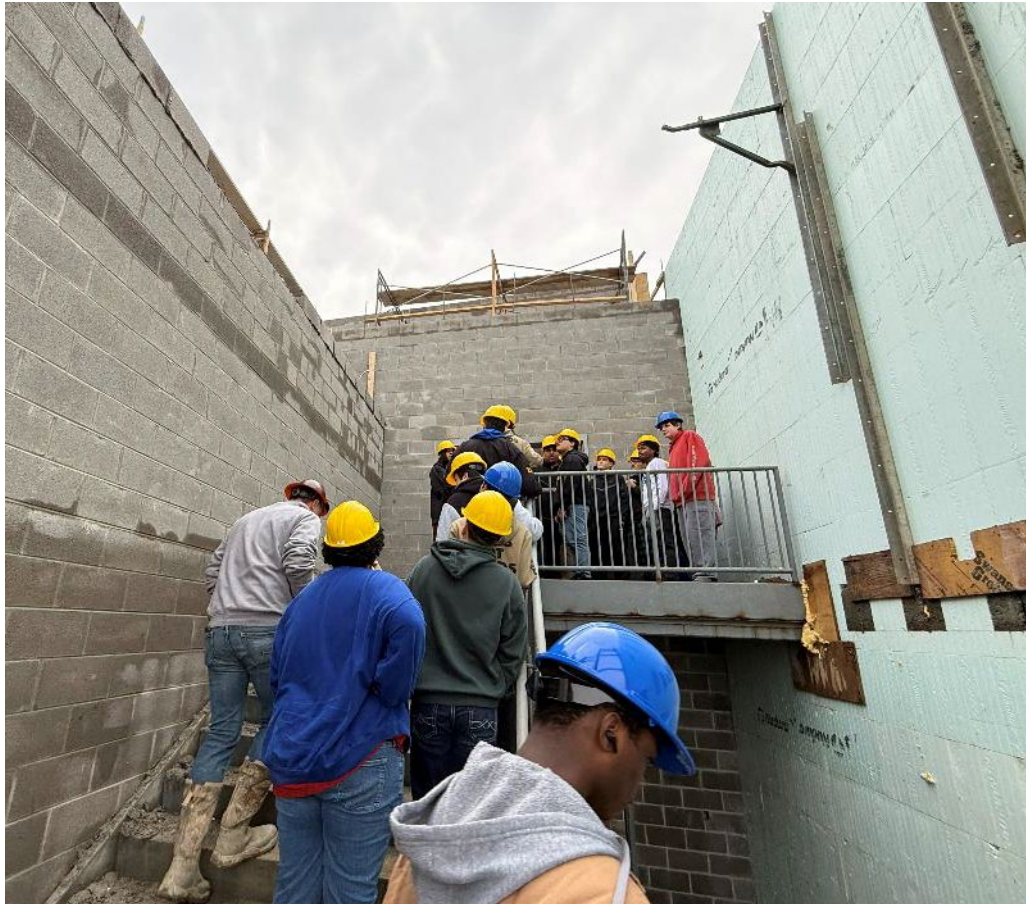

Week Ending March 6, 2026


New Henry Clay High School

HCHS Living Lab Students Tour the New HCHS Construction Site
[Looking at Masonry, ICF, Storm Shelter Roof Formwork, and Steel Erection in Progress]



New Henry Clay High School

Area A (Classroom Wing) Levels 2 & 3: ICF Walls, IFA Frames, Laying CMU Walls, and HM Frames in Progress

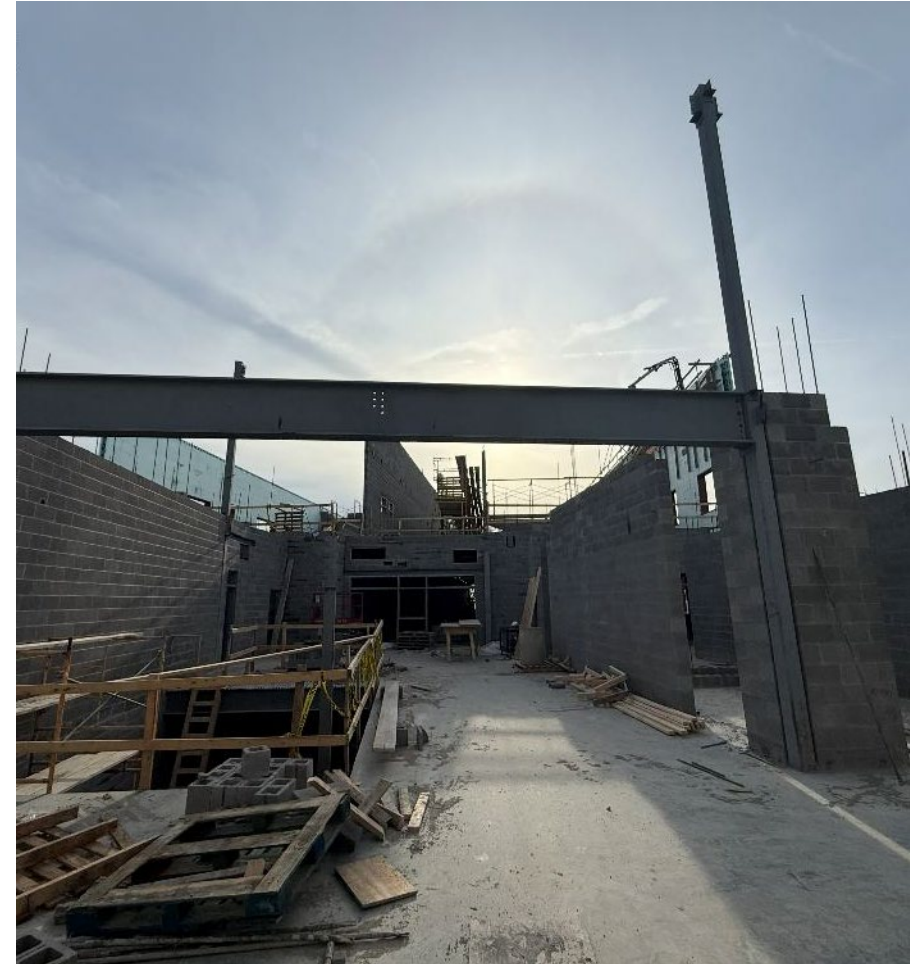

Week Ending March 6, 2026

New Henry Clay High School

Area E (Gymnasium): ICF Walls, IFA Frames and Laying CMU Walls in Progress



Week Ending March 6, 2026
