

Rise STEM Academy For Girls



Week Ending March 06, 2026



Rise STEM Academy For Girls

➤ **Work Completed:**

- Continued above ceiling/light work.
- Continue floor prep for terrazzo.
- Continued tile installation.
- Continued ceiling tile installation.
- Continued elevator work.
- Continued wall painting.
- Continued mechanical rooms work.
- LVT floor installation continued.
- Air diffuser installation continued

➤ **Upcoming Work / Look Ahead:**

- Storm system work will continue.
- Above ceiling work continues.
- Gyp board installation will continue.
- Tile installation will continue.
- Terrazzo installation will continue.
- Mechanical room work will continue.
- LVT floor installation will continue.
- Ceiling tile installation will continue.
- Painting will continue.

Rise STEM Academy For Girls

Terrazzo Work In Progress



Week Ending March 06, 2026



Rise STEM Academy For Girls

LVT Floor Installation In Progress



Week Ending March 06, 2026

Rise STEM Academy For Girls


Ceiling-Mounted diffuser Installation in Progress



Week Ending March 06, 2026

Rise STEM Academy For Girls


Drywall Installation in Progress

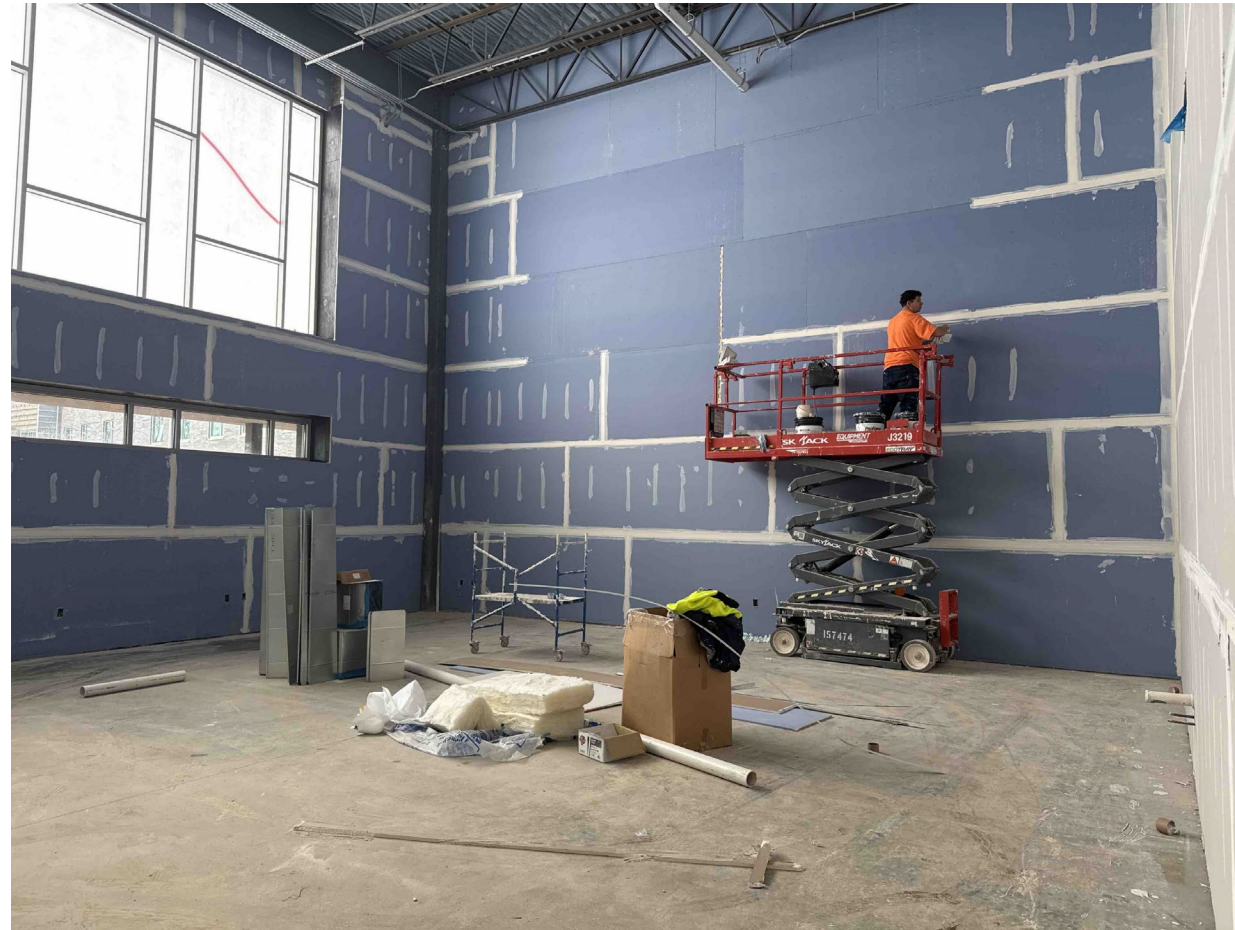

Week Ending March 06, 2026

Rise STEM Academy For Girls

Whiteboard Installation In Progress

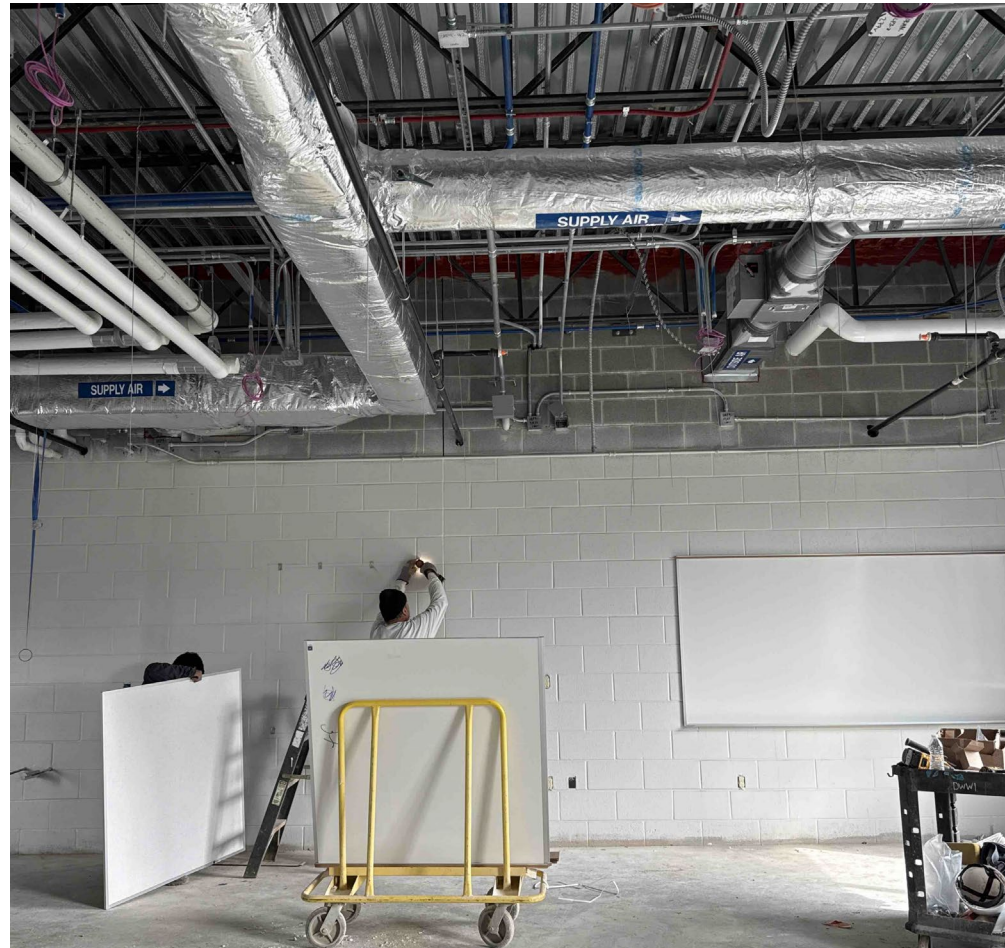

Week Ending March 06, 2026

Rise STEM Academy For Girls

Paint Work in Progress



Week Ending March 06, 2026

Rise STEM Academy For Girls

Gym's Ductwork in Progress



Week Ending March 06, 2026

Rise STEM Academy For Girls

Site Work in Progress



Week Ending March 06, 2026
