

New Elementary School on Greendale Road



➤ **Completed Work:**

- Work has returned since the winter weather.
- Laying of CMU masonry continues at the Cafeteria and the Second Floor.
- MEP installation continues in the classroom, throughout the corridors, and has begun in the Administration Area.
- The retention pond appears to be operating properly.
- Installation of metal stud framing continues at the tops of the EX-type wall.
- Installation of metal stud framing in the Administration Area has begun.
- Setting of the ICF forms has begun at the second floor.
- Grass sown last fall at the Northwest side of the property has returned.

➤ **Upcoming Work / Look Ahead:**

- Continue setting and filling the ICF forms.
- Continue placing concrete floor slabs.
- Continue laying of masonry in the kitchen area and the second floor.
- Continue the installation of MEP.
- Continue Sitework.
- Continue placing hollow core planks.
- Continue metal stud framing.

New Elementary School on Greendale Road



South Side of the Site and Building



Week Ending March 27, 2026

New Elementary School on Greendale Road



Installation of the Geothermal Lines to the Building from the Geothermal Field



Week Ending March 27, 2026

New Elementary School on Greendale Road



Laying of Masonry has Restarted Since the Winter Weather



Week Ending March 27, 2026

New Elementary School on Greendale Road



Plumbing Installation at Girls 123 and Boys 122 Restroom Bank



Week Ending March 27, 2026

New Elementary School on Greendale Road



Installation of Metal Stud Framing has Begun in the Administration Area




Week Ending March 27, 2026

New Elementary School on Greendale Road



Installation of Sprinkler Piping in the Administration Area was ongoing

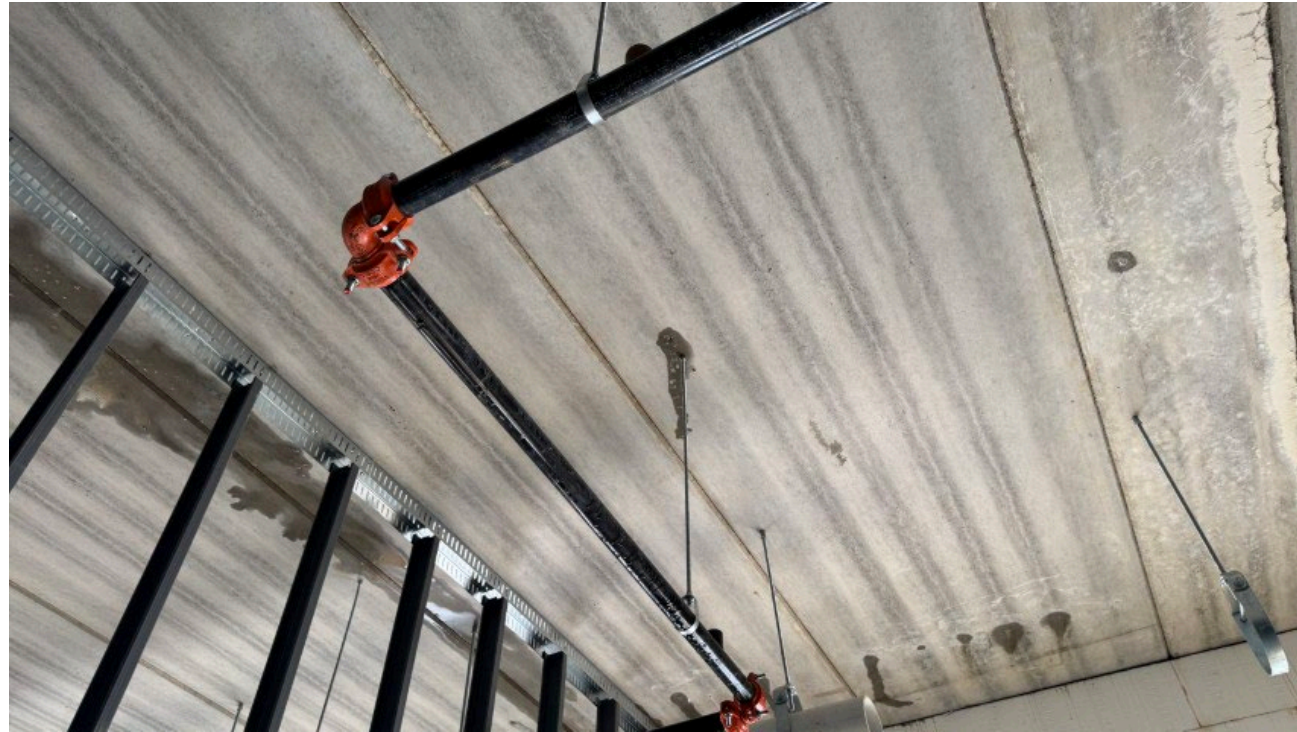

Week Ending March 27, 2026

New Elementary School on Greendale Road



MEP Installation Continues Through Corridor C01




Week Ending March 27, 2026

New Elementary School on Greendale Road



MEP Installation Continues Through Corridor C02

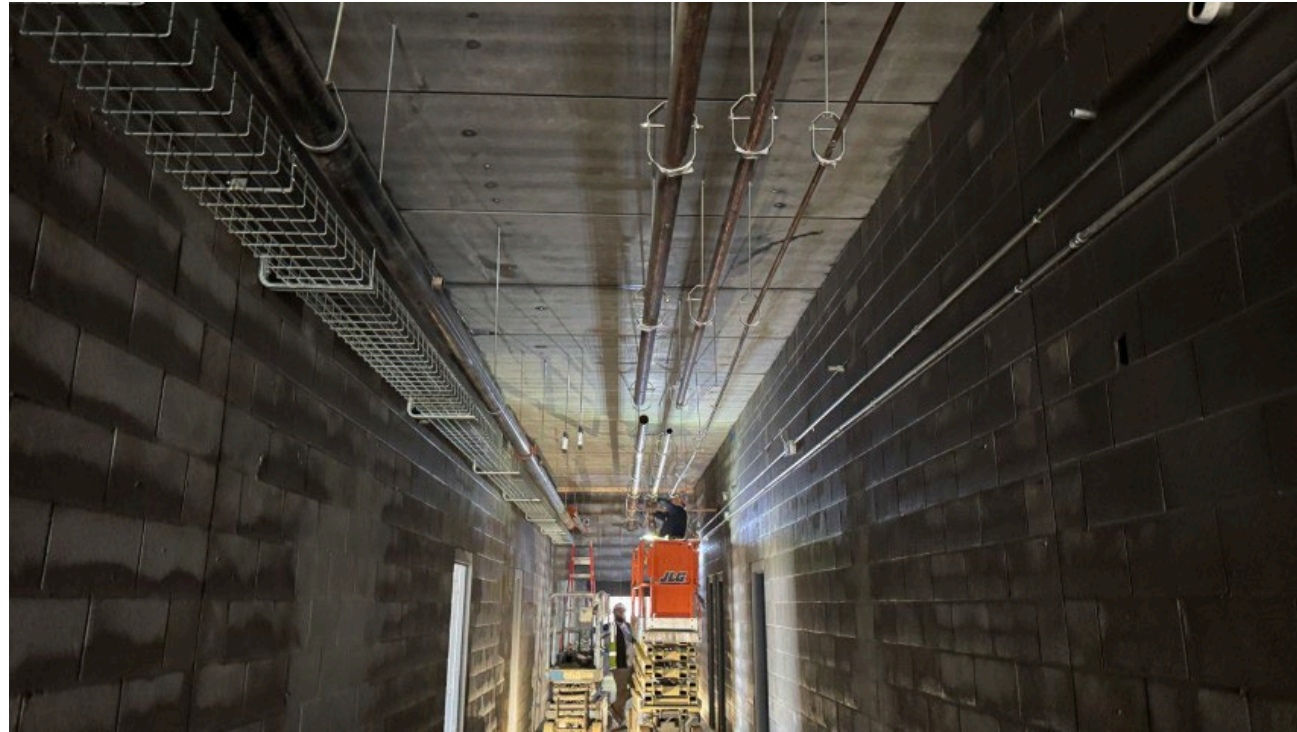

Week Ending March 27, 2026

New Elementary School on Greendale Road



MEP Installation Continues Through Classrooms



Week Ending March 27, 2026

New Elementary School on Greendale Road



Interior of the West Wall of Media Center 144



Week Ending March 27, 2026

New Elementary School on Greendale Road



Laid CMU Wall and Toilet Plumbing Rough-in at Girl's 156




Week Ending March 27, 2026

New Elementary School on Greendale Road



Placed Concrete Planks at Mechanical Mezzanine M200

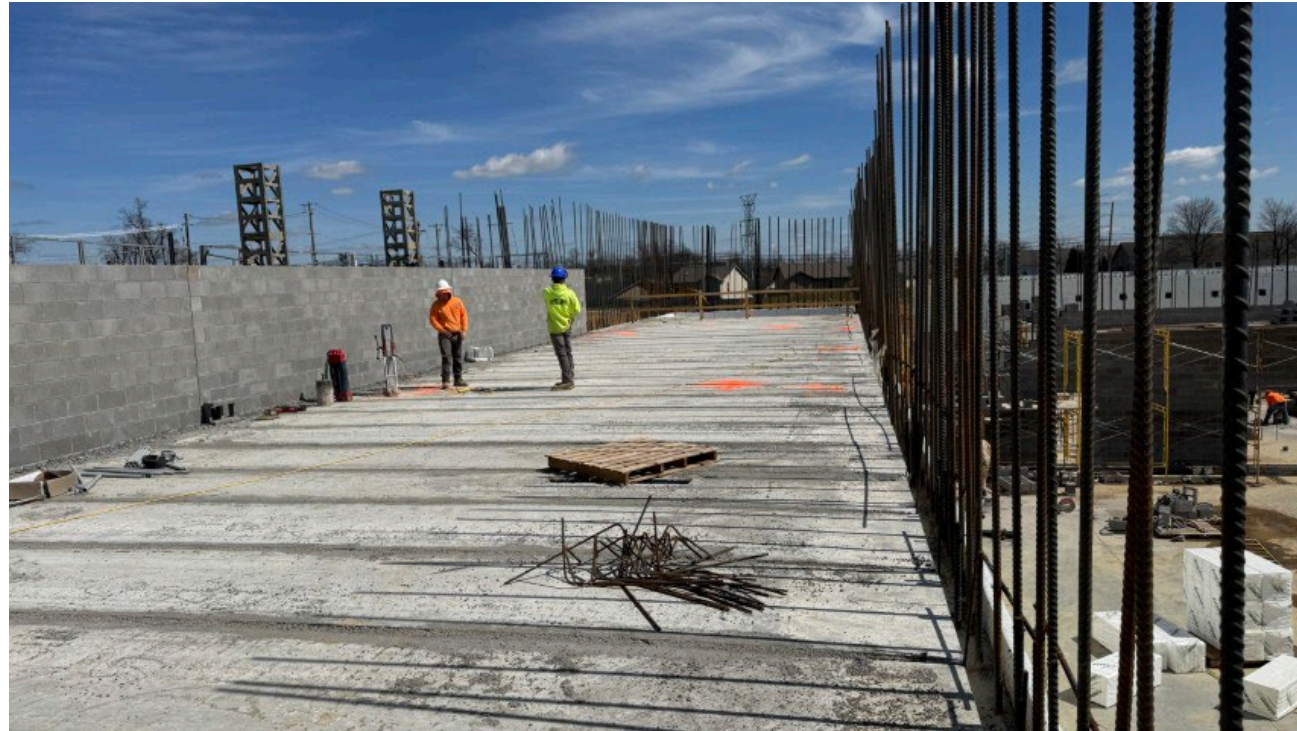

Week Ending March 27, 2026

New Elementary School on Greendale Road



Laying of CMU at the Second Floor Level



Week Ending March 27, 2026

New Elementary School on Greendale Road



Installation of the ICF forms has begun at the Second Floor



Week Ending March 27, 2026

New Elementary School on Greendale Road



Upper Retention Pond



Week Ending March 27, 2026

New Elementary School on Greendale Road



Construction of the First Upper Retention Pond has Started



Week Ending March 27, 2026

New Elementary School on Greendale Road



Lower Retention Pond



Week Ending March 27, 2026

New Elementary School on Greendale Road



Sown Grass is Returning in the Northwest Side of the Property



Week Ending March 27, 2026
